NOT MEASUREMENT SENSITIVE

MIL-HDBK-245E
14 June 2021

SUPERSEDING
MIL-HDBK-245D
3 April 1996

DEPARTMENT OF DEFENSE HANDBOOK

PREPARATION OF STATEMENT OF WORK (SOW)

This handbook is for guidance only.
Do not cite this document as a requirement.

AMSC N/A AREA MISC

DISTRIBUTION STATEMENT A. Approved for public release. Distribution is unlimited.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

FOREWORD

1. This handbook is approved for use by all Departments and Agencies of the Department of Defense.

2. This handbook is for guidance only and cannot be cited as a requirement in any DoD contract. Contractors or suppliers may utilize this document for guidance in preparing responses to Government requests for proposals.

3. This handbook provides guidance to create a SOW applicable to the possible types of acquisitions across the acquisition life cycle. The SOW specifies the tasks, also referred to as work requirements, to be accomplished by the contractor. The execution of those tasks is left to the contractor's discretion.

4. A sample SOW, reflecting format and content expectations, is provided in the Appendix.

5. Tasks or Work requirements, should be specified in the SOW. All data requirements regarding delivery, format, and content should be in the Contract Data Requirements List (CDRL) in conjunction with the appropriate Data Item Description (DID) as described in this handbook. Redundancy invites conflict and must be avoided.

6. Comments, suggestions, or questions on this document should be addressed to the current POC in the ASSIST online database at https://assist.dla.mil since contact information can change.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

TABLE OF CONTENTS

SECTION	PAGE
1. SCOPE	1
1.1 Scope	1
2. APPLICABLE DOCUMENTS	1
2.1 General.	1
2.2 Government documents.	1
2.2.1 Specifications, standards, and handbooks	2
3. DEFINITIONS	2
3.1 Acronyms.	2
3.2 Definitions	3
3.2.1 Standardization Document.	3
3.2.2 Acquisition Streamlining and Standardization Information System (ASSIST).	3
3.2.3 Non-Government Standard.	3
3.2.4 Performance Work Statement (PWS).	4
3.2.5 Statement of Objectives (SOO).	4
4. GENERAL GUIDANCE	4
4.1 General.	4
4.2 Relationship between SOW and appropriation.	4
4.2.a Task language.	4
4.2.b Appropriation categories.	4
4.3 Relationship between the SOW and contract.	5
4.4 SOW and contractor performance.	5
4.5 Relationship of contract sections to the SOW.	5
4.6 Format.	7
4.6.1 SOW Section 1-SCOPE.	7
4.6.2 SOW Section 2-APPLICABLE DOCUMENTS.	7
4.6.3 SOW Section 4-GENERAL REQUIREMENTS.	7
4.6.4 SOW additional sections.	8
4.6.5 SOW DO's and DON'Ts.	8
4.6.6 Title page.	8
4.6.7 Table of Contents.	9
4.6.8 Paragraph numbering and identification.	9
4.7 Data management.	9
4.8 Use of CDRL data.	10
4.9 Data Item Description.	10
4.10 SOW development.	10
4.11 Work Breakdown Structure.	10

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

5. DETAILED GUIDANCE 11
5.1 SOW phasing and results. 11
5.2 Adaptive Framework. 11
5.2.1 Determining user needs and identifying deficiencies. 12
5.2.2 Examples. 12
5.2.3 Services (non-personal). 13
5.2.4 Terminology. 13
5.2.5 Word usage. 13
5.2.6 Language style. 13
5.3 Statement of Objectives (SOO) Method. 14
5.3.1 SOO introduction. 14
5.3.2 SOO purpose. 14
5.3.3 SOO content. 14
5.3.4 SOO development approach. 15
5.3.5 SOO-RFP relationships. 15
6. NOTES 16
6.1 Intended use 16
6.2 Subject term (key word) listing: 16
6.3 Changes from previous issue. 16
6.4 Additional resources. 16
APPENDIX A: WORK WORDS/PRODUCT WORDS 19
APPENDIX B: LIST OF PHRASES HAVING MULTIPLE MEANINGS 22
APPENDIX C: STATEMENT OF WORK EXAMPLE 24
APPENDIX D: GENERIC STATEMENT OF WORK (SOW) TEMPLATE 28
APPENDIX E: VIRTUAL ACQUISITION OFFICE (VAO) SOW TEMPLATE 34
APPENDIX F: STATEMENT OF OBJECTIVES EXAMPLE 45
APPENDIX G: QUALITY ASSURANCE SURVEILLANCE PLAN EXAMPLE 56
APPENDIX H: PERFORMANCE WORK STATEMENT (PWS) EXAMPLE 65
CONCLUDING MATERIAL 71

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

1. SCOPE

1.1 Scope. This handbook applies to the preparation of a SOW for organizations acquiring deliverables and/or services. A SOW describes the essential and technical requirements for items, materials, or services including standards used to determine whether requirements have been met.

This handbook addresses preparation of a SOW. There are other documents that can be used depending on the contracting strategy. To assist the reader's understanding of related documents the handbook will cover the following:

a. A Statement of Objectives (SOO) is a government prepared document incorporated into the Request for Proposal (RFP) that states the overall solicitation objectives.

b. A Performance Work Statement (PWS) describes the work in terms of what is to be the required output rather than how the work is to be accomplished.

The Quality Assurance Surveillance Plan (QASP) is the document government personnel use to assess contractor performance. Using the Requirements Roadmap ensures that each performance objective is linked to a method of inspection incorporated in the QASP. The QASP identifies what is going to be inspected, the inspection process, and who will do the inspecting. The results of those inspections will then be used to document contractor performance. (An example of the QASP can be found in Appendix F)

There are other documents that can be used depending on the contracting strategy, including SOO (examples can be found in Appendix E), and Performance Work Statements (PWS) (a PWS template can be found in Appendix G). This handbook addresses preparation of a SOW.

This handbook implements the acquisition policies reflected in Department of Defense Instruction (DoDI) 5000.02 is aligned with the acquisition milestones and phases discussed in Section 5. The reader is encouraged to visit the DoD Issuances' website for additional instruction on the selected acquisition pathway and specific instructions found here: https://www.esd.whs.mil/Directives/issuances/dodi/. This handbook is for a SOW developed for use in DoD solicitations and contracts and provides a framework that results in a complete description of the work required. This handbook is for guidance only and cannot be cited as a requirement.

2. APPLICABLE DOCUMENTS

2.1 General. The documents listed below are not necessarily all of the documents referenced herein, but are those needed to understand the information provided by this handbook.

2.2 Government documents.

DEFENSE STANDARDIZATION PROGRAM OFFICE

SD-1 - Standardization Directory

SD-21 - Listing of Specifications and Standards Mandated for use by the Department of Defense by Public Laws or Government Regulations.

(Copies of these documents are available online at https://www.dsp.dla.mil)

STANDARDS DEPARTMENT OF DEFENSE

MIL-STD-881 - Work Breakdown Structures for Defense material items.

MIL-STD-961 - Defense and Program-Unique Specifications Format and Content.

(Copies of these documents are available online at https://quicksearch.dla.mil)

GUIDANCE

Defense Acquisition Guide (DAG)

(Copies of this guide are available online at https://www.dau.edu/tools/dag)

DIRECTIVES DEPARTMENT OF DEFENSE

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

DoDI 5000.02 - Operation of the Adaptive Acquisition Framework

DoDM 4120.24 - Defense Standardization Program (DSP) Procedures

DoD 5010.12-M - Procedures for the Acquisition and Management of Technical Data

(Copies of these documents are available online at https://www.esd.whs.mil/DD/DoD-Issuances/)

Chairman of the Joint Chiefs of Staff Instruction (CJCSI) 5123.01H, 31 Aug 2018 - Joint Capabilities Integration and Development System (JCIDS)

(Copies of this document are available online at https://www.jcs.mil/library/)

FORMS DEPARTMENT OF DEFENSE

DD Form 1423- 1 - Contract Data Requirements List (CDRL)
(Copies of this document are available online at https://www.esd.whs.mil/DD/DoD-Issuances/)

2.2.1 Specifications, standards, and handbooks. The following specifications, standards, and handbooks form a part of this document to the extent specified herein.

DEFENSE FEDERAL ACQUISITION REGULATION SUPPLEMENTS

DFARS 237.104 - Personal Services Contract

DFARS should be referred to for additional requirements associated with certain types of procurements, e.g. personal services, commercial items, etc.

(Copies of these documents are available online at https://www.acq.osd.mil/dpap/dars/dfarspgi/current/index.html)

FEDERAL ACQUISITION REGULATION

FAR 52.215-8 - Order of Precedence Uniform Contract Format

(Copies of these documents are available online at https://www.acquisition.gov/browsefar)

3. DEFINITIONS

3.1 Acronyms.

Acronym	Term
AAF	Adaptive Acquisition Framework
ACRN	Accounting Classification Reference Number
ASTM	American Society for Test and Material
CAGE	Commercial Activity / Government Entity
CDRL	Contract Data Requirements List
CJCSI	Chairman of the Joint Chiefs of Staff Instruction
CLIN	Contract Line Item Number
CNSS	Committee on National Security Systems
CNSSI	Committee on National Security Systems Instruction
CM	Configuration Management
CSA	Configuration Status Accounting
DAG	Defense Acquisition Guide
DCMS	Director, COMSEC Material System
DFARS	Defense Federal Acquisition Regulation Supplement
DID	Data Item Description
DISR	DoD Information Technology Standards Registry

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

DMSMS	Diminishing Manufacturing Sources and Material Shortages
DoD	Department of Defense
DoDD	Department of Defense Directive
DoDI	Department of Defense Instruction
EKMS	Electronic Key Management System
ESD	Electrostatic Discharge
ESOH	Environment, Safety, and Occupational Health
FAR	Federal Acquisition Regulation
FIPS	Federal Information Processing Standards
FRACAS	Failure Reporting and Corrective Action System
FRP	Full Rate Production
FTE	Full Time Equivalents
GFE	Government Furnished Equipment
GFP	Government Furnished Property
GFI	Government Furnished Information
HSI	Human System Integration
IUID	Item Unique Identification
JCIDS	Joint Capabilities Integration and Development System
ODC	Other Direct Costs
PCA	Physical Configuration Audit
PMR	Program Management Reviews
POC	Point of Contact
PWS	Performance Work Statement
QASP	Quality Assurance Surveillance Plan
RFP	Request for Proposal
SDS	Safety Data Sheets
SE	Systems Engineering
SLIN	Sub-Line Item Number
SOO	Statements of Objectives
SOW	Statement of Work
SPAWAR	Space and Naval Warfare Systems Command
URL	Uniform Resource Locator
WBS	Work Breakdown Structure

3.2 Definitions. For the purposes of this handbook, the following definitions apply:

3.2.1 Standardization Document. A generic term for a document used to standardize an item of supply, process, procedure, method, data, practice, or engineering approach. Standardization documents include defense specifications, standards, and handbooks; federal specifications and standards; guide specifications; commercial item descriptions; and non-government standards.

3.2.2 Acquisition Streamlining and Standardization Information System (ASSIST). The official database containing information about standardization documents used in the DoD. ASSIST provides electronic access to government standardization documents at https://quicksearch.dla.mil

3.2.3 Non-Government Standard. A national or international standardization document developed by a private sector association, organization, or technical society that plans, develops, establishes, or coordinates standards,

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

specifications, handbooks, or related documents. This term does not include standards of individual companies. NGSs adopted by the DoD are listed in the ASSIST database.

3.2.4 Performance Work Statement (PWS). A performance work statement is a statement of work for performance-based acquisitions that describes the required results in clear, specific and objective terms with measurable outcomes.

3.2.5 Statement of Objectives (SOO). The SOO is a government prepared document incorporated into the RFP that states the overall solicitation objectives.

4. GENERAL GUIDANCE

4.1 General. The SOW should specify in clear, understandable terms the work to be done in developing or producing the goods to be delivered or services to be performed by a contractor. The goods and services must be consistent with the appropriation to be used. Preparation of an effective SOW requires both an understanding of the goods or services that are needed to satisfy a particular requirement and an ability to define what is required in specific, quantitative terms. A SOW prepared in explicit terms will enable offerors to clearly understand the government's needs. The appropriation should sync to the good and services identified in the SOW "Requirements or Scope." The appropriations type (only) should be cited along with the SOW Requirements or Scope paragraph heading or subparagraphs if multi-appropriations are used. Quick look appropriation types are provided in paragraph 4.2.b. This facilitates the preparation of responsive proposals and delivery of the required goods or services. A well-written SOW also aids the Government in conduct of the source selection and contract administration after award.

4.2 Relationship between SOW and appropriation. The SOW defines (either directly or by reference to other documents) all work (non-specification) performance requirements for contractor effort. Appropriations are made for specified purposes and cannot be expended for purposes other than that stipulated. Ensure that the “efforts and services” contained in the SOW are consistent with the appropriation sought to be charged from a Purpose-Time-Amount standpoint. Specifically, the funds being cited on the SOW should be used for the proper purpose, within the legal timeframes established by Congress, and within the amounts authorized, appropriated and allocated to the program. Qualitative and quantitative design and performance requirements are contained in appropriations developed according to MIL-STD-961. Such appropriations are typically referenced in the SOW, but the specific qualitative or quantitative general technical requirements should not be spelled out in the SOW. For example, the referenced appropriation may cite reliability and maintainability requirements in terms of quantifiable mean-time-between failures and mean-time-to-repair; the SOW should task the contractor to establish, implement and control a reliability and maintainability program.

4.2.a Task language. Due diligence should be taken to ensure tasks language does not imply mixed appropriation. Accordingly, mixed or multi-appropriation tasks should be clearly separated and defined to prevent any confusion and delays with program execution and appropriation obligations. When multi-appropriation tasking statements are used, separate line items need to clearly delineate appropriation specific efforts. For example, multi-appropriation tasking statements accompanying funding documents need to clearly delineate appropriation specific efforts much like separate line items on contracts. The funding document should then cite the exact task(s) contained in the associated attachment that supports the funding being issued. Only one appropriation, one subhead under an appropriation, and one fiscal year may be cited on a funding document (i.e., PR). Some language or “verbiage” is more commonly used for one appropriation over another. It is important to note, however, that the context of how the words are being used will determine whether they are appropriate for the appropriation cited. In addition, some “services or deliverables” are associated with specific appropriations.

4.2.b Appropriation categories. Appropriation Categories are categories of government funding that group funds into areas of interest. The main appropriation categories and their availability are listed below:

Research, Development, Test, and Evaluation (RDT&E): appropriations fund the efforts performed by contractors and government activities required for the Research and Development (R&D) of equipment, material, computer application software, and its Test and Evaluation (T&E) to include Initial Operational Test and Evaluation (IOT&E) and Live-Fire Test and Evaluation (LFT&E). RDT&E also funds the operation of dedicated R&D installations activities for the conduct of R&D programs. Available two (2) Years.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Procurement: Appropriations fund those acquisition programs that have been approved for production (to include Low-Rate Initial Production (LRIP) of acquisition objective quantities), and all costs integral and necessary to deliver a useful end item intended for operational use or inventory upon delivery. Available three (3) years. Ships available for (5) years

Operation and Maintenance (O&M): appropriations fund expenses such as civilian salaries, travel, minor construction projects, operating military forces, training and education, depot maintenance, stock funds, and base operations support. Available one (1) year.

Military Personnel (MILPERS): appropriations fund costs of salaries and other compensation for active and retired military personnel and reserve forces based on end strength. Available one (1) year.

Military Construction (MILCON): appropriations fund major projects such as bases, schools, missile storage facilities, maintenance facilities, medical/dental clinics, libraries, and military family housing. Available five (5) years.

4.3 Relationship between the SOW and contract. The SOW should be compatible with the following:

a. Requirements that are mandated by law, established DoD policy or necessary for effective management of its acquisition, operation, or support.

b. At the outset of development, system-level requirements should be specified in terms of mission-performance, operational effectiveness, and operational suitability.

c. During all acquisition phases, solicitations and contracts, the SOW should state management requirements in terms of results needed rather than "how to manage" procedures for achieving those results.

4.4 SOW and contractor performance. After contractor selection and contract award, the contract SOW becomes a standard for measuring contractor performance. Consequently, the SOW author must consider the contractual and legal implications of the SOW during its preparation. As the contracted effort progresses, the government and the contractor will refer to the SOW to determine their respective rights and obligations. In this respect, the SOW “defines the contract and is subject to the interpretations of contract law.” The SOW must clearly define the work to be performed, since the language detailing the contractor's effort may be pertinent to legal questions concerning the scope of work.

4.5 Relationship of contract sections to the SOW. The government RFP or solicitation defines the government's requirements and constitutes the cornerstone of the program, as it ultimately shapes the resultant contract. The SOW preparer should work closely with the overall RFP drafter and all contract section authors to achieve consistency. Data deliverables are identified in CDRL exhibits to the contract. Each Contract Line Item Number (CLIN) in Section B needs to have corresponding work outlined in the SOW. Section F (Deliveries or Performance) requires delivery of data in accordance with these exhibits. The SOW should not conflict with the language in Section H. Clauses that may apply to a resulting contract are cited in Section I (Contract Clauses). Section J is a listing of all exhibits and attachments to the contract. The SOW could be included in Section C or as an attachment within Section J of the contract. Sections K, L, and M apply only to competitive solicitations. They are contained at the end so that when the contract is awarded, they can be removed. Section K includes representations, certifications, or the submission of other information by offerors. Section L includes instructions, conditions, and notices to offerors or respondents to guide in preparing their offers or bids in a manner that is responsive to the government’s RFP. Section M identifies the evaluation factors that will be utilized in awarding the contract. It contains the evaluation criteria listed in order of importance and other factors for award. The SOW and Work Breakdown Structure (WBS) (as discussed in paragraph 4.11) are utilized in preparing the corresponding CDRL, Section L, Section M, and other parts of the RFP/contract (see Figure 1).

Readers are encouraged to download and review the Contract Strategy Fact Sheets. The fact sheets can be used as a government contacting quick reference. The Contract Strategy Fact Sheets are located at: https://www.dau.edu/guidebooks/Shared%20Documents/Contract%20Strategy%20Fact%20Sheets.pdf

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

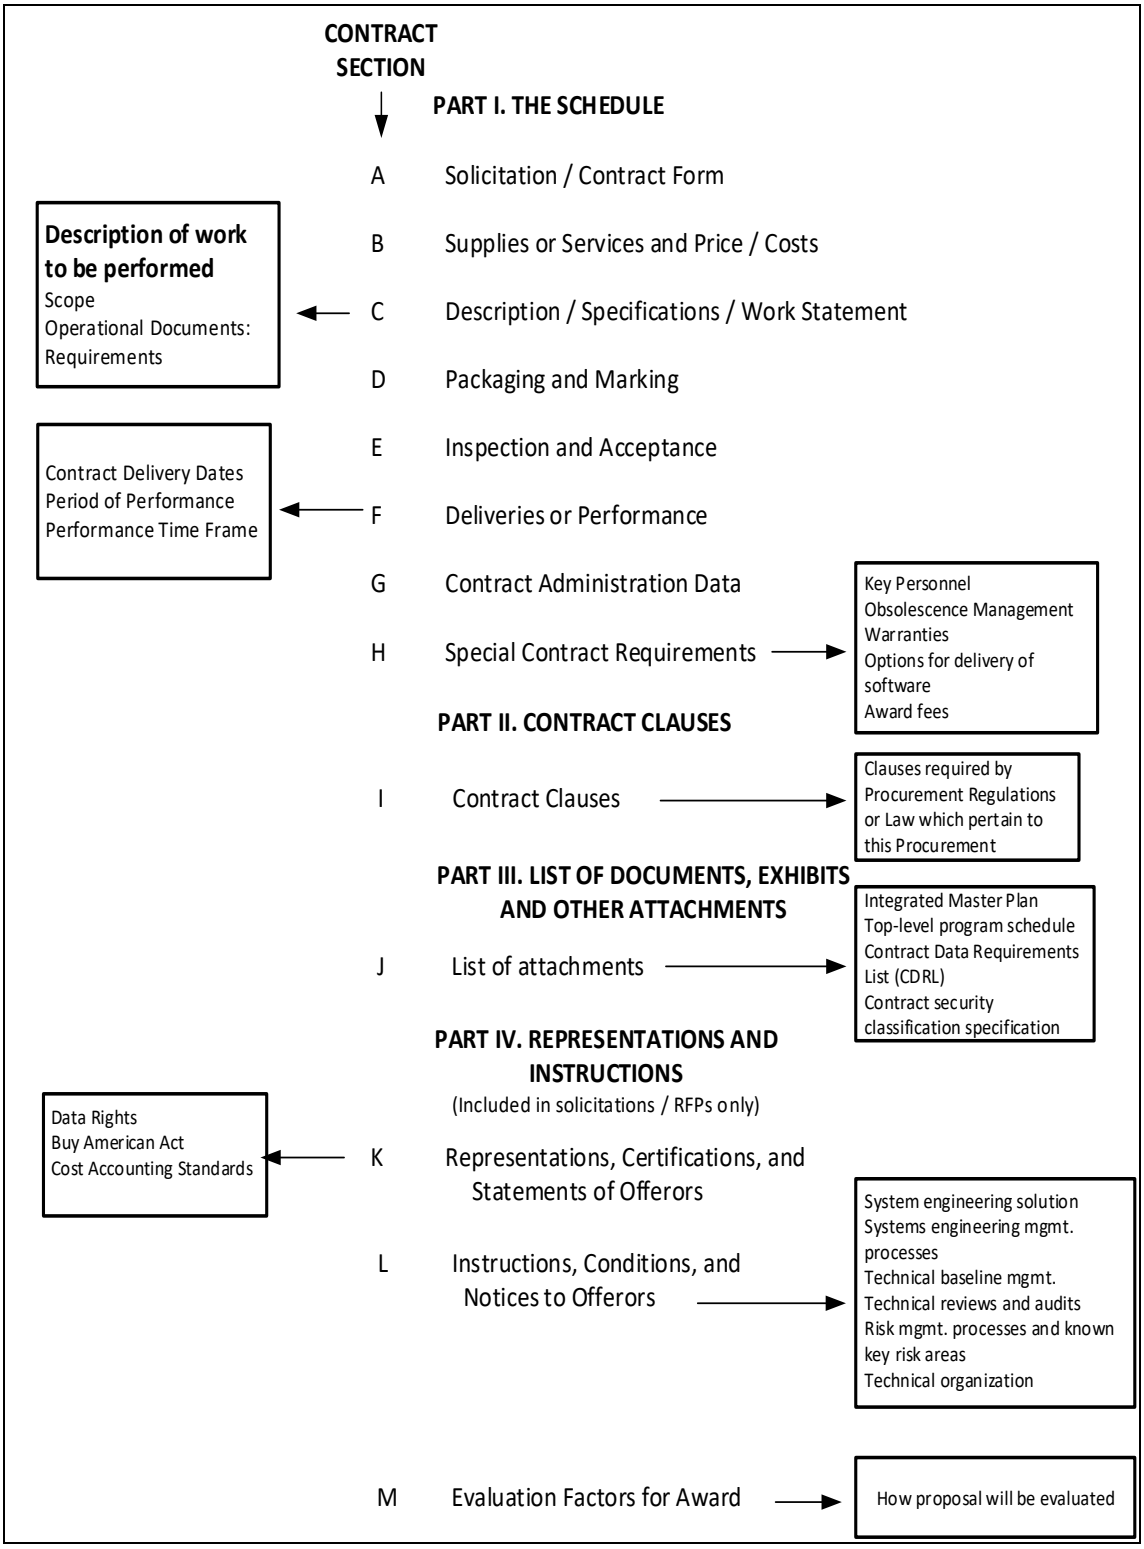


FIGURE 1. Relationship of government solicitation/contract sections to SOW/SOO

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Table 1 is intended to reduce internal RFP inconsistencies and aid in proposal preparation. It is provided as a reference tool for information only. In the event of conflict between this matrix and any other section of the RFP, the other section may take precedence. Because of the complex interrelationships among RFP/contract documents, use of a cross-reference matrix may be helpful (see Table 1).

TABLE 1. Cross reference matrix

Work Description	WBS Element	SOW Paragraph	CLIN	CDRL	Instructions To Offerors (SEC L)	Evaluation Factors (SEC M)	Requirement Located
Design B	2.2	3.2.2	0001	N/A	3.B.1	Tech 1.A	V1-p.64
Build A	2.3	3.2.3	0002	A001	3.B.2	Tech 1.B	V1-p.75

4.6 Format. The format for the SOW is as follows (subject to variations specified in Section 5 for specific types of SOW's):

SOW Section	Title
1	SCOPE
2	APPLICABLE DOCUMENTS
3	DEFINITIONS
4	REQUIREMENTS

Deviations from the standard format may be made by the author when necessary to accommodate program needs.

4.6.1 SOW Section 1-SCOPE. The scope paragraph defines the breadth and limitations of the work to be done. Separate indentures, such as introduction and/or background, under this Section are used in SOWs to provide additional information on complex acquisitions. Background information should be limited to only that information needed to acquaint the proposer with the acquisition requirement.

4.6.2 SOW Section 2-APPLICABLE DOCUMENTS. Military handbooks, government instructions, service regulations, technical orders, and policy letters, as a type, are not written in language suitable for contract application. In the event requirements of these documents must be included in a SOW, excerpts only should be used and should be made into either a clear task statement or a clear reference statement, and not for contract compliance. Any documents called out in Section 2 of the SOW should have the specific version referenced, i.e., by date or by revision letter. Reference only the absolute minimum applicable specifications and standards needed. As an alternative, specific paragraphs or sections of the applicable document may be identified in this section. Selectively invoke documents only to the extent required to satisfy the existing requirements. (The tailoring of reference document requirements should result in a reduction to the overall cost otherwise incurred if all requirements stated in a document are invoked).

The requirement for any specification and standard should be justified before being placed in Section 2 of the SOW. Therefore, Section 2 should not be prepared until the completion of Section 4, General Requirements, is complete.

4.6.3 SOW Section 4-GENERAL REQUIREMENTS. Specific tasks or work requirements are identified in SOW Section 4. These tasks, developed to satisfy program needs, are the contractor work requirements. Although the source selection evaluation board is responsible for the examination of SOW requirements in order to eliminate nonessential requirements, such examinations may be accomplished by the functional technical groups during development of the SOW. Well written SOW requirements have the following attributes:

a. Specifies requirements clearly to permit the government and offerors to estimate the probable cost and the offeror to determine the levels of expertise, manpower, and other resources needed to accomplish technical

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

objectives and goals. The government specifies the funding types align with the requirements needed to be accomplished. Funds identified will match Table 1.

b. States the specific requirements in such a way that the contractor knows what is required and can complete all tasks to the satisfaction of the contract administration office.

c. Written so specifically that there is no question of whether the contractor is obligated to perform specific tasks.

d. Selectively invokes documents only to the extent required to satisfy the existing requirements. (The tailoring of reference document requirements should result in a reduction to the overall costs otherwise incurred if all requirements stated in a document are invoked.)

e. Separates general information from direction so that background information and suggested procedures are clearly distinguishable from contractor responsibilities.

f. Avoids directing how tasks are to be performed and states only what results are required.

4.6.4 SOW additional sections. If more detail is needed, then additional sections may be added to satisfy program needs.

4.6.5 SOW DO's and DON'Ts.

a. DO:

Select a competent team with an experienced team leader.

Exclude "how to" requirements since the offeror should be tasked to provide the deliverables under the contract in the most cost-effective manner.

Use the program WBS, as discussed in Section 4.11 in this handbook to outline the required work effort.

Explicitly define any tailored limitations of all standards and specifications cited.

Exclude design control or hardware or software performance parameters because these requirements should be covered in a specification.

Give priority to commercial items over specification items when the former satisfies military requirements.

Ensure SOW is clear of any language for tasks which are inherently governmental functions.

Use authoritative websites, publications, technical orders, and any other document when creating a SOW.

An acronym list should be included as an attachment to the SOW.

b. DON'T:

Order, describe, or discuss CDRL data.

Invoke, cite, or discuss a Data Item Description (DID). Although the text of the SOW should not include the data format and content preparation instructions and/or data delivery requirements, a DID number listed on the CDRL may be cross-referenced in the SOW.

Specify technical proposal criteria or evaluation factors.

No funding amounts prescribed.

Specify design control parameters or the performance of hardware.

Impose on the contractor a Government format when a contractor format is acceptable.

Over specify. Specify only what is required and let the contractor establish the best method to fulfill the requirement.

Invoke in-house management instructions.

Use the SOW to establish or amend a specification.

4.6.6 Title page. All SOWs should have a title page or cover that shows the SOW title, preparation date, procurement request number or contract number, distribution statement, For Official Use Only/Controlled Unclassified Information (FOUO/CUI), revision number, date, and identity of the preparing organization (see Figure 2).

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

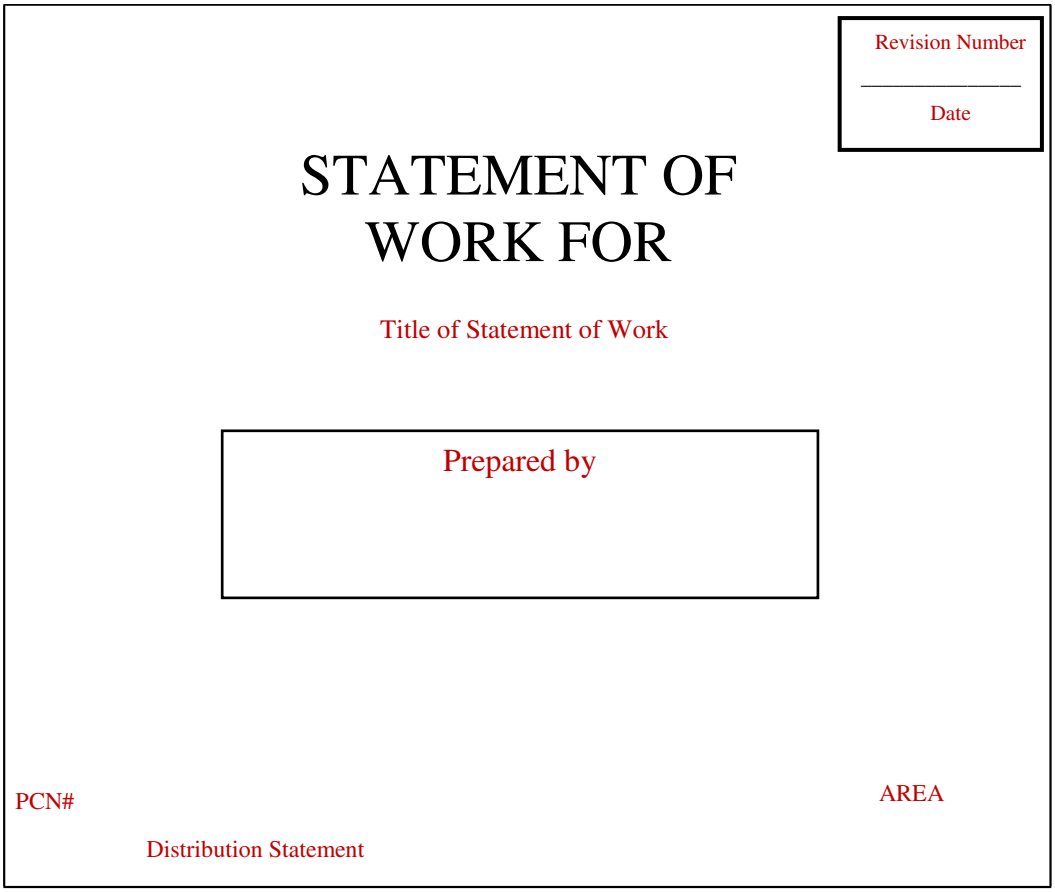


FIGURE 2. Sample SOW Title Page

4.6.7 Table of Contents. The document should contain a table of contents providing the number, title, and page number of each titled paragraph, figure, table, and appendix. For data in a database or other alternative form, this information should consist of an internal or external table of contents containing pointers to, or instructions for accessing, each paragraph, figure, table, and appendix or their equivalents.

4.6.8 Paragraph numbering and identification. Each paragraph and subparagraph should be numbered consecutively within each SOW section using a period to separate the number representing each sublevel. Paragraph numbering should be limited to the third sublevel, if possible, as shown in the following example for SOW Section 4:

General Requirement	4
1st Sublevel	4.1
2nd Sublevel	4.1.1
3rd Sublevel	4.1.1.1

Paragraph breakdowns should be kept to the level necessary to clearly define required contractor tasks. Only one task should be provided in a numbered paragraph or subparagraph to facilitate costing, referencing and tailoring of tasks. Each paragraph and subparagraph should be titled. Each title should clearly identify the funding type along with the paragraph heading or sub-paragraphs if multi-appropriations are used. Clearly defined tasks and the SOW language used to describe the task will ensure efforts do not mix funding types.

4.7 Data management. As the contractor performs and completes the SOW tasks, data is developed. Proper tailoring and scheduling of data submission items requires particular attention by the SOW preparers. The contractor's format may be the acceptable form for submission of data products. The SOW preparer should make

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

every effort to ensure that the CDRLs and DIDs reflect the anticipated need for data and to ascertain whether the specific data required will in fact be generated and available.

4.8 Use of CDRL data. The ordering and delivery of data which the Government requires are specified and scheduled through the use of the CDRL, DD Form 1423-1. The SOW author should exercise considerable care and attention to the data delivery implications of the SOW. While data may be inherently generated by a work task, recording and delivering the data in a specific format are cost drivers that must be considered when preparing the SOW and CDRLs.

4.9 Data Item Description. DIDs are DoD-approved documents that describe the format and content of the data requirements. After the need for recording and delivery of data resulting from a work task has been determined, appropriate DIDs should be selected from ASSIST using the search feature. The CDRL should only require data specifically generated in a SOW work task. The SOW, and not the DID, must task the contractor to perform work. At the end of each SOW task paragraph, the DIDs and/or CDRL that are associated with the effort described in the task may be identified in parentheses.

To understand the relationship of a SOW to the CDRL and DID (see Figure 3), consider the example where the SOW includes a requirement that, "the contractor should establish, implement and control a Configuration Management (CM) program." The associated CDRL would order a CM data item and identify due date, distribution and other such parameters while the DID would provide the format and content requirements for that particular CM item, with non-essential references tailored out of the DID. Data items should only be added if the Government will formally accept submittal from the contractor.

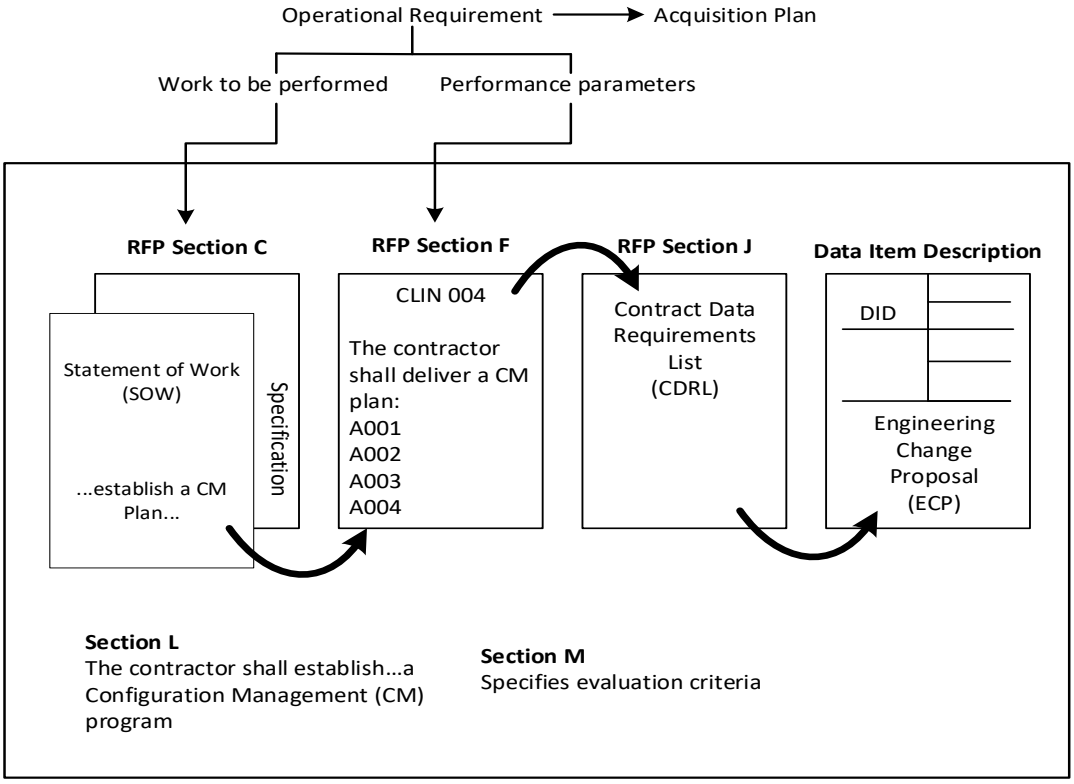


FIGURE 3. SPEC-SOW-CDRL-DID Relationship

4.10 SOW development. Section 4 of this handbook describes how the SOW content changes depending on which acquisition phase it supports.

4.11 Work Breakdown Structure. A WBS should be used in developing a SOW. MIL-STD-881 should be used for guidance. A WBS provides the framework for a disciplined approach of structuring and defining the total project or program. It is a product-oriented family tree composed of equipment, services, and other items which

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

make up the project or program, and provides the basis for progress reporting, performance and engineering evaluations, and financial data reporting. When preparing the SOW, a complete application of a WBS may not be necessary in all programs, however, the underlying philosophy and structured approach can and should be applied. The CLIN and the SOW should be constructed to correlate with the WBS. Use of a WBS during SOW development facilitates a logical arrangement of the SOW elements and provides a convenient checklist to trace all necessary elements of the program and ensure that they are addressed in the SOW. The WBS will evolve into greater detail as the system definition and acquisition phases advance. For each phase, the WBS must be in sufficient detail to cover all the required work in that phase, as well as to produce the technical information needed for the next phase. The WBS may be tailored to the minimum level required to manage program risk.

5. DETAILED GUIDANCE

5.1 SOW phasing and results. All programs, including highly classified programs, should accomplish certain core activities. These activities must be tailored to satisfy an identified need using common sense and sound business practices. The acquisition process follows one of six acquisition pathways and is structured in logical phases separated by major decision points called milestones (See DoDI 5000.02). Each milestone is an opportunity for a review to determine if the program should continue. The decision to enter the next phase or not is based on results obtained in the acquisition phase preceding that milestone. SOW requirements are tailored to support the acquisition of information, hardware, software, technical data and the logistic support required during any particular life cycle phase.

5.2 Adaptive Framework. The following are pathway descriptions for programs to adopt and tailor. Each pathway is governed by separate policies, the program manager should "tailor-in" the processes, reviews, and documents necessary for their program for their decision authority approval. Readers are encouraged to review DoDI 5000.2, section 4.1 and the DAU hosted AAF online resources located at: https://aaf.dau.edu/ for additional information.

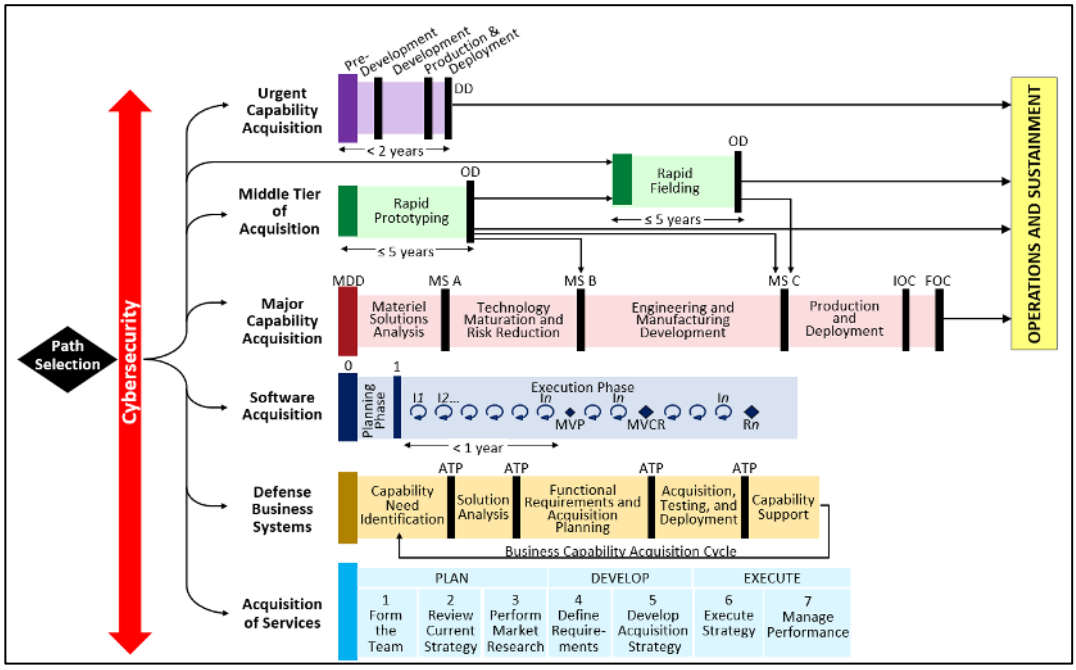


FIGURE 3. Additive Acquisition Framework (AAF)

Pathway descriptions:

a. Urgent Capability Acquisition: The purpose of the Urgent Capability Acquisition (UCA) pathway is to field capabilities to fulfill urgent existing and/or emerging operational needs or quick reactions in less than 2 years

b. Middle Tier of Acquisition (MTA): The Middle Tier of Acquisition pathway is used to rapidly

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

develop fieldable prototypes within an acquisition program to demonstrate new capabilities and/or rapidly field production quantities of systems with proven technologies that require minimal development

c. Major Capability Acquisition: Major Capability Acquisition is used to acquire and modernize military unique programs

d. Software Acquisition: This pathway is to facilitate rapid and iterative delivery of software capability to the user

e. Defense Business Systems (DBS): This pathway is used to acquire information systems that support DoD business operations. This pathway applies to defense business capabilities and their supporting business systems, including those with "as-a-service" solutions to include: financial and financial data feeder; contracting; logistics; planning and budgeting; installations management; human resources management; training and readiness systems; and may also be used to acquire non-developmental, software intensive programs that are not business systems

f. Acquisition of Services: This pathway is for the acquisition of contracted services with a total estimated value at or above the simplified acquisition threshold

Note: *For additional information on the AAF see the DoDI 5000.2.*

5.2.1 Determining user needs and identifying deficiencies. All acquisition programs are based on identified, documented, and validated mission needs. Mission needs result from assessments of current and projected capability requirements. Mission needs may establish a new operational capability, improve an existing capability, or exploit an opportunity to reduce costs or enhance performance. If the potential solution results in a new program, an appropriate level review should be held to document its validity and joint potential, and confirm that the requirements have been met or considered.

a. Any. "Any" is an ambiguous word. Authors may intend it to denote "plurality" and readers may interpret it to denote "oneness." Also, when "any" is used to describe the selection of items from a list, it's the reader who does the selecting, not the author. Which items and how many the reader selects are beyond the control of the author.

b. Assist. "Assist" connotes personal services. It infers working side-by-side, being subject to supervision. The word is totally undefined in terms of identifying the work and its range and depth. Spell out explicitly what the contractor must do.

c. As Required. The result of this approach is an undefined work condition. It has no expressed limitations. It places the Government in a position of not expressing its minimal needs. It could lead to a debatable condition concerning the contractor's compliance with the contract or order. The SOW must be declarative as to its minimal needs.

d. As Applicable / As Necessary. If the Government does not know what is necessary or applicable, it must not leave to the contractor the responsibility for determining the minimal needs of the contract. The SOW should forthrightly state the requirements so that the contractor can comply with the requirement using their best efforts and expertise to accomplish the tasks.

e. As Directed. This condition, as a part of a work task in an SOW, connotes a personal services situation in which the contractor is placed under direct supervision. "When directed" may be used in conjunction with a task order contract to indicate that specific tasks may be initiated at various times during the period of contracted performance.

f. Including but not limited to. This term is generally inserted when the drafter is unsure of requirement or criteria. However, it creates an unspecific requirement which creates ambiguity. Only list known requirements.

g. Etc. This word also introduces potentially more unidentified ambiguous requirements.

5.2.2 Examples. Examples are provided in the Appendix. The example SOW is intentionally broad and incomplete to illustrate the types of information required.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

5.2.3 Services (non-personal). The product of non-personal services is the result of work tasks being performed. The requirements that establish the work must be defined in terms of work words and not product words. If the work to be performed is painting a building, the task must define what is to be painted and to what standards. The product of such a contract is obviously a building painted and completed by a certain time. If the SOW is prepared properly, contractor monitoring can be kept to a minimum as long as the task is completed on time and within cost. The Government has the requirement to inspect the product and either accept or reject it based on the contractor's conformance to the prescribed work requirement. The wide variety of non-personal services requirements cause this type of contract to take on many forms. However, in all applications, two factors are important to ensure that the services purchased are indeed- non-personal. These factors are: (a) the SOW must establish explicitly what work is to be done and require the delivery of a product or result other than periodic progress reports and (b) the contractor's employees must not be supervised or controlled by the Government during the execution of the work and production of the product or result. In this regard, the SOW must be explicit, inclusive and comprehensive in prescribing the work requirements. For a more complete discussion of a personal versus a non-personal services contract, refer to DFARS 237.104.

5.2.4 Terminology. A frequent problem encountered in defining the tasks in a SOW is the use of non-specific words and phrases such as: “any”- “assist”- “as required”- “as applicable/as necessary” and “as directed.” Do not use any of these words. The following rationale for precluding their use is provided:

a. Any. "Any" is an ambiguous word. Authors may intend it to denote "plurality" and readers may interpret it to denote "oneness”. Also, when "any" is used to describe the selection of items from a list, it's the reader who does the selecting, not the author. Which items and how many the reader selects are beyond the control of the author.

b. Assist. “Assist” connotes personal services. It infers working side-by-side, being subject to supervision. The word is totally undefined in terms of identifying the work and its range and depth. Spell out explicitly what the contractor must do.

c. As Required. The result of this approach is an undefined work condition. It has no expressed limitations. It places the Government in a position of not expressing its minimal needs. It could lead to a debatable condition concerning the contractor's compliance with the contract or order. The SOW must be declarative as to its minimal needs.

d. As Applicable / As Necessary. If the Government does not know what is necessary or applicable, it must not leave to the contractor the responsibility for determining the minimal needs of the contract. The SOW should forthrightly state the requirements so that the contractor can comply with the requirement using their best efforts and expertise to accomplish the tasks.

e. As Directed. This condition, as a part of a work task in an SOW, connotes a personal services situation in which the contractor is placed under direct supervision. "When directed” may be used in conjunction with a task order contract to indicate that specific tasks may be initiated at various times during the period of contracted performance.

f. Including but not limited to. This term is generally inserted when the drafter is unsure of requirement or criteria. However, it creates an unspecific requirement which creates ambiguity. Only list known requirements.

g. Etc. This word also introduces potentially more unidentified ambiguous requirements.

5.2.5 Word usage. Another area of concern in establishing the SOW for non-personal services is the overuse of the words and phrases "support” and "engineering and technical services":

a. Support is an ambiguous term. Specify the specific type of support needed.

b. The terms "engineering and technical services" encompass a broad area of expertise. The SOW must state the minimal needs, even if it means broadening the work limitations to cover anticipated work tasks. For clarification, the SOW may include some examples of typical work to be done.

5.2.6 Language style. SOW requirements should be written in language understandable to all potential program participants. Requirements should be stated explicitly in a topical, logical, chronological, or similarly structured order, avoiding words that allow for multiple interpretations. Use technical language sparingly with simple wording predominating in concise sentences. Use "should" whenever a provision is mandatory. “Will” expresses a declaration of purpose or intent; for example, "The Government will review all recommendations and

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

provide direction within thirty calendar days." Use active rather than passive voice; for example, "The contractor should establish a program", not "A program should be established by the contractor."

Spell out acronyms and abbreviations the first time and put the abbreviated version in parentheses after the spelled-out phrases. This will define them for each subsequent use. Acronyms and abbreviations may be defined in a glossary. Many of the common acronyms used are found in the Appendix.

Use verbs that identify work and performance task requirements and answer the explicit question: "What are the work requirements?" When selecting the appropriate work word that properly expresses the degree of contractor involvement, the SOW author must explicitly define the total nature of the work requirement.

Avoid using "Any," "Either," "And/Or," as these words imply that the contractor can make a choice which may not support the intent of the SOW. Do not use pronouns. Repeat the noun to avoid any misinterpretation. Terminology should be consistent throughout the SOW. When referring to a specific item, use the same phrase or word, particularly when referring to technical terms and items. Where words can be spelled in several different ways, employ the most common spelling. Make every effort to avoid ambiguity. A list of ambiguous phrases is provided in the Appendix.

5.3 Statement of Objectives (SOO) Method.

5.3.1 SOO introduction. The SOO is a Government prepared document incorporated into the RFP that states the overall solicitation objectives. It can be used in those solicitations where the intent is to provide the maximum flexibility to each offeror to propose an innovative development approach. Offerors use the RFP, product performance requirements, and SOO as a basis for preparing their proposals including a SOW and CDRL. Note: The SOO is not retained as a contract compliance item.

5.3.2 SOO purpose. The program SOO should provide the basic, top level objectives of the acquisition and is provided in the RFP in lieu of a Government written SOW. This approach provides potential offerors the flexibility to develop cost effective solutions and the opportunity to propose innovative alternatives meeting the stated objectives. It also presents the Government with an opportunity to assess the offeror's understanding of all aspects of the effort to be performed, by eliminating the 'how to' instructions to accomplish the required effort normally contained in the SOW the Government provides to prospective offerors.

5.3.3 SOO content. The Government may include a SOO as part of the RFP, listed in Section J, attached at the end of the RFP, or referenced in Section L and/or M, and defining the top level program objectives. Alternatively, the SOO may be placed in Section L of the RFP (e.g., as an annex). The SOO is developed to be compatible with the mission need statement (MNS), operational requirements document (ORD), technical requirements from the system requirements document (SRD)/systems specification, and the WBS/dictionary. The SOO should address product oriented goals rather than performance requirements. SOOs are normally in the 2-4 page range. The SOO is not a one for one replacement of the SOW. Sections L and M should logically follow with instructions to the offerors asking for proposal information supporting the objectives and evaluation criteria that clearly identify how the offeror's responses will be evaluated. Each portion of the RFP must support one another. The key is to keep the SOO clear and concise and to provide potential offerors with enough information and detail to structure a sound program, designed to be executable and satisfy government objectives. The SOO is used, along with other information and instructions in the RFP, by offerors to develop the contract WBS, SOW, and other documents supporting and defining the offerors proposed effort. SOO content depends both on the type of program and on the program phase. It is possible that a 'mature' program, such as one which has been fielded for some time, could require slightly more detail in the SOO to properly integrate with other, ongoing parts of the program. The SOO is replaced at contract award in the contract by the proposed SOW.

1. Program Objectives
   a. Multi-phased program
   b. One program, multi-contractor
   c. One phase contract
2. Contract Objectives (WBS 00000)

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

a. Objectives in paragraph 2.0 are traceable to Level 0 WBS

b. For multi-phase programs, describe objectives for each phase in a format similar to an indentured list (clearly indicate which phases are part of the anticipated contract and any phases that will involve separate contracts).

Note: *The SOO should not address each WBS element, but each WBS element should be traceable to something in the SOO. For example, a SOO may instruct the bidder to address their engineering approach. That is not a particular WBS element, but several WBS elements might be created to breakout the engineering tasks. Generally, a broad and sweeping objective statement will trace to more WBS elements than would be the case for a very narrowly focused objective statement.*

5.3.4 SOO development approach. A systematic process is essential for SOO development. The following steps are an integral part of that process:

a. Conduct market research to determine whether commercial items or non-developmental items are available to meet program requirements.

b. Review the requirement documents which authorize the program and define its basic objectives. Complete a risk assessment and expound the basic objectives of the program to incorporate the major technical and programmatic risks.

c. Review the various DoD/services/joint services requirements documents for program management, acquisition and control impact.

d. Prepare a bibliography citing the specific portions of all applicable governing instructions, directives, specifications and standards with which the program must comply. Keep these requirements to the absolute minimum.

e. Categorize the work described by the program WBS into that which will be done in-house and the objectives of that work that need Contract Work Breakdown Structure (CWBS) to be contracted.

f. For each RFP/contract defined, prepare a SOO from the objectives identified.

5.3.5 SOO-RFP relationships.

a. Section L: Section L of the RFP must include instructions to the offeror that require using the SOO to construct and submit a SOW and CDRL. An example of such wording follows:

"The Statement of Objectives (SOO), included as (cite location of SOO in the RFP), provides the Government's overall objectives for this solicitation. Offerors should use the SOO, together with other applicable portions of this RFP, as the basis for preparing their proposal, including the CWBS, SOW and CDRL. The offeror should ensure all aspects of the SOO are addressed. The SOW should specify in clear, understandable terms the work to be done in developing or producing the goods to be delivered or services to be performed by the contractor. Preparation of an effective SOW requires both an understanding of the goods or services that are needed to satisfy a particular requirement and an ability to define what is required in specific, performance based, and quantitative terms. The offerors understanding of both required goods/services, and work effort required to accomplish should be fully demonstrated in the offeror's proposed CWBS, SOW, and CDRL. For complex interrelationships among RFP/contract documents, use of a cross-reference matrix may be helpful.

The offeror should use their proposed SOW to prepare a CDRL including appropriately tailored DID references. The requirements listed below (if any) are known minimum Government data requirements. The offeror may include additional data requirements. All data requirements should be traceable to specific tasks defined in the SOW. Specified on DD Form 1423.

1. (Cite minimum data requirements here if any)
2. . . .
3. . . .

(End of Section L example wording.)

b. Section M: Evaluation Factors for Award should include sufficient criteria to:

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

1. Evaluate the offeror's ability to successfully achieve the SOO objectives,
2. Ensure a sound approach is proposed
3. Verify that all requirements can be met.

The Government's intention to evaluate the proposed SOW should be stressed in both Section L and Section M. The offeror's proposed CWBS, SOW, and CDRL's should be evaluated as critical elements in assessing the offerors understanding of both required goods/services, and work effort required to accomplish them.

6. NOTES

6.1 Intended use. Used in the preparation of a SOW.

6.2 Subject term (key word) listing:

Contract Data Requirements List (CDRL)

Contract Line Item Number (CLIN)

Data Item Description (DID)

Request for Proposal (RFP)

Statement of Work (SOW)

Work Breakdown Structure (WBS)

6.3 Changes from previous issue. Marginal notations are not used in this revision to identify changes with respect to the previous issue due to the extent of the changes.

6.4 Additional resources. The following set of documents can assist in the development of the SOW:

The listed Parts of the FAR and Defense Finance Accounting Service (DFAS) have applicability to all Statements of Work developed for DoD acquisitions and should be referred to during the development of a SOW.

Adaptive Acquisition Framework - A set of acquisition pathways to enable the workforce to tailor strategies to deliver better solutions faster, see https://aaf.dau.edu/.

Contract Strategy Factsheet – Concise contract quick reference for all acquisition professional. https://www.dau.edu/guidebooks/Shared%20Documents/Contract%20Strategy%20Fact%20Sheets.pdf

FAR Part 10/DFARS Part 210 - Prescribes when Market Research is required for Federal (FAR) and Defense (DFARS) acquisitions. Essentially, Market Research is required before the development of any new requirements to be used in the contracting for supplies and services. Market Research must be tailored to the scope and purpose of the acquisition. Additional guidance on conducting and tailoring Market Research can be found in SD-5 Market Research (available at https://quicksearch.dla.mil/)

FAR Part 11/DFARS Part 211 - Prescribes rules and preferences for describing agency needs (stating requirements) in Federal (FAR) and Defense (DFARS) acquisitions. Agency needs as included in the Statement of Work, should reflect a balance between User's Needs (what is wanted) and Market Research (what is available or feasible).

DoD 7000.14 – Financial Management Regulation

The listed DoDIs provide policies for the development, management, and documentation of Defense Acquisition Systems and may be useful in understanding the purpose and content of the documentation for a Defense System.

DoDI 5000.02 - Provides high-level guidance and descriptions of the Adaptive Acquisition Framework Pathways available for the development of Defense Systems. https://www.esd.whs.mil/DD/

DoDI 5000.74 - Provides requirements and responsibilities for managers of the acquisition of services (as opposed to supplies) within the Department of Defense. Typically, a PWS is used in lieu of a SOW for the Acquisition of Services.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

DoDI 5000.75 - Provides requirements and Program Management roles and responsibilities in the development of Defense Business Systems. DoDI 5000.75 also provides requirements for, and a structure for, documentation for that acquisition. SOW should be aligned and consistent with program documentation (e.g., Acquisition Strategy).

DoDI 5000.87 - Provides requirements and Program Management roles and responsibilities in the development of custom software within the Department of Defense. DoDI 5000.87 also provides requirements for, and a structure for, documentation for that acquisition. SOW should be aligned and consistent with program documentation (e.g., Acquisition Strategy).

DoDI 5000.81 - Identifies the types and sources of Urgent Operational Needs (UONs) and provides requirements and Program Management role and responsibilities in the development and fielding systems to meet those UONs. DoDI 5000.81 also provides requirements for, and a structure for, documentation for that acquisition. Statements of Work should be aligned and consistent with program documentation (e.g., Acquisition Strategy).

DoDI 5000.80 - Provides requirements definitions and procedures for the conduct of Middle Tier of Acquisition (Rapid Prototyping or Rapid Employment) program. DoDI 5000.80 also provides Program Manager and Product Support Manger roles and responsibilities and the associated procedures associated with the Middle Tier of Acquisition. SOW should be aligned and consistent with program documentation (e.g., Acquisition Strategy).

DoDI 5000.85 - Provides requirements and Program Management roles and responsibilities in the development of systems being develop as Major Capability Acquisitions within the Department of Defense. DoDI 5000.85 also provides requirements for, and a structure for, documentation for that acquisition. SOW should be aligned and consistent with program documentation (e.g., Acquisition Strategy).

DoDI 5000.88 - Provides policy and procedures for conducting a comprehensive engineering program for defense systems, including the engineering management activities necessary to guide the development of defense systems. Engineering tasks included within a SOW should be aligned with the engineering program documentation developed in accordance with DoDI 5000.88 (e.g., Systems Engineering Plan).

DoDI 5000.89 - Provides guidance for the planning and execution of Test and Evaluation in support of Defense Acquisition Programs. Test and Evaluation tasks included within a SOW should be aligned and consistent with program test and evaluation documentation developed in accordance with DoDI 5000.89(e.g., Acquisition Strategy, Test and Evaluation Master Plan).

DoDI 5010.44 - Provides policy for the development and implementation of Intellectual Property strategies. Tasks related to the acquisition of Intellectual Property in Statements of Work should be aligned and consistent with program documentation developed in accordance with DoDI 5010.44 (e.g., Intellectual Property Strategy).

DoDI 5000.82 - Provides policies and procedures for the Acquisition of Information Technology within the Department of Defense. DoDI 5000.82 also identifies unique program documentation associated with the acquisition of Information Technology. SOW tasks associated with the acquisition of Information Technology within SOW should be aligned and consistent with applicable program documentation developed in accordance with DoDI 5000.82 (e.g., Acquisition Strategy, Cybersecurity Strategy).

DoDI 5000.86 - Provides requirements and identifies key acquisition documents associated with Acquisition Intelligence. Statements of work including Acquisition Intelligence related tasks should be aligned and consistent with program documentation developed in accordance with DoDI 5000.86 (e.g., Acquisition Strategy, Program Protection Plan)

DoDI 5000.83 - Establishes policy, assigns responsibilities, and provides procedures for science and technology (S&T) managers and engineers to manage system security and cybersecurity technical risks. DoDI 5000.83 also identifies considerations to be included in the development of the Science and Technology and Program Protection Plans, SOW tasks associated with Science and Technology Protection or Program Protection should be aligned and consistent with applicable program documentation developed in accordance with DoDI 5000.83 (e.g., Program Protection Plan)

DoDI 5000.84 - Provides policy for the conduct of Analyses of Alternatives within the Department of Defense. Statements of work associated with the conduct or support of an Analysis of Alternatives (AoA) should be consistent with the approved program documents developed in accordance with DoDI 5000.84 (e.g., Initial Capabilities Documents (ICD), AoA Study Guidance, and AoA Study Plan).

DoDI 5000.87 - Provides instruction for the “Operation Of The Software Acquisition Pathway”. The software acquisition pathway is for the timely acquisition of custom software capabilities developed for the DoD. Software programs that meet the definition of a covered Defense Business System (DBS) should use the DBS pathway in accordance with DoDI 5000.75 but may elect to incorporate this pathway for custom developed software. Programs executing the software acquisition pathway are not subject to the Joint Capabilities Integration and Development

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

System (JCIDS). Programs executing the software acquisition pathway will not be treated as major defense acquisition programs even if exceeding thresholds in Section 2430 of Title 10, United States Code. See Section 800 of Public Law 116-92.

DoDI 5000.90 - Prescribes policy, responsibilities, and procedures for the implementation of Cybersecurity within DoD acquisitions. SOW that include Cybersecurity tasks should be aligned to the program documentation developed in accordance with DoDI 5000.90 (e.g., Cybersecurity Strategy (CSS), Program Protection Plan.)

SAE-GEIA-859 - Data Management Standard

(Note: The SAE-GEIA-859, has been adopted by the DoD as the Data Management Standard. Copies of these documents are available online at https://www.dau.mil.edu/tools/dag).

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

WORK WORDS/PRODUCT WORDS

A.1 SCOPE

A.1.1 Scope. The appendix provides a set of guiding critical differences in the meaning of work words versus the product words identified in connection with deliverable data. The sample list of work words and product words assist the SOW writer to clearly describe work performed verses products delivered.

A.2 PROCEDURE

A.2.1 Select the key word. Select the key word that properly defines the degree of contractor involvement. Specify what is to be done and the total nature of the work requirement. The word list provided in this Appendix is not complete but is provided to stimulate the thinking of the SOW writer by pointing out the critical differences in the meaning of work words versus the product words identified in connection with deliverable data.

A.2.1.1 Work words. When selecting the key work word that properly expresses contractor's involvement, the SOW writer must define explicitly the total nature of the work requirement in terms of what is to be done. In some cases, the "why" or the application of the results of the performed work may be stated if it clarifies the requirement. The following sample list contains words that have the inherent value of work. This list is offered as a reminder of the various shades of meaning conveyed by choice of words.

Analyze	(solve by analysis)
Annotate	(provide with comments)
Ascertain	(find out with certainty)
Attend	(be present at)
Audit	(officially examine)
Build	(make by putting together)
Calculate	(find out by computation)
Consider	(think about, to decide)
Construct	(put together; build)
Control	(direct; regulate)
Contribute	(give along with others)
Compare	(find out likeness or differences)
Create	(cause to be; make)
Determine	(resolve; settle; decide)
Differentiate	(make a distinction between)
Develop	(bring into being or activity)
Define	(make clear; settle the limits)
Design	(perform an original act)
Erect	(put together; set upright)
Establish	(set up; settle; prove beyond dispute)

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Evaluate	(find or fix the value of)
Evolve	(develop gradually, work out)
Examine	(look at closely; test quality of)
Explore	(examine for discovery)
Extract	(take out; deduce, select)
Fabricate	(build; manufacture, invent)
Form	(give shape to; establish)
Formulate	(to put together and express)
Generate	(produce, cause to be)
Identify	(to show or to find)
Implement	(to carry out, put into practice)
Install	(place; put into position)
Inspect	(examine carefully or officially)
Institute	(set up; establish, begin)
Interpret	(explain the meaning of)
Inquire	(ask, make a search of)
Integrate	(to add parts to make whole)
Investigate	(Search into; examine closely)
Judge	(decide; form an estimate of)
Make	(cause to come into being)
Maintain	(to keep in an existing state, to continue in, carry on)
Manufacture	(fabricate from raw materials)
Modify	(to change, alter)
Monitor	(to watch or observe)
Notice	(comment upon, review)
Observe	(inspect, watch)
Originate	(initiate, to give rise to)
Organize	(integrate, arrange in a coherent unit)
Perform	(do, carry out, accomplish)
Plan	(devise a scheme for doing, making, arranging activities to achieve objectives)
Probe	(investigate thoroughly)
Produce	(give birth or rise to)
Pursue	(seek, obtain or accomplish)
Reason	(think, influence another’s actions)
Resolve	(reduce by analysis, clear up)
Record	(set down in writing or act of electronic reproduction of communications)
Recommend	(advise, attract favor of)
Review	(inspection, examination or evaluation)
Revise	(to correct, improve)
Study	(careful examination or analysis)
Seek	(try to discover; make an attempt)

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Search	(examine to find something)
Scan	(look through hastily, examine intently)
Screen	(to separate, present, or shield)
Solve	(find an answer)
Test	(evaluate, examine)
Trace	(to copy or find by searching)
Track	(observe or plot the path of)
Update	(modernize, make current)

A.2.1.2 Product word list. Although Non-personal Services contracts may not result in data as a deliverable product, a large portion do. This list of product words is provided to assist in identifying those products.

Agenda	Manuals
Audio visual aids	Manuscript
Books	Materials
Cards	Minutes
Certificates	Outlines
Charts	Proposals
Databases	Pamphlets
Data centers	Plans
Decks	Portals
Documentation	Procedures
Publications	Recommendations
Drawings	Records
Drives	Recordings
Equipment	Reproducible
Files	Requests
Findings	Sheets
Forms	Software
Guides	Specifications
Graphics	Standards
Hardware	Systems
Illustrations	Tapes
Lists	Web sites
Ledgers	
Logs	

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

LIST OF PHRASES HAVING MULTIPLE MEANINGS

B.1 SCOPE

B.1.1 Scope. This appendix provides a list of phrases having multiple meanings. This list is provided as an example of those phrases to be avoided. The appendix does not provide an exhaustive list of examples, like constructs of open ended scope language are to be avoided.

B.2 GUIDANCE

B.2.1 List of phrases having multiple meanings.

To the satisfaction of the contracting officer,
As determined by the contracting officer,
In accordance with instructions of the contracting officer,
As directed by the contracting officer,
In the opinion of the contracting officer,
In the judgment of the contracting officer,
Unless otherwise directed by the contracting officer,
To furnish if requested by the contracting officer,
All reasonable requests of the contracting officer should be complied with,
Photographs should be taken when and where directed by the contracting officer.
In strict accordance with,
In accordance with best commercial practice,
In accordance with best modern standard practice,
In accordance with the best engineering practice,
Workmanship should be of the highest quality,
Workmanship should be of the highest grade,
Accurate workmanship,
Securely mounted,
Installed in a neat and workmanlike manner,
Skillfully fitted,
Properly connected,
Properly assembled,
Good working order,
Good materials,
In accordance with applicable published specifications,
Products of a recognized reputable manufacturer,

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Tests will be made unless waived,

Materials should be of the highest grade, free from defects or imperfections, and of grades approved by the contracting officer.

Kinks and bends may be cause for rejection,

Carefully performed,

Neatly finished,

Metal parts should be cleaned before painting,

Suitably housed,

Smooth surfaces,

Pleasing lines,

Of an approved type,

Of standard type,

Any phrases referring to "The Government inspector."

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

STATEMENT OF WORK EXAMPLE

C.1 SCOPE

C.1.1 Scope. This appendix provides an example Statement of Work (SOW).

C.2 APPLICABLE DOCUMENTS

C.2.1 Applicable documents. All documents invoked in the requirements section of the SOW must be listed in this section by document number and title. These documents may include Standards, Specifications and other reference documents needed to identify and clarify the work task or deliverable product. DoD and Departmental Instructions should not be used in the SOW to control contractor effort. Also, any document listed in this section must be invoked and selectively tailored to meet minimal needs of the planned procurement in the requirements section. The version of any document cited in the SOW should be specified in this section.

C.2.2 Department of Defense specifications.

C.2.3 Department of Defense standards.

C.2.4 Other Government documents.

C.2.5 Industry documents.

C.3 GENERAL REQUIREMENTS (FUNDING TYPE)

C.3.1 General requirements. The below are sample sections per the Defense Acquisition Guide (DAG). The content of the SOW is dependent on which phase of the acquisition cycle you are in. A SOW for an R&D effort is different than production. Remember work requirements are stated in the SOW, not how to build it. The funding type identified at the “GENERAL REQUIREMENTS” paragraph implies one funding type to support the effort.

C.3.2 Program Management. The progress, status and management reports will be provided. The reports address the progress of the effort, status of any problem resolution or identification of new problems, summary of safety-related actions, significant events, and updated contract schedule.

a. CDRL Deliverable(s):

b. Progress, Status, and Management Report

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

C.3.3 Program Reviews. The contractor shall conduct quarterly reviews, report on cost, schedule, technical progress, program risks and mitigations, and technical performance measures. The contractor shall present the Risk Management Database and Risk Management Chart as part of the Project Management Review Presentation Materials.

a. CDRL Deliverable(s)
b. Conference Agenda
c. Presentation Material
d. Report, Record of Meeting / Minutes

C.3.4 System Engineering (SE). SE ensures the effective development and delivery of capability through the implementation of a balanced approach with respect to cost, schedule, performance, and risk using integrated, disciplined, and consistent SE activities and processes. SE-related policy, guidance, specifications, and standards are intended to successfully guide the technical planning and execution of a program across the acquisition life cycle.

C.3.5 Environment, Safety, and Occupational Health (ESOH). Perform ESOH hazard identification and risk management in accordance with MIL-STD-882E. The safety assessment identifies safety-related hazards that may be present in the physical system configuration, including specific procedural controls and precautions that should be followed for risk mitigation. Identify hazardous materials contained in or used with the system. Include environmental and occupational health risks in ESOH assessments. Hazardous materials are to be identified for systems per DoDI 5000.85 and DoDI 5000.88.

C.3.6 Reliability and Maintainability Program. Create and maintain a Failure Reporting and Corrective Action System (FRACAS) to document all problems found during the manufacturing, fabrication, assembly, test, operation, and maintenance aspects of the system life cycle for each system produced.

a. CDRL Deliverable(s):
b. FRACAS Report

C.3.7 Data. Technical data and rights to that data are described in relation to the technical design and implementation as well as cost, schedule, performance, and risk in this section. Data related topics are described such as:

a. Compatibility requirements with DoD computing infrastructure.
b. Compatibility requirements with DoD physical infrastructure.
c. Description of drawings, practices, procedures and deliverables.
d. Hardware and software information

C.3.8 Human System Integration (HSI). As part of SE, integrate consideration for the human part of the system into the design and operations of the system by inserting into manpower, personnel, training, human factors engineering, environment, safety, occupational health hazards, and personnel survivability areas. (Describe the Manpower, Personnel and Training and Education requirements for a cybersecurity workforce needed in the Cybersecurity section D.3.10)

C.3.9 Electromagnetic (EM) Spectrum Requirements and Electromagnetic Environmental Effects (E3). For spectrum dependent systems, identify what frequency assignments and spectrum certifications such as DD Form 1494 are needed. E3 control is concerned with proper design and engineering to minimize the impact of the EM

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

environment on equipment, systems, and platforms. See standards and handbooks such as MIL-STD-461 in ASSIST.

C.3.10 Technical Reviews and Updates. Provide SE and technical reviews that include technical and programmatic cost, schedule and performance status and risks. These reviews will be in coordination with other required reviews and meetings in the SOW to increase coordination and reduce duplication.

a. CDRL Deliverable(s)

b. Conference Agenda.

c. Presentation Material.

d. Report, Record of Meeting / Minutes.

C.3.11 Cyber Security. Ensure procedures and processes are in place for the protection of DoD program information residing on or transiting DoD and corporate networks and information systems. The objective is to protect DoD information, not just DoD systems, and it relates to all programs, not just those Information Technology (IT) focused.

Address cybersecurity workforce challenges and efforts designed to improve Manpower, Personnel, Training and Education in a challenging cyber environment. Describe the type of workforce available to work on cyber security issues.

C.3.12 Configuration Management. The CM plan documents life cycle CM planning and provides CM program milestones and schedules to monitor program status. Implement an internal CM system for the control of all configuration documentation, physical media, and physical parts. For software, the system shall address the evolving configuration and support environments (engineering, implementation, and test) used to generate and test the product.

C.3.13 Configuration Change. Establish and maintain a Configuration Status Accounting (CSA) database. All baselines and changes shall be documented in the database. Provide CSA reporting in accordance with the guidelines in section 7 “Configuration Status Accounting” in MIL-HDBK-61B. Provide the traceability of all changes from the original baseline configuration documentation of each configuration item.

a. CDRL Deliverable(s):

b. Configuration Status Accounting Report

C.3.14 Packaging Handling, Storage and Transportation. Package and handle hardware and related parts in accordance with MIL-STD-2073-1E, Change Notice 1 DoD Standard Practice for Military Packaging.

C.3.15 Diminishing Manufacturing Sources and Material Shortage. Manage obsolescence over the entire period of the contract, and notwithstanding any obsolescence issues or problems, the Contractor remains responsible for meeting all performance and other requirements of this contract.

a. CDRL Deliverable(s):

b. Annual Obsolescence Report

C.3.16 Physical Configuration Audit. The contractor shall conduct a Physical Configuration Audit (PCA) jointly with the Government, The contractor shall develop and deliver a Configuration Audit Plan. (CDRLA002) At the

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

completion of PCA and all action items are closed, the contractor shall develop and deliver a Configuration Audit Summary Report. (CDRLA018)

a. CDRL Deliverable(s):

b. Configuration Audit Summary Report (Physical)

C.3.17 Provisioning Items Ordering Spares. Delivery of spare parts for provisioning orders. Provisioning Items Ordering (PIO) will be ordered by the Government in accordance with the PIO CLIN in the contract which is defined upon contract award.

C.3.18 Reliability and Maintainability Program. Create and maintain a Failure Reporting and Corrective Action System (FRACAS) to document all problems found during the manufacturing, fabrication, assembly, test, operation, and maintenance aspects of the system life cycle for each system produced.

a. CDRL Deliverable(s):

b. FRACAS Report

C.3.19 Test and Certification. Submit a Production Test Plan, which shall address Low-Rate Initial Production (LRIP) and Full Rate Production (FRP) test events.

a. CDRL Deliverable(s):

b. Production Test Plan

C.4 NOTES

C.4.1 Definitions. Provide definitions of key terms such as:

Waiver - A waiver is the acceptance of an item, which during manufacture, or after having been submitted for Government acceptance is found to depart from specified requirements, but nevertheless is considered suitable for use “as is” or after repair by an approved method.

Deviation - Deviation is the Government approval prior to the manufacture of an item, to depart from a particular requirement(s) of an item’s current approved configuration documentation for a specific number of units or specified period of time. A deviation is a temporary departure from the requirements and does not change the product baseline.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

GENERIC STATEMENT OF WORK (SOW) TEMPLATE

D.1 SCOPE

D.1.1 Scope. This appendix provides a generic Statement of Work (SOW) Template.

D.2 FORMAT

D.2.1 Format. The SOW format herein is only meant to be a guide and is not necessarily all-inclusive; as such, contents should be tailored to the requirement. Consult your National Oceanic and Atmospheric (NOAA) Acquisition and Grants Office (AGO) Contracting Officer and the NOAA Acquisition Process Guide (APG) for further guidance.

D.3 PREPARATION

D.3.1 Preparation. You will need to prepare a SOW, for instance, when acquiring a service but not relying on the Contractor's commercial description to define the requirement. In this situation, purchasers are tailoring the commercial services performed by the Contractor (e.g., program management services) to meet a particular Government need (e.g., management of a process improvement program).

D.4 SOW SECTIONS

D.4.1 SOW sections:

- Background
- Objectives
- Scope
- Applicable Documents
- Requirements
- Tasks
- Delivery
- Government-Furnished Property (GFP)
- Security Considerations
- Travel
- Special Material Requirements
- Other Unique Requirements and Considerations
- Place of performance
- Period of performance
- Notes

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

D.5 BACKGROUND

D.5.1 Background. Identified as the "Introduction," this section provides information needed to acquaint the reader with the basic acquisition situation. The background information may:

- Identify the requirement in very general terms;
- Describe why the project is being pursued and how it relates to other projects;
- Summarize any statutory authority or regulations affecting the overall requirement; and
- Identify any background materials attached to the SOW.

D.6 OBJECTIVES

D.6.1 Objectives. This section should provide a concise overview of:

- The contract effort goals and objectives; and how the results or end products will be used.

D.7 SCOPE

D.7.1 Scope. Provide a brief statement of what the Government expects to accomplish under the contract-the breadth and limitations of the contract effort. It should not include specific work tasks or a description of deliverable products.

D.7.2 APPLICABLE DOCUMENTS

D.7.3 REQUIREMENTS

D.7.4 TASKS

D.7.4.1 Tasks. Sometimes identified as "Requirements" or "Work Requirements," this section defines the tasks that the Contractor must complete during contract performance. The description of task requirements will depend on the approach that is selected to describe the required effort.

- For a Performance-Based Work Statement, this section should describe requirements in terms of results required rather than the methods for completing the work. This latitude will permit the Contractor to develop new and innovative ways to complete those tasks.
- For a Level of Effort Statement of Work, this section should identify all tasks that must be performed and the hours to be devoted to each task.
- For a Detailed Statement of Work, this section should describe how the service must be accomplished. It may include precise measurements, tolerances, materials, quality control requirements, and other Government requirements that control the processes of the Contractor.

D.7.4.2 Government supervision. This section must describe requirements in a way that permits Contractor personnel to perform the service without direct Government supervision. Contractor personnel must not be subject to the type of supervision and control usually prevailing between the Government and its employees. For example, a SOW may permit the Government to approve key personnel, but must not permit the Government to approve all personnel performing the service. The SOW should also not include words (e.g., "use methods directed by the

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Contracting Officer's Representative (COR)") that appear to indicate that the Government is managing day-to-day operations. Other items to consider:

- Specify requirements clearly so that all readers can understand them.
- Reference only the absolute minimum applicable specifications and standards needed.
- Tailor specifications and other documents.
- Separate general information from direction.

D.8 TASK EXAMPLE

D.8.1 Task Areas. Include specific titles of all tasks for required performance.

Task 1 Title as applicable

Task 2 Title as applicable

Task 3 Title as applicable

D.8.2 Project Milestones/Completion Dates (Estimates and as applicable)

Task Number	**Work Milestones**	**Projected Completion Date**
1	Describe in-process milestone as applicable (first for this task)	Date
	Describe in-process milestone as applicable (second for this task)	Date
	Describe in-process milestone as applicable (third for this task)	Date
2	Describe in-process milestone as applicable	Date
3	Describe in-process milestone as applicable	Date

D.8.3 Task 1 – Title. Describe the specific service to be provided for this task. Include milestones that are to be accomplished as applicable and as identified on the milestone schedule. Milestones can include such things as preliminary reports or data submittals, attendance at meetings, etc.

D.8.4 Task 2 – Title. Describe the specific services to be provided. Include milestones that are to be accomplished as applicable and as identified on the milestone schedule. Milestones can include such things as preliminary reports or data submittals, attendance at meetings, etc.

D.8.5 Task 3 – Title. Describe the specific services to be provided. Include milestones that are to be accomplished as applicable and as identified on the milestone schedule. Milestones can include such things as preliminary reports or data submittals, attendance at meetings, etc.

D.9 DELIVERY

D.9.1 Delivery. This section should clearly state:

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

- What the Contractor must deliver. If different tasks have different delivery requirements, they must be clearly identified.
- When the Contractor must deliver. This may be stated using actual dates, days after contract award, or using some other method that clearly marks the required delivery date.
- Where the Contractor must deliver the service. This may be stated as a location, an organization, a person identified by position (e.g., Contracting Officer's Representative, a person identified by name or using some other description.)
- What documentation (if any) the Contractor must obtain from the Government to verify Government receipt of the delivery.
- Other items to consider: Include any associated review periods or incorporation of Government comments as applicable. Deliverables are different than task completion milestones. Milestones may not require a specific submittal. Include here the schedule for when final products such as data, reports or other items are required to be furnished to the primary requestor.

D.9.1 Example Deliverable Schedule

Deliverable	Description	Quantity/Media	Date Completed
1	Identify the specific deliverable	e.g. 5 printed copies and 3 copies on CD-ROM	dd-mm-yyy
	Government review (as applicable)		dd-mm-yyy
	Resubmit with Government comments	e.g. 5 printed copies and 3 copies on CD-ROM	dd-mm-yyy
2	Identify the specific deliverable	As applicable	dd-mm-yyy
3	Identify the specific deliverable	As applicable	dd-mm-yyy

D.9.2 Government-Furnished Property, Material, Equipment, or Information (GFP, GFM, GFE, or GFI). This section should identify any Government-furnished property provided to the Contractor. This includes all Government-furnished property, such as Government-furnished material, equipment, or information. If the list of property is extensive, this section should identify where that list can be found. Before offering to provide any property, make sure that it will be available when required, where required, and in the condition required by the contract. Failure to meet Government-furnished property requirements often lead to a Contractor claim for an equitable adjustment to contract price, delivery, or other requirements. See FAR 45 and NOAA APG for specific requirements about providing Government-furnished property.

D.9.3 Security. This section should identify any unique security requirements associated with contract performance (when applicable). These requirements may include, but are not limited to, such items as:

- Special pass or identification requirements;
- Special security clearance requirements; or
- Special escort requirements.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

D.9.4 Travel. Describe any travel requirements that are to be encountered in the performance of the service(s).

D.9.5 Special Material Requirements. Describe requirements for any special materials that are to be encountered in the performance of the service(s).

D.9.6 Other Unique Requirements. Discuss any other unique requirements or considerations, e.g. - Unique Item Identification (UID) and Radio Frequency Identification (RFID).

D.9.7 Place of Performance. This section should identify where the contract will be performed. If performance will occur at multiple Government locations, this section should indicate which tasks must be completed where. If performance will be at the Contractor's facility, the SOW need only state that requirement.

D.9.8 Period of Performance. The period of performance may be stated using actual dates, days after contract award, or using some other method. If different periods of performance will apply to different tasks, the tasks and related periods of performance should be clearly identified

---

D.10 SOW LANGUAGE TIPS

D.10.1 SOW Language tips. A variety of people with different perspectives and life experiences will read your SOW. Readers typically include Government and industry contracting personnel, managers, technical experts, accountants and lawyers. All these readers need to understand the SOW in a clear and concise manner; therefore, language selection is very important.

D.10.2 Tips to consider. Below are tips that you should consider when reviewing the SOW:

- Use simple words, phrases, and sentences whenever practical.
- Be concise, precise, and consistent. Keep sentences short and to the point. Normally the longer the sentence, the harder it is to understand.
- Use verbs in the active voice. A verb is in the active voice when it expresses an action performed by its subject. For example, "The Contractor shall report contract progress quarterly." Conversely, avoid using verbs in the passive voice. A verb is in the passive voice when it expresses an action performed upon its subject or when the subject is the result of the action. For example, "Contract progress shall be reported quarterly by the Contractor."
- Use "shall" or "must" when writing a requirement binding on the Contractor. Avoid "should" or "may" because they leave the decision on appropriate action up to the Contractor.
- Use "will" to indicate actions by the Government.
- Be consistent when using terminology. Use the same word to mean the same thing throughout your SOW. Avoid using different words to indicate the same type of action.
- Avoid redundancy. At best, requiring the Contractor to do the same thing in different parts of the SOW will add needless words to the SOW. At worst, there may be subtle differences in the requirements that may lead to a dispute during contract performance.
- Avoid vague or inexact phrases and generalizations.
- Avoid catchall and open-ended phrases, such as, "is common practice in the industry," "as directed," or "subject to approval." If you want to give the Contractor an opportunity to use their standard commercial practices, require each offeror to identify its commercial practices in a proposal and then include that proposal as part of the order/contract.
- Define technical terms.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

- Avoid using Government jargon. Assure that it is clearly defined whenever jargon must be used.
- Only use “any,” “either,” “and/or,” “etc.” when allowing the Contractor to select an alternative.
- Use abbreviations or acronyms only after spelling them out the first time they are used (e.g., National Climatic Data Center (NCDC)). Spell them out even if they are commonly used by NOAA because a commercial Contractor may not be familiar with them.
- Identify the date or version of any document referenced in your SOW.

D.11 NOTES

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

VIRTUAL ACQUISITION OFFICE (VAO) SOW TEMPLATE

E.1 SCOPE

E.1.1 Scope. This appendix provides a Virtual Acquisition Office (VAO) SOW Template.

E.2 TITLE SHEET FORMAT

E.2.1 Example title sheet follows:

<Insert Agency Name>

<Insert Program Office Name>

<Insert Project Name>

Statement of Work
for the
<Insert Acquisition Title>

<Insert Date>

E.3 DOCUMENT REVISION HISTORY

E.3.1 Document revision history

[*Example – Post-award*]

Mod. No.	Description of Changes	Requested By	Approved By	Date
None	Initial version	T. Smith	Thomas Smith	10/01/20XY
01	Added Task 005 to include transition of files from PDF format	J. Jones	Thomas Smith	12/15/20XY
03	Revised the mean time between failures	R. Howard	Thomas Smith	03/06/20XZ
0X				
0Y				
0Z				

[Note: The document revision history is most useful for tracking changes in a major acquisition. It may not be needed for less complex acquisitions. Pre-award, it can be used internally by the agency to track the origin of and/or changes to specific requirements (not included in the solicitation when released). Post-award, it can be used to provide a centralized list of changes incorporated by modification.]

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

E.4 SCOPE

E.4.1 Background. The mission of the <insert name of agency> is to <insert brief statement of agency mission>. The mission of the <insert name of program or project office> is to <insert brief statement of program/project mission >. This acquisition <insert brief overview and history>.

[Describe the general history and overview of the acquisition: what it is, why it's needed, who needs it, and for what purpose. Knowing how this procurement relates to predecessor acquisition(s) (if any) can help the contractor understand the basis for the government's need and what is required to perform or provide it.]

E.4.2 Objective. [The objective statement should tell the contractor what this initiative is trying to achieve: Do you need a faster, more efficient, more responsive, more user-friendly IT system? A need for maintenance of a water treatment plant including testing and provision of all required chemicals and compliance with Environmental Protection Agency (EPA) and local monitoring and testing requirements? An analysis of how program beneficiaries locate and use agency resources? How will that support your agency's mission?]

E.4.3 Scope of Work. [Provide a brief synopsis that summarizes the key elements of the requirement. Sample text: The contractor shall provide all resources necessary to accomplish the tasks and deliverables described in this Statement of Work (SOW). The contractor shall <insert a synopsize the project in a few key sentences)>.]

E.4.4 Period of Performance. The period of performance of this contract is <insert the period of performance>. [The period of performance can be expressed either via date certain (e.g. "from February 1, 20WX to January 31, 20YZ") or in relation to award, if the award date is not yet known (e.g. "36 months from the date of award"). It should also indicate whether the contract includes options (e.g. "The period of performance of this contract consists of a base year and four option years, beginning on October 1, 20XY" or if using a date from date of award – state the duration of each option period). Cite any clause or other reference to the period of performance that provides additional information.]

E.4.5 Place of Performance. <Describe the place of performance.>
[Contracts may be performed entirely at the contractor's facility (off site); entirely at a government facility (on site); partially at the contractor's primary facility, and partially at other locations or facilities (off-site); within the United States; in a foreign location; or at various locations. Specify where the work will take place, and identify any restrictions that may attach (such as, at a government facility, but only on days on which government operations are being conducted). Note that a number of legal, financial, and security considerations may attach to the place of contract performance, such as the Buy American statute, the allowable overhead cost applied, the expense and time associated with travel to and from a given location to attend meetings and reviews, and whether special security requirements will apply.]

E.5 APPLICABLE DOCUMENTS

E.5.1 Applicable documents. [Include applicable technical specifications, manufacturing standards, and security requirements, together with any other government-furnished information specific to the procurement. Include only the documents that are essential for performance of the contract. For ease of reference, we recommend providing hyperlinks to any documents that are publicly available instead of providing them individually upon request.

Citing these documents makes them enforceable under the contract, so the contractor can be held legally accountable for failure to comply. However, imposing tighter specifications than necessary may result in inflated costs to the government, so do not ask for adherence to specifications or standards that do not add needed value to the end-item or will not be used.

We recommend referencing only the relevant sections. Clearly identify which are for guidance only and which are for contract compliance.]

E.6 SPECIFIC REQUIREMENTS/TASKS

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

E.6.1 Task One
2.1.1 Subtask (*if any*)
2.1.2 Subtask

E.6.2 Task Two
Subtasks (*if any*)

E.6.3 Task Three (etc.)

[Describe the specific tasks the contractor must perform. Provide direction on any specific methodologies. (Also see FAR 8.405-2(b) for useful items to include in a SOW.) The description of task requirements will depend on the approach that is selected to describe the required effort.

- For a level-of-effort statement of work, this section should identify all tasks that must be performed and the estimated hours to be devoted to each task.
- For a detailed statement of work, this section should describe how the service must be accomplished. It may include precise measurements, tolerances, materials, quality control requirements, and other government requirements that control the processes of the contractor.

Define requirements in terms that encourage offerors to supply commercial items, or, to the extent that commercial items suitable to meet the agency's need are not available, non-developmental items.

This section must describe requirements in a way that permits contractor personnel to perform the service without direct government supervision. Contractor personnel must not be subject to the supervision and control usually prevailing between the government and its employees. For example, a SOW may permit the government to approve key personnel, but must not permit the government to approve all personnel performing the service. The SOW should also not include words (e.g., "use methods directed by the Contracting Officer's Representative (COR)") that appear to indicate the government is managing day-to-day operations. Other items to consider:

- Specify requirements clearly so all readers can understand them.
- Reference only the absolute minimum applicable specifications and standards needed.
- Tailor specifications and other documents.
- Separate general information from direction.
- Phrase requirements in layperson language. If you must use statistical and other technical terminology, provide a glossary of terms.

Also include references to desired performance and quality outcomes for both goods and services and the tools the government will use to ascertain their achievement. These will become the basis for performance metrics and the Quality Assurance Surveillance Plan.]

E.7 DELIVERY or DELIVERABLES

E.7.1 Delivery or deliverables. [For Department of Defense use "Contractor Data Requirements List" (CDRL), DD Form 1423, 1423-1, or 1423-2 per DFARS 215-470. These forms may be adapted by civilian agencies if/as applicable (see for example NOAA).]

[Provide a centralized compilation of all data and deliverable requirements of the contract; when (and how often) they are required; in what format and quantity; and to whom they are to be delivered. Displaying this in tabular format assists in post award administration. When data requirements are scattered throughout the SOW and specifications, they can be easy to miss. Creating a centralized checklist facilitates timely, compliant delivery of all necessary data and reports. You can either include it in the body of the SOW document, or cross-reference here to a separate document, and list it in the attachments.

Where a written milestone deliverable is required in draft form, indicate a completion time for the agency's review of the draft deliverable, e.g. within calendar days from date of receipt. The agency should also indicate the number of days the contractor has to deliver the final deliverable from date of receipt of the government's comments.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Sample Text: Timely submission of deliverables and reports is essential to successfully completing this requirement. Schedules for deliverables are specified in the attached <reference the table or DD Form 1423s>. All deliverables shall be prepared and submitted according to media, content, and schedule described in the <insert table or CDRL> and SOW.

FAR 4.10 – Uniform Use of Line Items, provides the following guidance for line items and subline items:

- Each line item may be subdivided into separate unique subsets (called subline items) to ease administration. If a line item has deliverable subline items, the line item is informational. A line item with subline items will contain only the information that is common to all subline items under it.
    - Subline items differentiate between or among certain characteristics of the line item, such as colors or sizes, dates of delivery, destinations, or places of performance.
    - Subline items are established to define deliverables or organize information about deliverables.
    - You may use informational subline items for administrative purposes. This type of subline item identifies information that relates directly to the line item and is an integral part of it (e.g., parts of an assembly or parts of a kit). Position informational subline items within the line item description, not in the quantity or price fields.
- Each line item:
    - Must be separately identifiable. Services are separately identifiable if they have no more than one statement of work or performance work statement.
    - Provide for a single unit price or total price
    - Identify the accounting classification citation
    - Identify the delivery schedule, destination, period of performance, or place of performance
    - Use a single contract pricing type (e.g., fixed-price or cost-reimbursement – no combinations in a single line item).
    - All subline items under one line item must be the same contract type as the line item.
    - Note -- this does not prohibit using different contract types for different line items, only that an individual line item can use only a single contract type.
    - If a contract contains a combination of fixed-price, time-and-materials, labor-hour, or cost-reimbursable line items, identify the contract type for each line item in the schedule (or a comparable section of the procurement instrument) to facilitate payment
- Table 1 at the end of this template provides a model covering the FAR required data elements. Elements denoted by an * in are recommended by VAO.
- Exceptions:
    - Indefinite-delivery contracts. The following elements are not known at time of award but must be provided in each order issued: accounting classification, delivery date and destination, or period and place of performance
    - Indefinite Delivery/Indefinite quantity (IDIQ) and requirements contracts. May omit the quantity at the line item level for the base award provided that the total contract minimum and maximum, or the estimate, respectively, is stated
    - Single unit price or single total price. The requirement for a single unit price or single total price at the line item level does not apply if any of the following conditions are present:
        - There are associated deliverable subline items that are priced
        - The line item or subline item is not separately priced
        - The supplies or services are being acquired on a cost-reimbursement, time-and-materials, or labor-hour basis.
        - The procurement instrument is for services and firm prices have been established for elements of the total price, but the actual number of the elements is not known until performance (e.g., a labor-hour contract for maintenance/repair). The contracting officer may structure these procurement instruments to reflect a firm or estimated total amount for each line item.
- VAO recommends including the following notice to contractors:

Notice to contractors:

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

All information and data related to this project that the contractor gathers or obtains shall be both protected from unauthorized release and considered the property of the government. The contracting officer will be the sole authorized official to release verbally or in writing, any data, the draft deliverables, the final deliverables, or any other written or printed materials pertaining to this contract. Press releases, marketing material, or any other printed or electronic documentation related to this project, must not be publicized without the written approval of the contracting officer.]

[Note: Use sections 3.0-9.0 as applicable to your requirement.]

E.8 MEETINGS

E.8.1 Meetings. [Explain the contractor's responsibilities for attending and/or supporting meetings. For example: For all meetings, the contractor shall be responsible for providing meeting materials, and administrative and facilitation support. Meetings will be conducted at either the <insert agency> location at <insert address>, or through an alternative method of communication (such as a teleconferencing), as approved by the Contracting Officer.

Sample text, as applicable, for specific types of meetings. Require only the meetings that are essential to performance monitoring. For example, a contract for delivery of commercial products may not require any meetings.

E.8.2 Post-award Kickoff Meeting. Within _____ business days of contract award, the Government will conduct a post-award kickoff meeting at <insert location> (specific date and time to be mutually agreed upon).

E.8.3 Intermittent Project Status Reviews. At the sole discretion of the Government, intermittent project status reviews may be conducted on an informal basis (by telephone or teleconference) or in person at <insert location> on <insert time period or upon X days advance notice> as approved by the Contracting Officer (CO). The Government anticipates no more than two intermittent project status reviews per month.]

E.8.4 Monthly Project Status Reviews. Monthly status meetings to be conducted on the first Monday of each month. The Contractor is responsible for reporting the previous month's activities (including any risks, issues, or concerns, and actual or recommended actions for their mitigation), and projected activities for the following month.

E.8.5 Program Management Review. The Government will conduct monthly, quarterly, program management reviews at [location], to review the progress of the program, identify any risks, issues, or concerns, and provide feedback on the Contractor's progress and performance. The Contractor shall provide written data and verbal presentations as to the financial status of the <insert name of program> (projected vs. incurred costs), any identified any risks, issues, or concerns (and their mitigation or its plans for their mitigation.]

E.9 REQUIRED TRAVEL and OTHER DIRECT COSTS (ODCs)

E.9.1 Required travel and other costs. [If travel will be required, identify the travel requirements, locations involved, personnel involved (typically by labor category and number), estimated number of trips, and duration of anticipated travel. If the travel will be reimbursed by the Government, discuss the basis for reimbursement, e.g. in accordance with the Federal Travel Regulation. On a fixed price contract where the travel needs are known and well-defined, travel may be built into the contract price and not separately reimbursed. If applicable, state the Government official authorized to approve contractor travel, e.g., the Contracting Officer's Representative (COR).

Sample text, if appropriate: The principal place of performance is <identify location>. Accordingly, reimbursable travel and per diem for the contractor's employees performing work on a regular basis at this place of performance is not authorized. Any changes to this must be approved in advance by the contracting officer.]

E.10 GOVERNMENT FURNISHED PROPERTY/EQUIPMENT/INFORMATION

E.10.1 Government furnished property/equipment/information. [Provide a comprehensive list of all government-

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

furnished property/ equipment/ information to be furnished to the awardee, and when and how it will be furnished, in accordance with the requirements of FAR 45.201. If lengthy, this can be an attachment to the solicitation. At minimum, this includes:

a. The name, part number and description, manufacturer, model number, and National Stock Number (if needed for additional item identification tracking and management, and disposition)
b. Quantity/unit of measure
c. Unit acquisition cost (if applicable)
d. Unique-item identifier or equivalent (if available and necessary for individual item tracking and management)
e. A statement as to whether the property is to be furnished in an "as-is" condition and instructions for physical inspection

FAR 45. 102 policy is that contractors are ordinarily required to furnish all property necessary to perform contracts and government property is provided only under limited circumstances. Consider that if the schedule is contingent on the contractor's timely receipt of any government-furnished items, there is likely to be a one-for-one slip in delivery of the required end-item (a delay for which the contractor cannot be held responsible). Also, the CO is required to verify that the contractor has an approved government property control system.

Some agencies have automated systems for producing such lists and for tracking GFP/GFE/GFI after award (see for example Department of Defense).]

E.11 SPECIAL INSTRUCTIONS

Line Item #	**Description**	**Product or Service Code (PSC)**	**Accounting classification**	**Unit of measure**	**Quantity**	**Unit price (FP)**	**Total price**	**Delivery schedule *OR* Period of performance**	**Destination *OR* Place of performance**	**SOW reference***
001			Typically one, but If multiple accounting classifications for a single deliverable apply, include the dollar amount for each					Due date or frequency		
002		Not required in the line item if there are associated deliverable subline items that include the actual detailed identification								
002-01										

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

002-02			For informational (administrative) subline items, an accounting classification citation is not required							
	Add rows as needed									

E.11.1 Special instructions. [In this section, identify any requirement that is not appropriate to other sections of the SOW that the offeror/awardee needs to be aware of that will have an impact on performance. For example: if this is expected to be a long-term procurement for services over several successive contracts, stipulations concerning the incumbent's obligation to cooperate fully with any successor contractors during transition would be included here. If this is one of the follow-on contracts, include a similar stipulation requiring the successor contractor to cooperate fully with the incumbent.) Other examples include data rights, Section 508 compliance, or FAR 52.237-3—Continuity of Services.]

Line Item #	**Description**	**Product or Service Code (PSC)**	**Accounting classification**	**Unit of measure**	**Quantity**	**Estimated cost**	**Fee (if any)**	**Total estimated cost plus any fee**	**Delivery schedule *OR* Period of performance**	**Destination *OR* Place of performance**	**SOW reference***
001			Typically one, but if multiple accounting classifications for a single deliverable apply, include the dollar amount for each						Due date or frequency		

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

002		Not required in the line item if there are associated deliverable subline items that include the actual detailed identification	For informational (administrative) subline items, an accounting classification citation is not required								
002-01											
002-01											
	Add rows as needed										

E.12 NOTES (OPTIONAL) GLOSSARY OF ABBREVIATIONS AND ACRONYMS

E.12.1 Notes glossary of abbreviations and acronyms. When unique definitions, abbreviations and acronyms are required or would provide value to the SOW include in notes.
[Include a simple two-column table listing all acronyms and abbreviations used in the document, and their meanings. If the list is extensive, this can be an attachment. This glossary is important because different agencies (or even a single agency) may use one acronym or abbreviation to mean very divergent things: is an ATP an "acceptance test procedure"—or an "authorization to proceed"? Is a COE a "common operating environment," a "center of excellence"—or a "certificate of eligibility"? Even if you spell out the acronym or abbreviation at first usage, in a very large document, such definitions can be difficult to locate later. Having a glossary for quick reference will make the meanings of acronyms and abbreviations easier for the contractor to find.]

[A Note About Restrictive Legends:
All government-generated technical documents specific to a given solicitation are sensitive in that any competitor's advance knowledge of their contents could be construed to give that offeror a competitive advantage over the other participants. Therefore, we recommend that until release of a draft or final solicitation, SOWs and all other procurement documents include a footer on every page containing language like the following:

Source Selection Information--See FAR 2.101 and 3.104

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Your agency may have its own preferred restrictive legend. Check with your supervisor, policy department, agency FAR supplement, or the Office of General Counsel.]

E.12.2 TABLE 1: Model for List of Deliverables

E.12.2.1 For fixed-price line items:

Line Item #	Description	Product or Service Code (PSC)	Accounting classification	Unit of measure	Quantity	Unit price (FP)	Total price	Delivery schedule *OR* Period of performance	Destination *OR* Place of performance	SOW reference*
001			Typically one, but If multiple accounting classifications for a single deliverable apply, include the dollar amount for each					Due date or frequency		
002		Not required in the line item if there are associated deliverable subline items that include the actual detailed identification								
002-01										
002-02			For informational (administrative) subline items, an accounting classification citation is not required							

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

	Add rows as needed									

E.12.2.2 For cost-reimbursement line items:

Line Item #	Description	Product or Service Code (PSC)	Accounting classification	Unit of measure	Quantity	Estimated cost	Fee (if any)	Total estimated cost plus any fee	Delivery schedule *OR* Period of performance	Destination *OR* Place of performance	SOW reference*
001			Typically one, but if multiple accounting classifications for a single deliverable apply, include the dollar amount for each						Due date or frequency		
002		Not required in the line item if there are associated deliverable subline items that include the actual detailed identification	For informational (administrative) subline items, an accounting classification citation is not required								
002-01											

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

002-01											
	Add rows as needed										

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

STATEMENT OF OBJECTIVES EXAMPLE

F.1 SCOPE

F.1.1 Scope. This appendix provides a Statement of Objectives example.

F.2 AGILE FORMAT

F.2.1 Agile format. From Defense Acquisition Documents Statement of Objectives Agile Format

F.2.2 Agile example. Request for Quote Overview- Task Order 0001:
The AGENCY intends to award an initial Task Order under the Multiple Award Blanket Purchase Agreement for Sales Force Development Support Services to support the implementation of a Customer Relationship Management System (CRMS) Application utilizing the Sales Force Platform.

Note: All sections of this Request For Quotation (RFQ) will be incorporated into the contract except the Statement of Objectives, Instructions, and Evaluation Factors.

F.2.3 Table of Contents.

Section A. Statement of Objective

Section B. Instructions to Offerors

Section C. Evaluation of Offers

F.3 SECTION A: STATEMENT OF OBJECTIVE

F.3.1 Introduction and Overview.
Insert technical and agency background information specific to the Product.

F4 OBJECTIVE

F.4.1 Objective. The objective of this task order is to utilize the agile development process to establish to develop a Customer Relationship Management (CRM) application for the AGENCY.

PRODUCT VISION: The purpose of the CRM application will be to maintain a centralized view of all interactions and improve the outreach experience to citizens contacting and engaging with the AGENCY through various methods. This new system will replace all critical and major businesses processes supported today by the legacy CRM system and any additional legacy systems.

For this task order, the contractor will utilize their proposed agile software development methodology to implement the CRM system. This methodology defines the repeatable process of providing development and deployment services in small iterations lasting two to five weeks, which generally results in the delivery of usable software, data, or product, which have little to no inherent defects. Each iteration shall be defined in the PWS and should document how planning, requirement analysis (user story building), design, coding, testing, quality assurance, and documentation will all meet the contractor's proposed "Definition of Done."

A Minimum Viable Product (MVP)of this system is expected within the first 6 months under this task

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

order. It is the Agency's desire that the critical components, which are defined as "must haves" in Appendix X, are included to the greatest extent possible in the MVP. Additional major business components are defined as "should haves" and "nice to haves."

F.5 SCOPE

F.5.1 Scope. The scope of this task order falls under Functional Areas 1, 2, 3 & 6 of the Blanket Purchase Agreement (BPA) and includes:

- Initial application design and implementation
- System configuration to support business processes
- Integration for input and output methods
- Workflow design and implementation
- Overall collaboration of applications
- Enhancements, patches, and updates to applications, data, or cloud systems
- Data import of records collected from legacy systems
- Automated testing
- Training of end users on the systems

Scope does not include:

- Workstations, data centers, server systems, and connectivity
- Supporting Legacy applications/systems

F.6 PERIOD AND PLACE OF PERFORMANCE

F.6.1 Period and Place of Performance. The period of performance start date of the acquisition is XX/XX/XXXX

The primary place of performance for this effort will be at government or contractor facilities if designated.

F.7 ORDER TYPE/AWARD TERM OPTION INCENTIVE

F.7.1 Order Type/Award Term Option Incentive. This task order shall be Firm Fixed Price (FFP)/Award Term Option Incentive.

For this task order, the Government will offer two (2) Award Term Options which may encompass future enhancements, releases, development efforts, or operations & maintenance related to the establishment of the Enterprise Collaboration platform or the CRM application. Award Terms may only be awarded for an overall "Excellent" performance rating based on mutually accepted metrics, which will be included in an Award Term Plan to be executed on or around Kick Off. The Government will appoint an Award Term Determining Official (ATDO) who will provide the official performance review and approval for an Award Term Option to be exercised. The ATDO in conjunction with the Contracting Officer will make a unilateral decision as to the exclusion of any portion of the performance period from the evaluation of ratings and calculation of the award term.

Award Term Options are not required to be consecutive with the previous period of performance of the base period or additional options, but may not be exercised longer than 6 months after the final date of the period of performance. Award Term Options can be awarded for no more than one year. They are contingent on continued Government requirements and funding availability for the CRM application. The Award Term Options are un-priced options that will be negotiated and approved from a technical and budgetary standpoint prior to the Contracting Officer awarding the option. Award Term Options must adhere to the proposed Agile methodology and processes as awarded at the BPA level unless an exception is provided by the Contracting Officer prior to award.

Functional Requirements, translated into Epics and User Stories that will be used to populate the Product Backlog may include, but are not limited to:

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

F.8 CONTRACT LINE ITEM NUMBER (CLIN) FORMAT

F.8.1 Contract Line Item Number (CLIN) Format. The Offeror shall submit their proposed CLIN structure in a manner that represents agile software development methodology in which iterations are priced.

BASE PERIOD: 6 months

CLIN 0001, FFP- Completion - The Contractor shall provide services for the Government in accordance with the Performance Work Statement (PWS)

Length of Iteration	_____Weeks
Price Per Iteration	$XXXXX
Period of Performance:	6 months
Firm Fixed Price (Completion):	$XXXXX

The contractor shall be paid upon the completion of each iteration upon its acceptance and verification by the Contracting Officer's Representative (COR). Invoices shall be submitted at the end of each iteration in accordance with the delivery schedule as established in the Performance Work Statement.

F.9 TECHNICAL OVERVIEW

F.9.1 Technical Overview.

a. Technical Environment
The platform will contain Controlled Unclassified Information (CUI) and Personally Identifiable Information (PII). No classified information will be contained in these systems. Federal Information Processing Standard (FIPS) 199 classification is likely High for Availability, Moderate for Integrity, and Low for confidentiality.

b. Stakeholders
For the completion of this task, the AGENCY will provide access to the following stakeholders:

Product Owner: Will manage designated products and communicate with the stakeholder community, are empowered to make business decisions rapidly, set work priorities within designated products, and will remove obstacles to product success. They help write user stories, manage a product's backlog, and work with AGENCY management and partners as customers on a daily basis. Product owners make the final call on functionality and features for their products.

c. Contracting Officer's Representative (COR): Will be responsible for approving end deliverables, managing the Quality Assurance Surveillance Plan (QASP), evaluating performance, and managing schedule according to the submitted Performance Work Statement (PWS)

d. Stakeholders: For this effort the following offices have been designated as Stakeholders for the CRM application:

e. End Users: (provide specific information about End Users of the system-could also provide personas of "typical end users" as part of SOO) The current system supports roughly XXXXXXX end users. The majority of these end users are US Citizens accessing the AGENCY website for correspondence

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

related to XXXXXX. End Users may be used in this effort in usability testing and/or customer satisfaction surveying.

F.10 REQUIRED TASKS

F.10.1 Required Tasks. List the required tasks to be completed. The following are examples of task:

Task 1: Initial Environment System Configuration and Implementation

Objective: Contractor shall provide the AGENCY with a secure, stable, records compliant, commercial collaboration, workflow enabled environment.

i. The contractor shall design the system for maximum interoperability across all AGENCY offices to ensure flexibility in leveraging the system for future applications.

ii. The contractor shall configure the following system instances to support tiered code-release separation and quality assurance and an automatic testing methodology:

iii. The contractor shall seek to configure off-the-shelf aspects of the selected platform before recommending a customized coding approach. The contractor shall develop system configuration in such a manner as to leverage maximum re-use and sharing across the platform. The contractor shall ensure that all changes with impacts to other applications on the platform are minimized. Where such changes are required, they shall be documented and the release coordinated well in advance with the appropriate product owner and development team.

iv. The contractor shall provide incremental documentation through sprint cycles that results in full technical documentation or configuration for all software development efforts and product releases with all information necessary to document processes, procedures, code artifacts, and/or policies that were implemented in the creation of the development work.

v. Once any functionality is released under this call, it shall be the responsibility of the contractor to fix at their own expense any resulting bugs or system defects that are related directly to the contractor's implementation, code, or application design. The fix of these bugs shall not affect other scheduled user stories, deliverables, or releases and shall be at no cost to the government. This requirement for fixing bugs or defects is not considered system maintenance or application enhancements.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

vi. The contractor shall design and implement a user rights, permissions, and security model as notionally described in APPENDIX A -Rights Model Spreadsheet.

vii. The system shall securely transmit all data using Secure Socket's Layer encryption at 128-bit or higher.

viii. The system shall restrict all network traffic to be accessible only from designated networks.

ix. The contractor shall design database entities to comply with the FRA as amended:

x. The contractor shall configure the system such that complete sets of database records (FRA) can be easily exported into separate, discrete export files.

Task 2: CRM Application Design and Implementation

Objective: The contractor shall design and implement basic system features to support traditional CRM functions including the following:

Include listing of the basic features that will initially be included in the MVP. This is not ALL features just the high level overview of the most important or required features of the CRM for the specific end users supported. This can also be included as an attachment and not in the SOO.

Example:
1. One centralized constituent record per citizen with links to all associated vital data and correspondence records
2. Newsletters (bulk e-mail)
3. Reports and dashboards
4. Advanced search
5. External web forms (Contact Us)
6. Internal web forms (Greetings)
7. Rules engines, workflow, analytics, and service-level-agreements
8. Ad-hoc data import and export
9. Document version control, workflow, and library templates/repository

xi. The contractor shall utilize the system support business processes as described in APPENDIX B-Vignettes Slide Deck and APPENDIX C –User Stories as the basis for the CRM application. While it is anticipated the MVP will include these initial features the final User Stories implemented will be prioritized and managed by the Product Owner and/or COR in conjunction with the contractor based upon a mutual agreed upon Product Roadmap and Backlog.

xii. The contractor shall ensure the system is configured to support expansion for additional requirements.

xiii. The contractor shall configure the system in a way to support "Open Source" publishing.

Task 3: Data Import collected from Legacy Systems

Objective: The contractor shall import data collected from legacy systems in a manner that maintains vital record data such as name, address, e-mail address; association data such as group-membership, interests, contact preferences, flags, and affiliations; as well as correspondence items, linkage with constituent record, contact history, and attachments.

xiv. The contractor shall analyze, assist with exports, de-duplicate/scrub, prepare, and import data that has been collected from legacy systems including:

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

- The primary legacy CRM system,
- Provided as a government intermediary MySQL database available to the contractor
- Approximately 40GB of data and 400GB of file attachments

xv. The contractor shall work with the government stakeholder offices during design sessions to identify and separate legacy system data into two sets of relevant data: Operational data records and Historical data records.
- Operational data records are required for critical business processes and shall be prioritized, imported, and available to users at system activation
- Historical data which must be imported to ensure overall data integrity for the stakeholder departments and shall be treated as a lesser priority than operational data but planned for with regard to overall data integrity

xvi. The contractor shall verify in writing to the Government that data migrated from the legacy system to the new system is complete and accurate in accordance with the Federal Records Act and any other applicable federal law, according to the agreed upon framework coordinated with AGENCY and the Contractor and that all data is accessible.

Task 6: Documentation and Training

Objective: The contractor shall provide complete documentation for all systems and applications and provide training that will enable end users to utilize the system.

xvii. The contractor shall provide comprehensive training materials for end users and system administrators for utilization and administration of the system.

- Videos or self-guided training materials may be used
- Training features built into the system are used to the greatest extent possible

xviii. The contractor shall provide initial end-user training on a per-department basis during the initial on-boarding of users to the new system.

xix. The contractor shall provide “train-the-trainer“ classes for selected trainers and administrators.

F.10.2 Operational Constraints

a. Legal Constraints:
i. The system shall store records in a manner compliant with both the Federal Records Act (FRA) of 1950

b. Data Export Constraints:
i. The system shall enable export and transfer of records to the National Archive and Records Administration (NARA) in an agreed upon file format.

c. Operational Constraints:
i. All applications must meet Section 508 Accessibility Requirements

F.10.3 Deliverables. Deliverables under this Task Order are defined as the completion and acceptance according to the “Definition of Done” as proposed for this task order, which are based on the contractor’s agile software development methodology.

Each deliverable shall incorporate AGENCY IT requirements as detailed in the Appendix of this document and the United States Digital Service Playbook standards (https://playbook.cio.gov) and be compliant with Section 508.

F.10.4 Inspection and Acceptance.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

F.10.4.1 Overview. The contractor shall ensure proper control and coordination of all deliverables to ensure they are on time. Unless otherwise stated, the Government will review deliverables and notify the contractor of acceptance or non-acceptance within 5 business days. Representatives of the contractor shall meet with the COR and other members of the Government as necessary to review status of deliverables.

F.10.4.2 Notice Regarding Late Delivery. The Contractor shall notify the COR, or other authorized representative designated in each Task Order, as soon as it becomes apparent to the Contractor that a scheduled delivery will be late. The Contractor shall include in the notification the rationale for late delivery, the expected date for the delivery, and the project impact of the late delivery. Such notification in no way limits any Government contractual rights or remedies, including, but not limited to, termination.

F.10.4.3 Default Acceptance. Notwithstanding the foregoing, any deliverable requiring acceptance by the Government shall be deemed to be accepted by the Government if no written notice of non-conformity has been received by the Contractor within the acceptance period.

F.10.5 SECTION B: INSTRUCTIONS TO OFFERORS

F.10.5.1 Submission of quotes. Quotes shall be submitted by 12:00 noon Eastern Standard Time on Month, Day, and Year.

Quotes shall be submitted to:

Quote submission will consist of two (2) parts: Technical Submission and Price

In addition to price the following factors will be used to determine best value. Technical factors are more important than price:

- Performance Work Statement
- Proposed QASP

F.10.5.2 Section I – Technical submission. The Technical submission shall include the following:

- FACTOR 1 – Performance Work Statement (PWS)
- FACTOR 2 – Notional Quality Control Plan
- Technical Assumptions, Conditions or Exceptions

F.10.5.3 FACTOR 1 – Performance Work Statement. Offerors shall provide a Performance Work Statement (PWS) in response to the Statement of Objectives and this RFQ. The deliverables under this PWS are to have functionality scheduled for an available release without defects.

The PWS shall clearly illustrate the process through which agile development of software in small iterations lasting two to five weeks, which results in the delivery of usable product. The Offeror must propose a "Definition of Done" that will establish the criteria must be met before a "product increment" or User Story is considered done. This will demonstrate the validation necessary to complete an iteration.

The PWS shall describe how user stories are to be sized, how estimation and determination of sizes shall be accomplished, and how these will correlate to iterations and throughput for this task order.

Additionally, the PWS should provide a detailed process for management of the overall task order including working with the Product Manager, COR, and End Users to capture user stories, prioritize, and work-off the product backlog.

The Offeror shall demonstrate in its PWS how the applications, databases, and other products it will produce will meet all requirements for compliance with Section 508 and AGENCY'S IT Security Requirements.

F.10.5.4 FACTOR 2 – Proposed Quality Assurance Surveillance Plan (QASP). Offerors shall propose a

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Quality Assurance Surveillance Plan (QASP) and Performance Measurement approach which is commensurate with the agile software development methodology proposed. This shall include how proposed performance standards will be monitored, evaluated, and reported. The purpose of the notional QASP is to provide evaluators with an understanding of how measures and metrics will be applied based on the proposed technical solution.

F.10.5.4.1 Technical Assumptions, Conditions, or Exceptions. Technical submissions shall include all (if any) assumptions, conditions, or exceptions with any of the requirements or terms and conditions of the Statement of Objectives. If not noted in this section of your quote, it will be assumed that there are no assumptions for award, and that the Contractor agrees to comply with all of the terms and conditions as set forth herein. It is not the responsibility of the Government to seek out and identify assumptions, conditions, or exceptions buried within the submission.

The Government reserves the right to reject any quote that includes any assumption that impacts or affects the Government's requirements.

F.10.5.5 SECTION II – PRICE. The price quote shall include the following:

Offerors shall submit a price quote, which shall include the following:

- Firm Fixed Price per iteration
- Firm Fixed Price by CLIN
- Supporting documentation
- Assumptions, conditions, and exceptions related to price

The Government anticipates that a Firm Fixed Price Task Order will be issued as a result of this solicitation.

F.10.5.5.1 Supporting Documentation. Supporting documentation - The price quote shall provide supporting documentation to support the pricing proposed. This shall demonstrate the correlation between the proposed technical solution in the PWS and the pricing submitted. The supporting documentation shall also include a Basis of Estimate (BOE) which aligns to how the pricing methodology is applied within each iteration. The BOE should include, but is not limited to, such things as:

- Number of Teams proposed
- Size of Agile Teams
- Labor categories, including BPA Pricing, used to comprise Team
- User Story sizing
- Additional discounts applied

F.10.5.5.2 Price Assumptions, Conditions, or Exceptions. Submit all (if any) assumptions, conditions, or exceptions with any of the terms and conditions of this statement of objectives. If not noted in this section of your quote, it will be assumed that the offeror proposes no assumptions for award, and agrees to comply with all of the terms and conditions as set forth herein. It is not the responsibility of the Government to seek out and identify assumptions, conditions, or exceptions buried within the offeror's quote. The Government reserves the right to reject any quote that includes any price assumptions, conditions, or exceptions that impact or affect the Government's objectives or requirements.

F.10.6 SECTION C: EVALUATION OF OFFERS

F.10.6.1 Evaluation and Basis of Award. This task order will be awarded to the SIIS BPA award holder that can provide the services that represent the best value to the Government.

Award will be made to that responsible Offeror whose combination of those factors offering the best overall value to the Government utilizing a tradeoff process. This will be determined by comparing differences in technical capability with differences in price to the Government. In making this comparison, the Government is more concerned with obtaining superior technical merit. However, the Government will not make an

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

award at a significantly higher Price to the Government to achieve slightly superior technical merit. The Government reserves the right to make an award to other than the lowest priced Offeror or to the Offeror with a higher technical score if the Contracting Officer determines that to do so would result in the best value to the Government.

In addition to price, this assessment will be based on the Technical Factors of Factor 1-Performance Work Statement, Factor 2 – QASP

F.10.6.2 FACTOR 1 – Performance Work Statement. The Government will evaluate the feasibility of the proposed PWS to meet the Objectives of the Agency.

F.10.6.3 FACTOR 2 – Quality Assurance Surveillance Plan (QASP) The Government will evaluate whether the proposed performance standards align with the proposed agile development methodology, the rationale behind the proposed performance standards and assess whether the total solution will ensure that the performance standards are met.

F.10.6.4 Technical Assumptions, Conditions, or Exceptions. All assumptions shall be evaluated as part of the individual factor or sub factor to which they apply. The Government reserves the right to reject any quote that includes any assumption(s) that impact satisfying the Government's requirements.

F.10.7 SECTION II – PRICE

F.10.7.1 Price. Price will be evaluated to determine whether the firm, fixed price proposed is reasonable. This determination will be based on the review of the technical solution in comparison to the total proposed price and the backup documentation submitted. Pricing for this effort is required to be of a unit of measure that is equivalent to the proposed iteration cycle as proposed in the Performance Work Statement. The technical solution for sizing, iteration time, and throughput must correlate to the proposed pricing.

F.10.7.1.1 Price Assumptions, Conditions, or Exceptions. Submit all (if any) assumptions, conditions, or exceptions with any of the terms and conditions of this statement of work. If not noted in this section of your quote, it will be assumed that the offeror proposes no assumptions for award, and agrees to comply with all of the terms and conditions as set forth herein. It is not the responsibility of the Government to seek out and identify assumptions, conditions, or exceptions buried within the offeror's quote. The Government reserves the right to reject any quote that includes any price assumptions, conditions, or exceptions that impact or affect the Government's objectives or requirements.

F.10.8 APPENDIX TO REQUEST FOR QUOTE

F.10.8.1 Appendix.

APPENDIX A: Notional CRM Rights Model Spreadsheet
APPENDIX B: Vignettes Slide Deck
APPENDIX C: Enterprise Collaboration and User Stories –Final

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Instance Name	Description and Purpose
Development	Description: The Development instance(s) will exist as the primary development site for integrators to fix bugs, develop new features, and test unit functionality to ensure items are ready for update to Staging. These instances will be accessed typically only by administrators and developers. Purpose: To provide isolated system instance(s) for active development and/or Unit Testing. User-base: Integrator development team and infrequently the Integrated Project Team as required. Availability: The Development instance(s) shall not be bound to any Service Level Agreement and may be subject to maintenance and upkeep on an as-needed basis. Feature Set: The Development instance(s) shall run the code version required for active development. Data: The Development instance(s) shall dummy data such that it is rendered non-sensitive and non-specific for the purposes of development.
Staging	Description: The Staging instance shall be a system for formal User Acceptance Testing and Training as well as collaboration with the Integrated Project Team and agency user community. Purpose: To separate User Acceptance Testing and Training activities from Unit Testing or Production activities. User-base: Integrator development team, the Integrated Project Team, and designated users for testing and training as required. Availability: The Staging instance shall be generally available to Integrated Project Team members during working hours (7:30am – 7:30pm) and at the integrator's discretion for maintenance and upkeep. Feature Set: The Staging instance shall run the most current version of the production code. It may be updated with Unit Test or new release code until being fully replaced with the current code after the next production release. Data: The Staging instance shall include masked, truncated, or redacted agency data such that it is rendered non-sensitive for the purposes of testing and training.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Production	Description: The Production instance shall be a system supporting the work of active Production instance users. Purpose: To separate development and testing activities from actual government business processes and records. User-base: The integrator's development team, the Integrated Project Team, and the Production user community. Availability: The Production instance shall be available for user access in accordance with the service level agreement for the platform. Feature Set: The Production instance shall run the current version of the production code feature set after a release to production. The Production and Recovery instances must run the same code version at all times. Data: The Production instance shall include live, SBU agency data and only be modified by authorized users within their assigned security roles. The data set active on the Production instance should be complete, comply with both Federal Records Act (FRA) requirements, be backed up in accordance with the platform disaster recovery plan, and be able to be properly exported for transfer to National Archives and Records Administration (NARA) at the appropriate times.
Recovery	Description: The Recovery instance shall be an entirely separate, hot fail-over system to support the work of the Production instance users in the event of an outage or inaccessible Production instance. Purpose: To provide continuity of operations for critical business processes as well as recovery and preservation of production data in the event of a catastrophic outage with the Production instance. User-base: The integrator's development team, the Integrated Project Team, and the Production user community. Availability: The Recovery instance shall be available for user access in accordance with the service level agreement for the platform. Feature Set: The Recovery instance shall run the current version of the production code feature set after a release to production. The Production and Recovery instances must run the same code version at all times. Data: The Recovery instance shall include live, CUI agency data and only be modified by authorized users within their assigned security roles. The data set active on the Recovery instance should be complete, comply with both Federal Records Act requirements, be backed up in accordance with the platform disaster recovery plan, and be able to be properly exported for transfer to NARA at the appropriate times.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

QUALITY ASSURANCE SURVEILLANCE PLAN EXAMPLE

G.1 SCOPE

G.1.1 Scope. This appendix provides an example Quality Assurance Surveillance Plan (QASP).

G.2 FORMAT

G.2.1 Format of title page. The following is an example of the QASP title page.

Quality Assurance Surveillance Plan (QASP)
Version – <enter date or version #>

For <enter contract title>
Contract Number: < upon award, enter contract number>
Contract Description: < enter contract description >
Contractor's Name: < upon award, enter name of contractor > (hereafter referred to as the contractor).

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

G.3 VISION

G.3.1 Vision. Vision (import from Acquisition Requirements Roadmap Tool (ARRT) or Charter)

G.4 MISSION

G.4.1 Mission. Mission (import from ARRT or Charter)

G.5 PURPOSE

G.5.1 Purpose. This QASP is a government-developed document used to determine if the contractor's performance meets the performance standards contained in the contract. The QASP establishes procedures on how this assessment/inspection process will be conducted. It provides the detailed process for a continuous oversight process:

- What will be monitored
- How monitoring will take place
- Who will conduct the monitoring
- How monitoring efforts and results will be documented

The contractor is responsible for implementing and delivering performance that meets contract standards using its Quality Control Plan. The QASP provides the structure for the government's surveillance of the contractor's performance and their Quality Assurance/Quality Control (QA/QC) actions to assure they meet contract standards. It is the government's responsibility to be objective, fair and consistent in evaluating contractor performance.

The QASP is not part of the contract nor is it intended to duplicate the contractor's quality control plan. This QASP is a living document. Flexibility in the QASP is required to allow for an increase or decrease in the level of surveillance necessary based on contractor performance.

The government may provide a copy of the QASP to the contractor to facilitate open communication. In addition, the QASP should recognize that unforeseen or uncontrollable circumstances might occur that are outside the control of the contractor.

Bottom line, the QASP should ensure early identification and resolution of performance issues to minimize impact on mission performance.

G.6 AUTHORITY

G.6.1 Authority. Authority for issuance of this QASP is provided under Part 46 of the Federal Acquisition Regulation, Inspection of Services clauses, which provides for inspection, acceptance and documentation of the service called for in the contract or order. This acceptance is to be executed by the contracting officer or a duly authorized representative.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

G.7 ROLES AND RESPONSIBILITIES

G.7.1 Roles and Responsibilities. The following personnel shall oversee and coordinate surveillance activities.

G.7.1.1 Program/Project Manager (PM) or Functional Services Manager (FSM). The PM/FSM provides primary program oversight, nominates the COR, ensures the COR is trained before performing any COR duties and supports the COR's performance assessment activities. While the PM/FSM may serve as a direct conduit to provide Government guidance and feedback to the Contractor on technical matters, they are not empowered to make any contractual commitments or any contract changes on the government's behalf.

Assigned PM/FSM: <enter name>
Organization or Agency: <enter organization or Agency name>
Telephone: <enter number>
Email: <enter address>

G.7.1.2 Contracting Officer (KO). The KO shall ensure performance of all necessary actions for effective contracting, ensure compliance with the contract terms, and shall safeguard the interests of the United States in the contractual relationship. The KO shall also ensure that the contractor receives impartial, fair, and equitable treatment under this contract. Determine the final assessment of the contractor's performance.

Assigned KO: <enter name>
Organization or Agency: <enter organization or Agency name>
Telephone: <enter number>
Email: <enter address>

G.7.1.3 Contracting Officer's Representative (COR). The COR is responsible for providing continuous technical oversight of the contractor's performance. The COR uses the QASP to conduct the oversight/surveillance process. The COR shall keep a Quality Assurance file that accurately documents the contractor's actual performance. The purpose is to ensure that the contractor meets the performance standards contained in the contract. The COR is responsible for reporting early identification of performance problems to the KO. The COR is required to provide an annual performance assessment to the KO which will be used in documenting past performance. The QASP is the primary tool for surveillance of the contractor's quality program and help the COR to document contractor performance. The COR is not empowered to make any contractual commitments or to authorize any contractual change on the Government's behalf.

G.7.1.4 Other Key Government Personnel. (enter name or delete this line if not applicable). This may include performance monitors, inspectors, technical experts, or others who provide information that helps the COR monitor contractor performance.

G.7.1.5 Contractor Representatives. The following employees of the contractor serve as the contractor's Program Manager and Task Manager for this contract. (Complete this section after the contract award)

G.7.1.6 Contractor Program Manager - <upon award, enter name> Telephone: <enter number> Email: <enter address>

G.7.1.7 Contractor Task Manager - <upon award, enter name> Telephone: <enter number> Email: <enter address>

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

G.7.1.8 Other Key Contractor Personnel - <upon award, enter name or delete these lines if not applicable> Title: <enter title> Telephone: <enter number> Email: <enter address>

G.8 PERFORMANCE REQUIREMENTS AND METHOD SURVEILLANCE

G.8.1 Contract Surveillance. The goal of the QASP is to ensure that contractor performance is effectively monitored and documented. The COR's contribution is their professional, non-adversarial relationships with the KO, PM and the contractor, which enables positive, open and timely communications. The foundation of this relationship is built upon objective, fair, and consistent COR evaluations of contractor performance against contract requirements. The COR uses the methods contained in this QASP to ensure the contractor is in compliance with contract requirements. The COR function is responsible for a wide range of surveillance requirements that effectively measure and evaluate the contractor's performance. Additionally, this QASP is based on the premise that the contractor, not the government, is responsible for management and QC/QA actions to successfully meet the terms of the contract.

G.8.2 Surveillance Matrix. The Surveillance Matrix (see sample at Attachment 1) is the list of performance objectives and standards that must be performed by the contractor. This matrix details the method of surveillance and frequency the COR will use to validate and inspect these performance elements. Inspection of each element will be documented in the COR file.

DFARS 222.17 mandates including surveillance for ensuring compliance with Combatting Trafficking in Persons (CTIP) in the QASP. Use the CTIP sample checklist from PGI 222.17. See the DoD CTIP website.

Performance objectives define the desired outcomes. Performance Standards define the level of service required under the contract to successfully meet the performance objective. The inspection methodology defines how, when, and what will be assessed in measuring performance. The Government performs surveillance, using this QASP, to determine the quality of the contractor's performance as it relates to the performance element standards. The Performance Requirement Summary (PRS) should be used to form the foundation of the COR's inspection checklist.

G.8.3 Performance Rating Definitions. The performance ratings below reflect definitions at FAR 42.1503 Table 42-1. The COR will use these rating to evaluate the quality of contractor's performance. *[If your organization requires that you use a different rating mechanism, insert it here.]*

Performance Rating	Definition
Exceptional	Performance meets contractual requirements and exceeds many to the government's benefit. The contractual performance of the element or sub-element being evaluated was accomplished with few minor problems for which corrective actions taken by the contractor were highly effective.
Very Good	Performance meets contractual requirements and exceeds some to the Government's benefit. The contractual performance of the element or sub-element being evaluated was accomplished with some minor problems for which corrective actions taken by the contractor were effective.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Satisfactory	Performance meets contractual requirements. The contractual performance of the element or sub-element contains some minor problems for which corrective actions taken by the contractor appear or were satisfactory.
Marginal	Performance does not meet some contractual requirements. The contractual performance of the element or sub-element being evaluated reflects a serious problem for which the contractor has not yet identified corrective actions. The contractor's proposed actions appear only marginally effective or were not fully implemented.
Unsatisfactory	Performance does not meet most contractual requirements and recovery is not likely in a timely manner. The contractual performance of the element or sub-element contains a serious problem(s) for which the contractor's corrective actions appear or were ineffective.

Note 1: Plus or minus signs may be used to indicate an improving (+) or worsening (-) trend insufficient to change the evaluation status.

Note 2: N/A (not applicable) should be used if the ratings are not going to be applied to a particular area for evaluation.

G.9 PERFORMANCE REPORTING

G.9.1 Corrective Action Report (CAR). Describes how discrepancies are reported and resolved (see sample CAR below).

G.9.2 Customer Complaint Form. (See sample customer complaint form below)

G.9.3 Performance Assessment Report (PAR) (See sample customer PAR below)

G.9.3.1 Surveillance Matrix

Statements	**Standards/AQLs**	**Inspections**	**Ratings**
Maintain and repair elevators for XYZ Organization.			
The Contractor shall inspect, maintain, and test elevators for passenger and cargo elevator systems. Deliverables: A01 Reports	**a)** Standard commercial practice for the specific elevator system, consistent with technical manuals. **b)** Downtime for required schedule maintenance is met **AQL:** 99.2% of the time	**What:** Elevators Documents **How:** 100% review of documents Continuous observation Customer feedback trouble reports **Who:** Users, Technical engineers, and COR **Incentive:** $100 deduct for out of compliance documentation $50 deduct for failure to perform preventive maintenance on schedule **Standard(s): Incentive** applies to	

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

		standard (a) only	
The Contractor shall conduct preventive maintenance for elevator systems.	**a)** Preventive maintenance performed IAW the manufacturer's manual 100% of the time **b)** Meets all warranty requirements	**What:** Preventive Maintenance Records Log Books Inspection Deficiency Write-up resolutions **How:** Records and Visual Inspection On-site periodic inspections **Who:** Mechanical Staff Engineer **Incentive:** $100 deduct for each PM procedure not performed IAW manufacturer manuals **Standard(s):** Inspection applies to all standards	
The Contractor shall assure parts availability for continuous operation. Deliverables: A02 Parts Inventory List	**a)** Sufficient parts are available to support the required Ao and the mandated parts list **AQL:** Ao is maintained Mandated Parts List is complete 98.8% of the time	**What:** Parts Inventories Availability Records **How:** Records and Visual Inspection On-site periodic inspections **Frequency:** After completion of each inventory **Who:** COR for Ao Mechanics Staff for parts **Standard(s):** Inspection applies to all standards	

G.9.4 Inspection Methodologies:

G.9.4.1 M1: Inspection of Reports. All reports shall be reviewed upon receipt. The reviewer will report any flaws in the document and categorize the flaws (Editorial, Format, and/or Substance).

G.9.4.1.1 Corrective Action Report.

CORRECTIVE ACTION REPORT (CAR) ***(If more space is needed, use reverse and identify by number)***			
1. CONTRACTOR	2. CONTRACT NUMBER	3. TYPE OF SERVICES	
4. FUNCTIONAL AREA		5. SUSPENSE DATE	6. CONTROL NUMBER

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

7. DEFICIENCY ☐ MAJOR ☐ MINOR FINDING: FINDING IMPACT: *Please respond with a written corrective action plan that details the corrective action of the cited deficiency, the cause of the deficiency, and actions taken to prevent recurrence by Suspense Date in Block 5. If date was not entered in Block 5, the contractor is not required to provide a response.*	
8. QUALITY ASSURANCE PERSONNEL (COR)	
TYPED NAME AND GRADE	SIGNATURE AND DATE
9. ISSUING AUTHORITY	
TYPED NAME AND GRADE	SIGNATURE AND DATE
10. COR RESPONSE TO CONTRACTOR CORRECTIVE ACTION AND ACTION TAKEN TO PREVENT RECURRENCE	
11. COR DETERMINATION ☐ ACCEPTED ☐ REJECTED	12. CLOSE DATE

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

G.9.4.1.2 Customer Complaint Record.

CUSTOMER COMPLAINT RECORD			DATE/TIME OF COMPLAINT
SOURCE OF COMPLAINT			
ORGANIZATION	BUILDING NUMBER	INDIVIDUAL	PHONE NUMBER
NATURE OF COMPLAINT			
CONTRACT REFERENCE			
VALIDATION			
DATE/TIME CONTRACTOR INFORMED OF COMPLAINT			
ACTION TAKEN BY CONTRACTOR			
RECEIVED/VALIDATED BY			

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

G.9.4.1.3 COR Corrective Action and Prevention Record.

1. CONTRACT/TASK ORDER NUMBER	2. CONTRACTOR	3. TYPE OF SERVICES	
4. QUALITY ASSURANCE PERSONNEL (COR) SIGNATURE AND DATE		**5. COR PHONE**	**6. SUSPENSE DATE**
I. PERFORMANCE			
7. ☐ DEFICIENCY (CHECK ALL BOXES THAT APPLY) ☐ NEW ☐ REPEAT ☐ NO DEFICIENCY NOTED	8. SERVICES SUMMARY or PWS PARAGRAPH ITEM REVIEWED		
9. BRIEF DESCRIPTION OF DEFICIENCY (IF DEFICIENCY BOX WAS CHECKED)	10. DETAILED PERFORMANCE ASSESSMENT		
II. CONTRACTOR VALIDATION			
11. CONTRACTOR REPRESENTATIVE ☐ CONCUR ☐ NON-CONCUR	12. CORRECTIVE ACTION ESTIMATED COMPLETION DATE		
13. CONTRACTOR REPRESENTATIVE CORRECTIVE ACTION AND PREVENTION OF RECURRENCE OR REASON FOR NON-CONCURRENCE OF COR CITED DEFICIENCY			
III. ACTION CORRECTED			
14. ☐ CONCUR ☐ NON-CONCUR COR SIGNATURE AND DATE			
15. COR REMARKS (REQUIRED)			
6. CONTRACTOR REPRESENTATIVE REMARKS			

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

PERFORMANCE WORK STATEMENT (PWS) EXAMPLE

H.1 SCOPE

H.1.1. Scope. This appendix provides an example of a Performance Work Statement (PWS).

H.2 VISION STATEMENT

H.2.1 Vision Statement. The Clark River is the safest river to navigate. This is a hypothetical sample of creating a PWS, QASP, and Performance Requirements Summary (PRS).

H3 INTRODUCTION

H.3.1 Introduction. Type your introduction here

H.3.2 Mission. The Clark River has not been dredged for over 10 years. There have been numerous safety issues where large personal watercraft had been grounded due to insufficient depth and inaccurate channel marking. These hazards on the river greatly impact the safe usage of the river. These conditions have great potential for reducing the desirability of the river as a tourism destination.
By making the river safe and navigable, the Clark River Authority (CRA) will be able to deliver to its citizens and visitors an ultimate vacation destination.

H.3.3 Background. Put your background information here

H.3.4 Scope. The intent of this acquisition is to upgrade the Clark River into a reliable waterway for personal watercraft. The Clark River project consists of 42 miles of waterway from Point Look-out to Point Look-in. There are 6 drawbridges and 2 swing bridges with one ferry (6 car capacity) for crossing the river.
This contract is to establish and maintain the river to facilitate the recreational use of its citizens in a safe and reliable manner for a period of 5 years.
There are approximately 16 tributary areas that flow into the river that can impact the channel.

H.4 GENERAL REQUIREMENTS

H.4.1 General Requirements. This section describes the general requirements for this effort. The following sub-sections provide details of various considerations on this effort

H.4.2 Non-Personal Services. The Government shall neither supervise contractor employees nor control the method by which the contractor performs the required tasks. Under no circumstances shall the Government assign tasks to, or prepare work schedules for, individual contractor employees. It shall be the responsibility of the contractor to manage its employees and to guard against any actions that are of the nature of personal services, or give the perception of personal services. If the contractor believes that any actions constitute, or are perceived to constitute personal services, it shall be the contractor's responsibility to notify the Procuring Contracting Officer (PCO) immediately.

H.4.3 Business Relations. The contractor shall successfully integrate and coordinate all activity needed to execute the requirement. The contractor shall manage the timeliness, completeness, and quality of problem identification. The contractor shall provide corrective action plans, proposal submittals, timely identification of issues, and effective management of subcontractors. The contractor shall seek to ensure customer satisfaction and professional and ethical behavior of all contractor personnel.

H.4.4 Contract Administration and Management. The following subsections specify requirements for contract, management, and personnel administration.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

H.4.4.1 Contract Management. The contractor shall establish clear organizational lines of authority and responsibility to ensure effective management of the resources assigned to the requirement. The contractor must maintain continuity between the support operations at [insert location] and the contractor's corporate offices.

H.4.4.2 Contract Administration. The contractor shall establish processes and assign appropriate resources to effectively administer the requirement. The contractor shall respond to Government requests for contractual actions in a timely fashion. The contractor shall have a single point of contact between the Government and Contractor personnel assigned to support contracts or task orders. The contractor shall assign work effort and maintaining proper and accurate time keeping records of personnel assigned to work on the requirement.

H.4.4.3 Personnel Administration. The contractor shall provide the following management and support as required. The contractor shall provide for employees during designated Government non-workdays or other periods where Government offices are closed due to weather or security conditions. The contractor shall maintain the currency of their employees by providing initial and refresher training as required to meet the PWS requirements. The contractor shall make necessary travel arrangements for employees. The contractor shall provide necessary infrastructure to support contract tasks [tailor this for on-site and off-site support]. The contractor shall provide administrative support to employees in a timely fashion (time keeping, leave processing, pay, emergency needs).

H.4.5 Subcontract Management. The contractor shall be responsible for any subcontract management necessary to integrate work performed on this requirement and shall be responsible and accountable for subcontractor performance on this requirement. The prime contractor will manage work distribution to ensure there are no Organizational Conflict of Interest (OCI) considerations. Contractors may add subcontractors to their team after notification to the Procuring Contracting Officer (PCO) or Contracting Officer Representative (COR). Cross teaming may or may not be permitted.

H.4.6 Contractor Personnel, Disciplines, and Specialties. The contractor shall accomplish the assigned work by employing and utilizing qualified personnel with appropriate combinations of education, training, and experience. The contractor shall match personnel skills to the work or task with a minimum of under/over employment of resources. The contractor shall ensure the labor categories as defined in the Labor Categories document (see attachment), labor rates, and man-hours utilized in the performance of each Task Order (PWS line item) issued hereunder will be the minimum necessary to accomplish the task [*consider application based on contract type and whether or not pre-established rates exist*].

The Contractor shall provide the necessary resources and infrastructure to manage, perform, and administer the contract.

H.4.7 Location and Hours of Work. Accomplishment of the results contained in this PWS requires work at [*specify location*] and at various contractor, subcontractor, and Government facilities (mainly in the continental United States). Normal workdays are Monday through Friday except US Federal Holidays. Workers typically work eight (8) hours per day, 40 hours per week. Flextime workers start not earlier than 0600 and not later than 0900. Core hours of work are from 0900 to 1500 daily. All employees are expected to be available during core hours. [*Tailor to reflect contract type and approach.*] [*NOTE: Address weather or security closures and how they will be handled. Any surge requirements need to be addressed. If you have shown surge hours in your historical representation, you need to identify the reason for the surge. (e.g. fiscal year-end, short-term situations may make performance in excess of 8 hours per day, 40 hours per week necessary on occasion, contractor must ensure that they can provide for this type of contingency).*]

H.4.8 Travel / Temporary Duty (TDY). Travel to other government facilities or other contractor facilities may be required and will be specified in the PWS. All travel requirements (including plans, agenda, itinerary, or dates) shall be pre-approved by the government (subject to local policy & procedures), and is on a strictly cost reimbursable basis. Costs for travel shall be billed in accordance with the regulatory implementation of Public Law 99-234 and FAR 31.205-46 Travel Costs (subject to local policy & procedures; may reference FAR).

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

H.5 PERFORMANCE REQUIREMENTS

H.5.1 Performance Requirements. The following section specifies the Performance Objectives and Performance Elements for the contract.

H.5.2 Make the river navigable. There are two main factors in keeping navigability: depth and width.

H.5.2.1 The contractor shall establish and maintain depth of channel for Clark River. The depth of the river is important to accommodate any size boat passing through.

Performance Standards

Standard (STD): 12 feet deep, mean low water

Acceptable Quality Limit (AQL): Any location less than 12 feet deep cannot exceed 4 linear feet perpendicular to the channel. No more than 4 occurrences of this per mile.

STD: 12 feet deep, mean low water
AQL: No points with depth less than 11 feet
Deliverables
A004 Monthly Status Report

H.5.2.2 The contractor shall collect, manage, and dispose of dredged materials for Clark River.

Performance Standards
STD: Any non-compliant incidents shall be immediately remediated.
AQL: Remediation begins within 24 hours 100% of the time.
STD: Compliant with federal, state, EPA, and local laws and regulations
AQL: 100%
Deliverables
A001 Quality Control Plan for Dredged Material
A002 Monthly Dredged Materials Report

H.5.2.3 The contractor shall establish and maintain width of channel for Clark River. A wide channel is important in order to accommodate a high volume of boats.

Performance Standards
STD: 100 feet wide
AQL: No points less than 80 feet
STD: 100 feet wide
AQL: 90% of channel >= 100 ft
STD: 100 feet wide
AQL: Any bottlenecks in river (less than 100 feet shore to shore) shall have the channel within 10 feet of each shore line.
Deliverables
A002 Monthly Dredged Materials Report
A003 Project Plan
A004 Monthly Status Report

H.5.3 Identify the navigation channel. It is critical that the channel be properly marked.

H.5.3.1 The contractor shall maintain channel markers for Clark River.

Performance Standards
STD: Displaced markers / buoys replaced within 24 hours of detection
AQL: Additional time allowed for unsafe weather conditions
STD: Identifying information (color, numbers, letters, shape, etc.) must be clearly visible
AQL: All color discernible at 1/4 mile. 95% of all lettering/numbering legible at 200 yards
Deliverables
A004 Monthly Status Report

H.5.3.2 The contractor shall mark channel for Clark River. Proper channel marking is important for

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

safety.

Performance Standards
STD: Compliant with USCG Navigation rules
AQL: 100%
STD: Execute on a variety of platforms [Specify]
AQL: Execute on a variety of platforms [Specify]
STD: Visible
AQL: Visible within 1/4 mile during normal weather conditions
STD: Within 10 feet of channel edge
AQL: None greater than 15 feet, 90% of all buoys are within the standard
Deliverables
A004 Monthly Status Report

H.5.4 Update the navigation charts

H.5.4.1 The contractor shall update current navigation charts for Clark River.

H.6 SPECIAL REQUIREMENTS

H.6.1 Special Requirements. This section describes the special requirements for this effort. The following sub-sections provide details of various considerations on this effort.

H.6.2 Security and Safety. DD Forms 254: Overarching security requirements and Contractor access to classified information shall be as specified in the basic DD Form 254, which will be further identified in the DD Form 254 for each TO, as required. All contractor personnel with access to unclassified information systems, including e-mail, shall have at a minimum a favorable National Agency Check (NAC). Visitor Group Security Agreement. The contractor shall sign a Contractor Visitor Group Security Agreement to protect classified information involved in performance under this contract or Task Order. The Agreement will outline responsibilities in the following areas: Contractor security supervision; Standard Practice Procedures; access, accountability, storage, and transmission of classified material; marking requirements; security education; personnel security clearances; reports; security checks; security guidance; emergency protection; protection of government resources; DD Forms 254; periodic security reviews; and other responsibilities, as required.

H.6.3 Transition. The contractor shall follow the transition plan submitted as part of the proposal and keep the Government fully informed of status throughout the transition period. Throughout the phase-in/phase-out periods, it is essential that attention be given to minimize interruptions or delays to work in progress that would impact the mission. The contractor must plan for the transfer of work control, delineating the method for processing and assigning tasks during the phase-in/phase-out periods. [*Include as monitored item in monthly status report (or other deliverable) if this paragraph is applicable.*]

H.6.4 Government Furnished Materials**.** The Government will make available the materials, office space, communications capability and information (TAILOR AS NECESSARY) on the dates specified as identified in Attachment XX for use by the contractor in the performance of this contract.

H.6.5 Environmental Requirements. The contractor shall comply with all documents listed below as mandatory and referenced under paragraph 3.0, Performance Requirements. Compliance with documents listed as non-mandatory is the contractors' option.
Mandatory compliance (list)
Non Mandatory document (list)

H.6.6 Applicable Directives. The contractor shall comply with all documents listed below as mandatory and referenced under paragraph 3.0, Performance Requirements. Compliance with documents listed as non-mandatory is the contractors' option.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

Mandatory compliance (list)
Non-Mandatory document (list)

H.7 DELIVERABLES

H.7.1 Deliverables. The contractor shall provide deliverables as described in subsequent task orders. Deliverables shall be specified by the government. Format and delivery schedule for deliverables shall be outlined in CDRLs and/or other means TBD.

Identifier	Name	Description
A001	Quality Control Plan for Dredged Material	Document describing what will be done with the Dredged Material
A002	Monthly Dredged Materials Report	To be delivered by the 5th of each month
A003	Project Plan	
A004	Monthly Status Report	To be delivered by the 5th of each month.

H.8 RELATED DOCUMENTS

H.8.1 Related Documents. The following Documents are related to this project:
Environmental Regulations for Handling and Disposing of Dredged Materials

Identifier	Name	Description

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

A001	Quality Control Plan for Dredged Material	Document describing what will be done with the Dredged Material
A002	Monthly Dredged Materials Report	To be delivered by the 5th of each month
A003	Project Plan	
A004	Monthly Status Report	To be delivered by the 5th of each month.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.

CONCLUDING MATERIAL

Custodians:
Army – CR
Navy – EC
Air Force – 10

Review activities:
Army – AT
Navy – SH, AS, MC, YD
Air Force – 11, 13

Preparing activity:
Navy – EC
(Project: MISC-2018-004)

NOTE: The activities listed above were interested in this document as of the date of this document. Since organizations and responsibilities can change, you should verify the currency of the information above using the ASSIST Online database at https://assist.dla.mil.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T13:39Z
Check the source to verify that this is the current version before use.
