DATA ITEM DESCRIPTION

Form Approved
OMB No. 0704-0188

Public reporting burden for this collection of information is estimated to average 110 hours per response, including the time for reviewing instructions, searching existing data source, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington, VA 22202-4302, and to the Office of Management and Budget, Paperwork Reduction Project (0704-0811), Washington, DC 20503.

1. TITLE	2. IDENTIFICATION NUMBER
PRODUCTION PROGRESS CONFERENCE (PPC) AGENDA	DI-MGMT- 81252

3. DESCRIPTION/PURPOSE

3.1 This agenda provides scheduling and progress data and related information to be discussed during the scheduled Production Progress Conference (PPC). It identifies events, milestones, and schedules in the construction sequence using planned, revised and actual dates and provides the status of contractual deliverables, correspondence, changes and problem areas.

4. APPROVAL DATE (YYMMDD)	5. OFFICE OF PRIMARY RESPONSIBILITY (OPR)	6a. DTIC APPLICABLE	6b. GIDEP APPLICABLE
920302	NAVSEA PMS300		

7. APPLICATION/INTERRELATIONSHIP

7.1 This Data Item Description (DID) contains the format and content preparation instructions for the data product generated by the specific and discrete task requirement as delineated in the contract.

7.2 This DID supercedes UDI-A-26241B.

8. APPROVAL LIMITATION	9a. APPLICABLE FORMS	9b. AMSC NUMBER
		N6711

10. PREPARATION INSTRUCTIONS

10.1 General. The Agenda shall be in Contractor format. The outline herein is a guide intended to indicate the details of the format and content desired. The emphasis and depth of data and analysis shall be appropriate to the phase of the contract effort. When problem areas are identified, additional information to clearly explain the nature/status of the problem shall be included.

10.2 Schedule Of Key Events. The schedule shall show the flow of construction progress from beginning to end. Events are to be identified as a completed action during the construction phase; such as: a work package (system installation) or a test (system test).

10.2.1 The schedules shall be presented in matrix form with events in the left hand column. The percent of labor required to complete that item and the cumulative percent of labor shall be shown in the next two columns. The remaining columns are to have each event line item divided into two (2) lines. The upper line shall contain the original estimated completion date and the lower line shall contain the current estimated or actual completion date for each boat/craft under contract.

10.2.2 The fourth column from the left shall be identified as "Completion Dates". The subdivided event lines for each event shall be "original estimate" and the lower line "estimated/actual".

Continued on Page 2

. DISTRIBUTION STATEMENT A: Approved for public release; distribution is unlimited.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

10.2.3 Column five and all following columns shall be identified at the top by Navy assigned craft hull number (e.g. 9101, 9102, etc.). Original estimated dates for all events shall be provided. As actual events occur or as schedules are revised, the lower block current "estimate" or "actual" dates for each event, and for each hull as applicable, shall be revised. Estimated completion dates shall be followed with an "E" (e.g. 10/15/91E) while actual completion dates shall be followed by an "A" (e.g. 10/15/91A).

10.2.4 OPTION I The key events listed in table I shall be used for fiberglass hulls.

TABLE I. Key events for Fiberglass hulls

1.	Lofting
2.	Plugs and Molds
2.1	Hull Plug Fabrication
2.2	Hull Mold Fabrication
2.3	Deck Plug Fabrication
2.4	Deck Mold Fabrication
2.5	Miscellaneous Mold Fabrication
2.6	Miscellaneous Mold Fabrication
2.7	Pre-production Test Panel
3.	Production
3.1	Issue Construction Drawings
3.2	Contractor's Design Weight Estimate
3.3	Buoyancy Foam Qualification Tests
3.4	Hull Lamination
3.5	Laminate and Install Bulkheads and Hull Structural Members
3.6	Laminate Cure Test
3.7	Remove Hull From Mold
3.8	Laminate Properties and Core Bond Tests
3.9	Quality Control Weighing
3.10	Deck Lamination
3.11	Laminate Test
3.12	Seats and Miscellaneous Laminates
4.	Assembly
4.1	Install Flats
4.2	Install Seats
4.3	Install Deck
4.4	Install Miscellaneous Fiberglass Items
4.5	Foam Boat
4.6	Flotation Test

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

TABLE I. Key events for Fiberglass Hulls - Continued

5. Systems Installation 5.1 Propulsion System 5.2 Steering System 5.3 Fuel System 5.4 Bilge System 5.5 Electrical/Navigation System 5.6 Mooring and Anchoring Equipment 5.7 Communication System
6. Outfitting 6.1 Lifting Fittings 6.2 Sheer Guard Installation 6.3 Rails, Stanchions and Lifelines 6.4 Doors and Accesses 6.5 Covers, Curtains and Berthing 6.6 Painting, Coating and Deck Coverings 6.7 Acoustical Treatment 6.8 Lockers and Stowages
7. Testing and Trials 7.1 Pre-Trial Testing 7.2 Scale Weighing 7.3 Builder's Trials 7.4 Propeller Trials 7.5 Acceptance Trials 7.6 Correct Trial Deficiencies
8. Final Delivery 8.1 Covers 8.2 Prepare for Shipment 8.3 Ship from Contractor's Facility 8.4 Receipt at Destination

10.2.5 OPTION II The key events listed in Table II shall be used for metal hulls.

TABLE II. Key events for Metal Hulls.

1. Engineering 1.1 Issue Construction Drawings 1.2 Contractor's Design Weight Estimate
2. Hull Construction 2.1 Welder Certification 2.2 Welding Process Qualifications 2.3 Lofting 2.4 Set Up Jig

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

TABLE II Key events for Metal Hull - Continued

2.5 Erect Frames 2.6 Plate Hull 2.7 Hull Weld Radiography 2.8 Roll-over 2.9 Install Pilot House
3. Systems Installation 3.1 Propulsion System 3.2 Steering System 3.3 Piping Systems 3.4 Electrical Systems 3.5 Communications Systems
4. Outfitting 4.1 Sheer Guard & Fenders 4.2 Platforms & Flats 4.3 Deck Coverings, Berthing 4.4 Doors and Hatches 4.5 Joiner Work 4.6 Insulation and Sheathing 4.7 Painting 4.8 Rails, Stanchions, and Lifelines
5. Testing and Trials 5.1 System Tests 5.2 Tightness Tests 5.3 Scale Weighing 5.4 Inclining Experiment (first craft only) 5.5 Builder's Trials 5.6 Propeller Trials (first craft only) 5.7 Acceptance Trials 5.8 Correct Trials Discrepancies
6. Final Delivery 6.1 Prepare for Shipment 6.2 Ship Craft from Contractor's Facility 6.3 Receipt at Destination

10.3 Material Ordering Schedule. The material ordering schedule shall contain the information for materials with a delivery lead time of sixty (60) days or more and all high cost items which make up at least 75% of the material cost for construction of each boat/craft. The schedule shall be presented in matrix form with columns addressing the following:

a. Item Description
b. Purchase Order Number
c. Vendor
d. Lead Time
e. Scheduled Order Date
f. Actual Order Date
g. Required Delivery Date
h. Actual Delivery Date

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

i. Quantity of Craft Sets Received

10.4 Drawing Schedule. Drawings required by the contract shall be listed in matrix form with the following information for each drawing:

a. Drawing Item Number (e.g. 1, 2, 3, ...)
b. NAVSEA Drawing Number (last ten digits)
c. Contractor Drawing Number (if applicable)
d. Contractor and Government Entity (CAGE) Code
e. Drawing Title
f. Latest Revision
g. Required Submission Date
h. Date Submitted
i. Validation Dates
j. Latest Revision Dates

10.4.1 A status on drawings with a narrative on the following shall be provided:

a. Number of drawings submitted during last reporting period.
b. Total submitted to date.
c. Rationale for late submissions with a planned completion date and a statement of impact these late drawings may have on the construction schedule.
d. Number of drawings planned for next reporting period.

10.5 Installation And Start-Up Items. The Installation and Start-up Items required shall be listed and the status of each item shall be provided:

a. Item Nomenclature and Part Numbers
b. Scheduled Order Date
c. Actual Order Date
d. Lead Time
e. Date Received
f. Quantity Required
g. Quantity Received

10.6 Labor Progress. Labor progress shall be displayed graphically, similar to the format shown in Figure 1. The number at the bottom of the chart shall indicate the number of months from contract award date. The heading in each column at the top of the chart shall represent each calendar month starting with the month of award.

10.6.1 The estimated labor progress curve is plotted using data for the original estimated completion dates as shown on the schedule of key events.

10.6.2 Actual labor progress is plotted from the actual completion dates as shown on the schedule of key events.

10.6.3 Labor progress needed to meet the contract delivery dates is plotted for a comparison of the actual progress against the required progress needed to meet

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

contract schedules.

10.7 Total Progress. Physical progress shall be projected by using the schedule of key events. Material progress shall be reported as specified in the contract. A matrix that summarizes the total labor and total material progress shall be provided. The matrix shall identify each craft, the percent of labor and material complete for each craft and the percentage of contract completion each craft represents.

10.8 Change Orders. A matrix showing the status of Non Engineering Change Proposals (NECPs), Engineering Change Proposal (ECP), Value Engineering Change Proposals (VECP), Waivers and Deviation shall contain the following information for each change:

a. Change Number (e.g. ECP001)
b. Subject
c. Submission Date
d. Requested Response Date
e. Adjudication Date
f. Contract Modification Number (e.g. A00001)
g. Cost
h. Hull Applicability
i. Remarks

10.9 Test and Trial Schedule. All tests and trials required by the contract shall be listed in matrix format with the following information for each test or trial:

a. Title
b. Specification Section
c. Scheduled Date for each hull
d. Actual Date for each hull

10.10 Contract Data Status And Schedule (CDSS). The CDSS shall be in two separate sections. Each section shall include a heading consisting of: Identification of System/Item; Contract number; Prime Contractor; and date.

10.10.1 Section I. CDRL items with a one time submission (with or without revision), CDRL items with periodic submission (e.g. MTHLY) or CDRL items to be submitted as required shall be reported in Section I as follows:

a. Exhibit Line Item Number (ELIN) (e.g. A001)
b. Description/Title
c. Required Submission Date
d. Actual Submission Date
e. Revision Number and Date
f. Government Approval Required
g. Government Approval Date

10.10.2 Section II. Each CDRL item which requires a submission for each craft or for selected craft shall be reported in

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

Section II as follows:

a. ELIN
b. Description/Title
c. Scheduled Test Date (for testing only) (3rd column)
d. Actual Test Date (for testing only) (3rd column)
e. Required Submission Date (3rd column)
f. Actual Submission Date (3rd column)
g. The remaining columns, after the third, shall report the dates for each craft starting with first hull (e.g. 9101).

10.11 Quality Deficiency Reports (QDR). A matrix that identifies all QDRs issued since contract award shall contain the following information:

a. QDR Issue Date
b. Subject Matter
c. Current Status
d. Estimated Completion Date
e. Acutal Completion Date

10.12 Government-Furnished Material (Schedule A). For each schedule A item, show item description, required delivery date, actual delivery date and status of each item.

10.13 Government-Furnished Information (Schedule C). For each schedule C item, show item description, required delivery date, actual delivery date and status of each item.

10.14 Problems (Technical And Non-Technical). All problems to be discussed at the PPC shall be identified. The following information shall be listed: problem description; background information; and recommendations for resolution.

10.15 Correspondence. List all unanswered correspondence by Serial No., date, subject, if critical and why, who has action, and required response date.

10.16 Summary. Provide summary comments on overall progress; specifically, a discussion of all problems which will disrupt or otherwise adversely affect the orderly construction of the program including, but not limited to the items contained in the agenda, i.e., schedules, manpower, design, and material Contractor Furnished Matherial (CFM) or Government Furnished Material (GFM). Identify required Government action that is currently adversely affecting craft construction, the latest date by which the action can be taken, and the impact on construction schedules if not taken by that date. Identify the action items generated during the PPC.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.

Block 10. Preparation Instructions (Continued)

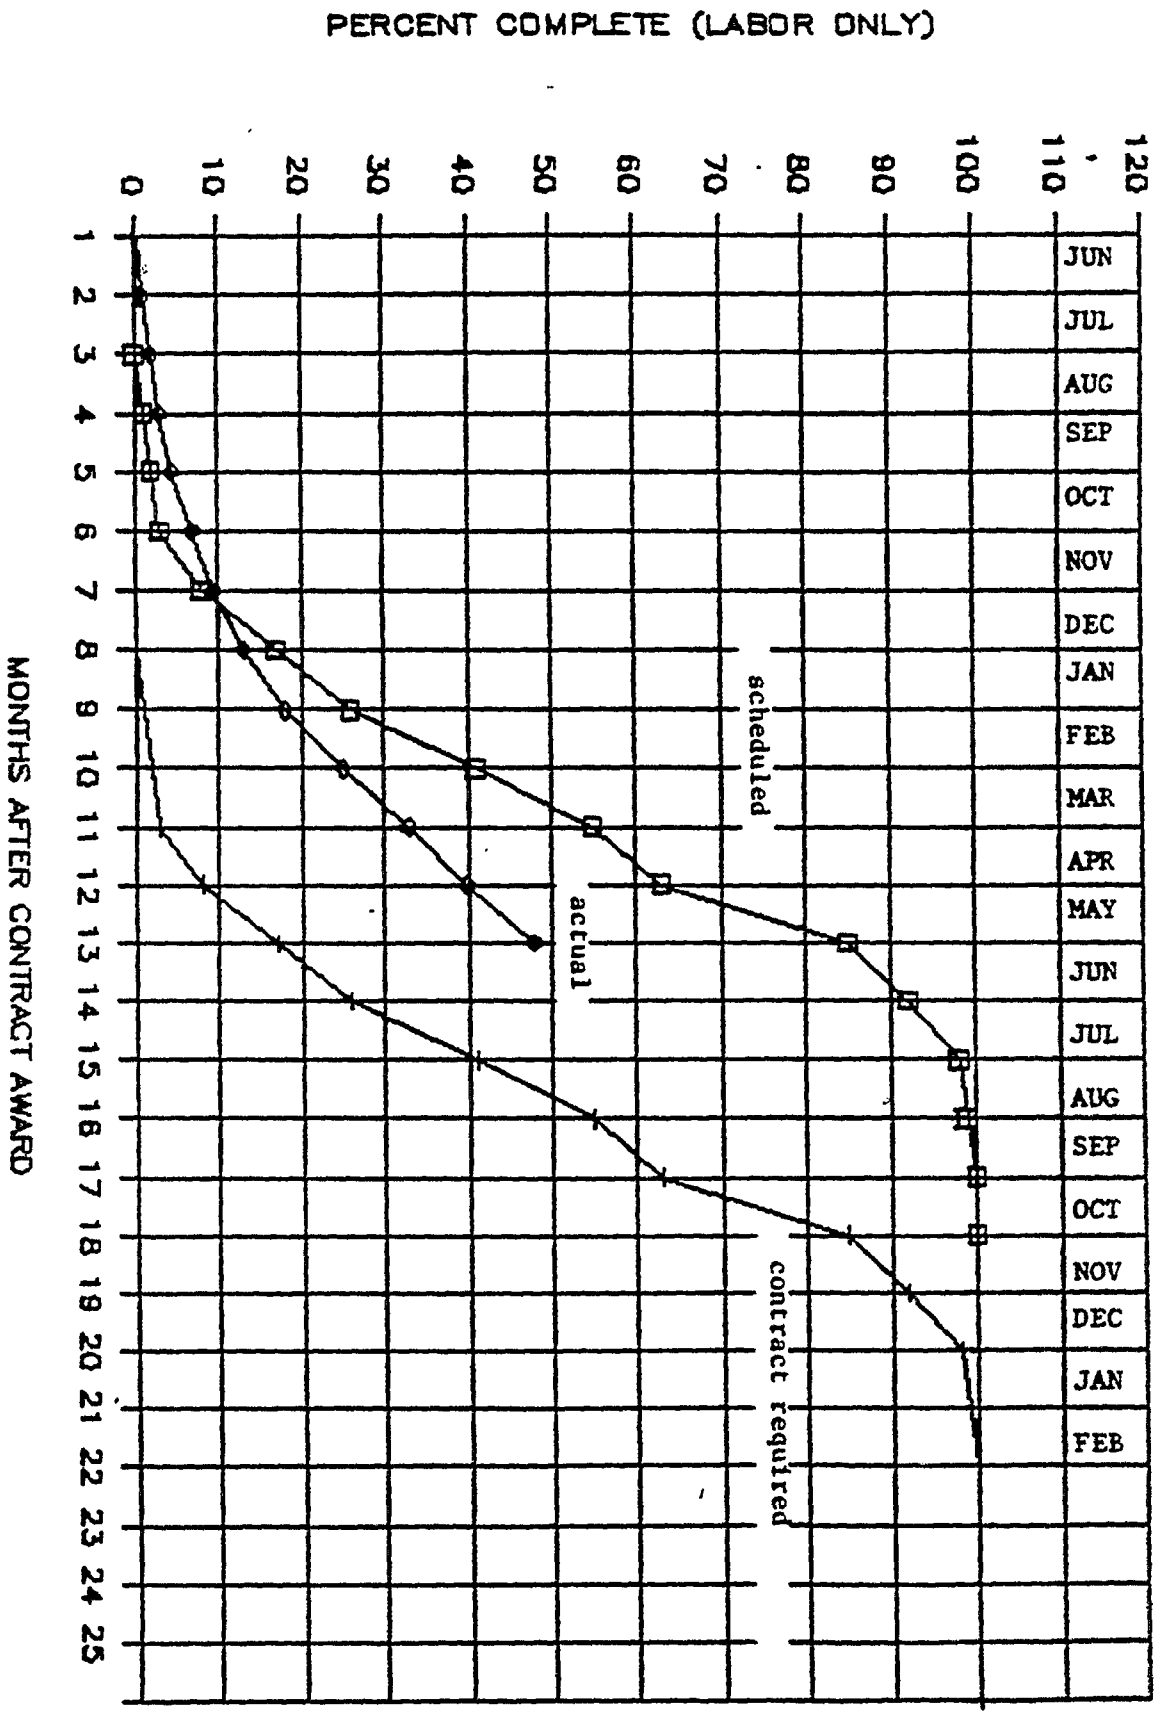


Figure 1

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:45Z
Check the source to verify that this is the current version before use.
