MILITARY SPECIFICATION

PROVISIONING MONITORING SYSTEM PROCEDURES FOR NAVAL SHIPBOARD ELECTRICAL AND MECHANICAL EQUIPMENT AND COMPONENTS

1. SCOPE

1.1 General.- This specification covers requirements designed to insure the timely completion and flow of provisioning technical documentation (PTD) for all provisionable shipboard mechanical and electrical equipments and components.

1.2 Specific.- This specification delineates the responsibilities of both industry and the Navy in the fulfillment of the requirements indicated; provides guidelines for establishing key action milestones; prescribes procedures for monitoring the completion and flow of all required provisioning technical documentation; encompasses instructions and procedures for the development and dissemination of schedules and reports and; provides instructions with regard to the use of the schedules and reports for implementing this specification and taking necessary corrective action.

1.3 Applicability.- This specification applies to all private and Navy shipbuilder furnished mechanical and electrical equipment required by:

(a) New construction contracts - Those contracts which specify that the delivery date of the ship, or first ship of multiple identical ship contracts, will be at least 24 months after the date of the contract.
(b) Conversion or overhaul contracts.- Those contracts which specify that the delivery/completion date of the ship, or first ship of multiple identical ship contracts, will be at least 12 months after the date of the contract.

2. APPLICABLE DOCUMENTS

2.1 The following documents of the issue in effect on date of invitation for bids or request for proposal, form a part of the specification to the extent specified herein.

SPECIFICATION

MILITARY
MIL-P-15137 - Provisioning Technical Documentation for Repair Parts, for Electrical and Mechanical Equipment (Naval Shipboard Use).

(Copies of specifications, standards, drawings, and publications required by suppliers in connection with specific procurement functions should be obtained from the procuring activity or as directed by the contracting officer.)

3. REQUIREMENTS

3.1 Responsibility.-

3.1.1 Shipbuilder.- The shipbuilder, referenced throughout this specification, is that activity engaged to build, convert or overhaul U. S. Naval ships and ships in the Military Assistance Program. The shipbuilder shall:

(a) Prepare a Provisioning Technical Documentation Submission Schedule (PTDSS) (see 3.3 and 20.1 of Appendix A).
(b) Provide facilities and attend a pre-provisioning conference which will be called and chaired by the supervising activity.
(c) Present the PTDSS to the pre-provisioning conference attendees for examination and acceptance by the supervising activity.
(d) Prepare and distribute the "Listing and Status of Provisionable Items Report (LSPIR)" (NAVSHIP REPORT 4423-1) (see figure 3) in accordance with 3.4 and section 30 of Appendix A.
(e) Take appropriate action to insure that the scheduled progress of the shipbuilder which is indicated in the LSPIR is met and, when directed by the supervising activity, take the necessary action to improve the progress of events which are behind schedule.

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.

3.1.2 Supervising activity.- The supervising activity, referenced throughout this specification, is the assigned contract administration office for contracts awarded to private shipbuilders. For ships constructed, converted and overhauled in Naval shipyards, the Naval shipyard is the supervising activity. The supervising activity will:

(a) Call and chair the pre-provisioning conference within 60 days after contract award or amendment, whichever is appropriate.
(b) Examine the PTDSS for conformance with requirements of 20.1 of Appendix A and approve the schedule, subject to necessary modifications, if any (see 3.1.1, 3.3 and 20.1 of Appendix A).
(c) Prepare and distribute the minutes of the pre-provisioning conference within 15 days after conference termination date.
(d) Review and monitor the LSPIR and direct the shipbuilder to take corrective action, as required (see 4.1).
(e) Prepare a Summary Status Report (NAVSHIPS Report 4423-3 figure 1) (see 3.5 and section
(f) Provide guidance to the shipbuilder and where necessary, request engineering or technical assistance from NAVSEC MECHDIV relative to provisionable items determination (see 6.1.3 and 10.1 of Appendix A).

3.1.3 Navy Ships Parts Control Center (SPCC) will:

(a) Attend the pre-provisioning conference (see 3.2).
(b) Examine the PTDSS and recommend necessary modifications, if any (see 20.1 of Appendix A).
(c) Screen the LSPIR and interface with the supervising activity for resolving conflicts between the LSPIR and the SPCC's records.
(d) Provide the shipbuilder, upon request of the supervising activity, with a sister ship COSAL (Part I) or a COSAL (Part I) for a similar type ship, for use as a guide in listing provisionable items as units, to be reported upon the PTDSS and LSPIR.
(e) Report to the supervising activity, using one copy of Part II of the LSPIR, the reason for each SPCC delinquent provisioning action. NOTE: Delinquent actions are defined as those SPCC provisioning events which, according to MIL-P-15137, shall take place within 60 days after receipt of complete PTD.

3.1.4 Naval Ship Engineering Center, Mechanicsburg Division (NAVSEC MECHDIV) will:

(a) Attend the pre-provisioning conference (see 3.2).
(b) Examine the PTDSS and recommend necessary modifications, if any (see 3.1.3, 3.3 and 20.1 of Appendix A).
(c) Review the Summary Status Reports (NAVSHIPS Report 4423-3) (figure 1) and exercise mission authority and responsibility for resolving problems of the nature requiring attention by NAVSEC and provide technical guidance as required.

3.1.5 Navy shipbuilding scheduling office.- The Navy shipbuilding scheduling office will provide scheduling assistance required by the shipbuilder, when requested via the supervising activity, to permit development of an acceptable schedule of provisioning progress.

3.2 Pre-provisioning conference.- The supervising activity will schedule, convene, and chair the pre-provisioning conference. The purpose of the pre-provisioning conference is to thoroughly indoctrinate the participants and thereby, ensure prompt and effective implementation of the Provisioning Monitoring System. The supervising activity will convene the conference within 60 days after the date of contract award or amendment and on a date that is mutually agreeable to the principal attendees. The conference will be held at the shipbuilder's site or at a location acceptable to the supervising activity.

3.2.1 Attendees.- Representatives of the shipbuilder, supervising activity, Naval Systems Command, Naval Ship Engineering Center, Mechanicsburg Division, Navy Ships Parts Control Center, and the Navy Shipbuilding Scheduling Office (when invited by the supervising activity) will attend the initial pre-provisioning conference. Attendees at subsequent pre-provisioning conference, if required, will be determined by the supervising activity.

3.2.2 Indoctrination.- Indoctrination will include, but not limited to, the following:

(a) A presentation on the objectives of the provisioning monitoring system and the responsibilities of each participant as set forth herein.

Source: https://assist.dla.mil -- Downloaded: 202640-19T21:19Z
Check the source to verify that this is the current version before use.

(b) Purpose of the LSPIR and development thereof, with emphasis on the need for completing all required actions prior to delivery of the ship(s).
(c) Review of MIL-P-15137 requirements as they relate to this specification.
(d) Coordination ground rules between the shipbuilder and the supervising activity and between the supervising activity and other Government activities.

NOTE: Excluding routine provisioning actions or events required by MIL-P-15137, all other communications, actions or events shall be coordinated with the supervising activity.

3.3 Provisioning Technical Documentation Submission Schedule (PTDSS).- This schedule, to be prepared by the shipbuilder and presented to the supervising activity at the pre-provisioning conference, shall conform to the requirements outlined in Appendix A (see 3.1.1 (a) and (c)).

3.4 Listing and Status of Provisionable Items Report (LSPIR).- This report, to be prepared by the shipbuilder (see 3.1.1.(d) and section 30 of Appendix A) shall be identified as NAVSHIPS Report 4423-1 (figure 4) and it will consist of two parts, namely; Part I, which shall list all provisionable mechanical and electrical equipments to be furnished under the contract or order and Part II, which shall list all Part I equipments for which the required provisioning action by SPCC and the shipbuilder is delinquent. Each list shall be in sequence of contract or order number and item number sequence within each contract or order. Delinquency shall be determined as indicated below and the number of delinquent items for both SPCC and the shipbuilder shall be totaled separately on the last page of Part II of this report:

(a) SPCC.- No entry in column 9B and the date of the LSPIR is more than 45 days subsequent to the date shown in column 8B.
(b) Shipbuilder.- No entry in column 8B and the date of the LSPIR is subsequent to the date shown in column 8A.

3.4.1 Multiple ship reporting.- With the approval of the supervising activity, the shipbuilder may prepare a single report for multiple ships provided that the following conditions are met:

(a) The shipyard is provisioning multiples of a class of ships on a concurrent or overlapping schedule.
(b) The majority of equipments to be furnished are exactly the same for each ship of the class.
(c) Separate LSPIRs, properly identified to effect accurate reporting, are prepared and submitted for those provisionable items which are not common to all hulls.
(d) The shipbuilder includes the first hull member of the series in the basic LSPIR with all other applicable hull numbers listed in the cover sheet or cover letter of the report.

3.4.3 Frequency of submission.- The initial LSPIR shall be submitted on the date determined at the pre-provisioning conference. Thereafter, the LSPIR shall be submitted once every month on the fifteenth day of the month, and will continue to be submitted until all SPCC and shipbuilder PTD actions have been completed.

3.4.3 Distribution.- The shipbuilder shall distribute the LSPIR as follows:

Activity	Number of copies
Supervising Activity (Contract Administration Office assigned in the contract)	Part I - 3 copies Part II - 1 copy
Commanding Officer Navy Ships Parts Control Center (Code 782) Mechanicsburg, Pa. 17055	Part I - 3 copies EAM cards- 1 deck Part II - 3 copies

3.5 Summary status report (NAVSHIPS Report 4423-3) (figure 1).- This report will be prepared by the supervising activity in accordance with the instructions and sample format (see figure 1) and in Appendix A (see section 40). The report will summarize the provisioning actions reflected in the LSPIR of the date on which the report is based.

3.5.1 Frequency of submission.- The Summary Status Report will be submitted within five days after receipt of each LSPIR from the shipbuilder.

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.

3.5.2 Distribution of the summary status report.- The supervising activity will distribute the Summary Status Report to the following activities:

	Number of copies
Officer in Charge Naval Ship Engineering Center Mechanicsburg Division (6832) Mechanicsburg, Pa. 17055	1 original
Commander, Naval Ship Systems Command (PMS_____) Washington, D. C. 20360	1 copy
Commanding Officer Navy Ships Parts Control Center (Code 702) Mechancisburg, Pa. 17055	1 copy
Commander, Philadelphia Naval Shipyard (Navy Shipbuilding Scheduling Office) Naval Base Philadelphia, Pa. 19112	1 copy

4. QUALITY ASSURANCE PROVISIONS

4.1 Report review.- Each "Listing and Status of Provisionable Items Report" will be reviewed by the supervising activity and the adequacy of the report as well as the progress achieved in relation to the LSPIR submitted for the previous month will be evaluated. The supervising activity will direct the shipbuilder to improve upon the adequacy of the report and the progressing of the shipbuilder responsible for the provisioning events, as appropriate and as necessary.

4.2 Corrective action.- The supervising activity's directions for corrective action by the shipbuilder will be in sufficient detail to insure desired results. Delinquent provisioning events will require individual examination to determined cause of delay and, when appropriate, the LSPIR will be adjusted by direction of the supervising activity to indicate new provisioning event dates commensurate with the findings of the examination. A copy of the corrective action directions to the shipbuilder will be attached to the Summary Status Report. A report on the results of the corrective action directions will accompany the Summary Status Report for the following month or months, as appropriate.

5. PREPARATION FOR DELIVERY

5.1 This section is not applicable to this specification.

6. NOTES

6.1 Definitions.-

6.1.1 Non-Provisionable items.- Shipboard equipments or components which do not meet the criteria established in the Applicability paragraph of MIL-P-15137.

6.1.2 Provisionable items.- Shipboard equipments and components which meet the criteria established in the Applicability paragraph of MIL-P-15137 (see 10.1 of Appendix A).

6.1.3 Provisioning.- The process of determining the range and depth of items (i.e., spares and repair parts, special tools, test equipment, and support equipment) required to support and maintain an end item of material.

6.1.4 Provisioning technical documentation.- That data required of an equipment contractor or shipbuilder, as specified in MIL-P-15137, to accomplish provisioning and related functions.

6.1.5 Pseudo Procurement Order No..- The number assigned by the shipbuilder and listed in the LSPIR when no formal Procurement Order Number exists. All such pseudo numbers shall be structured in the same manner as formal procurement order numbers.

6.2 Abbreviations.- The following abbreviations are commonly used in this specification:

(a) ADP - Automatic Data Processing
(b) COSAL - Coordinated Shipboard Allowance List
(c) EAM - Electric Accounting Machine
(d) EDD - Estimated Delivery Date of Ship

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.

(e) LSPIR - Listing and Status of Provisionable Items Report (NAVSHIPS Report 4423-1) (see figure 4)
(f) PTD - Provisioning Technical Documentation
(g) PTDSS - Provisioning Technical Documentation Submission Schedule
(h) SPCC - Navy Ships Parts Control Center, Mechanicsburg, Pa.

Preparing activity:
Navy - SH
(Project MISC-N491)

Source: https://assist.dla.mil -- Downloaded: 20260-19T21:19Z
Check the source to verify that this is the current version before use.

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.

APPENDIX A

PROVISIONING MONITORING SYSTEM PROCEDURES

10. PROVISIONABLE ITEM BREAKDOWN

10.1 Determination criteria.- For the purpose of preparing the PTDSS and LSPIR, provisionable items shall be broken down into units and accounted for accordingly. A unit is a component which performs an independent function, requires repair parts support and can be replaced individually. For example, each component comprising a pump assembly is a unit, e.g., the motor, and the controller are separate units and are to be counted as such in the preparation of the PTDSS and reported upon in the LSPIR as separate line items.

NOTE: When doubt exists as to whether or not an item is provisionable (see 6.1.3), the supervising activity will provide the guidance upon request.

10.1.1 Provisioning Documentation Requirement Guide (see figure 2).- This guide indicates responsibility for development of the PTD under various situations, when pseudo order numbers are to be used vice purchase order numbers and signifies PTDSS and LSPIR reportable items.

20. SCHEDULES

20.1 Provisioning Technical Documentation Submission Schedule (PTDSS).- The sample format (see figure 3) is based on an estimated total of 2200 provisionable item units. See section 10 for determining what constitutes a provisionable item unit.

20.1.1 Source documents.- Source documents which may be consulted for determining the number of shipbuilder furnished equipments/components are, but not limited to, the following:

(a) Ships plans and detailed specifications
(b) Material ordering guide
(c) Material ordering schedule
(d) Master erection schedule
(e) Allowance list for a sister ship or similar type ship (see section 10)
(f) Shipbuilder's group list, where applicable

20.1.2 Action milestones.- The action milestones of this schedule are designed to achieve a flow of PTD submission that will permit the timely preparation of the ship's allowance list and procurement of required repair parts.

20.1.3 Frequency of submission.- The initial PTDSS shall be presented to the supervising activity at the first pre-provisioning conference (Sec 5.1.1 (c)). The PTDSS need not be resubmitted unless changes are directed at the pre-provisioning conference and thereafter, only when circumstances necessitate a 5 percent change in the PTD schedule to be submitted by that specific milestone and which will prevail for a period of more than two months.

20.1.4 Achievement goals.- Figure 3 indicates that 95 percent of all shipbuilder required PTD shall be submitted at (EDD - 150) days and 98 percent at (EDD - 120) days. The remaining 2 percent shall be submitted as early as possible and in no instance, later than (EDD-0) days. These goals may vary slightly from ship to ship. All such variations will be made known at the initial pre-provisioning conference and the PTDSS will be adjusted accordingly during this meeting.

30. LSPIR PREPARATION INSTRUCTIONS

30.1 Preparation.- The shipbuilder shall prepare the LSPIR by EAM or ADP methods. Manually prepared reports are not acceptable. The format and data content of the report shall be as prescribed herein and on figure 4.

30.1.1 Responsiveness.- The shipbuilder shall make maximum effort to eliminate time-lag between dates of compiled information and publication of LSPIR. The shipbuilder's LSPIR transmittal letter will advise recipients of the final date for incorporating information received prior to printing LSPIR.

Source: https://assist.dla.mil -- Downloaded: 202640-19T21:19Z
Check the source to verify that this is the current version before use.

30.2 Data content.- Each unit of data to be reported in the LSPIR has been assigned a column number (see figure 4). Digital LAN field limitations are also prescribed. These requirements will not be changed without the explicit written approval of the supervising activity. All dates required by the LSPIR are to be recorded as Julian dates. The reporting of data required by all columns of the LSPIR, except for columns 10 and 15, is mandatory. The determination as to whether or not columns 10 and 15 will be used for the purpose indicated rests with the supervising activity. This decision will be made known at the initial pre-provisioning conference. Columns 12 and 13 are to be left blank.

30.3 Detailed instructions.-

30.3.1 Column 1 - Transaction code - (1 digit field) .- In order to relate the transaction as applying to either the first or second LAN card, the Shipbuilder shall post the transaction codes as follows:

Transaction Codes Card No. 1	Card No. 2	Transaction
"1"	"2"	When a provisionable item is recorded on the LSPIR for the first time.
"3"	"4"	When any change is made to the data in columns 10 through 18, excluding 16, of the previous report.
"5"	"6"	When a provisionable item is deleted. The deleted code remains on all subsequent issues, however, the transaction code "5" or "6" should be transferred to colum 16.

30.3.2 Other columns.- Other columns shall be posted as follows:

(a) Column 2 - Hull number - (5 digit field).- Enter ship account number. In multiple hull applications, list account number of first hull to which entry applies, identify other hulls in cover letter or on front page of print-out (see 3.4.1).

(b) Column 3 - Procurement order- (20 digit field).- Enter the number which identifies the procurement action as it appears on Purchase Order/Contract, including dashes, spaces, and characters. Shipbuilder manufactured items or Sub-Stock items (those held by the shipbuilder in his reserve stock) are to be assigned a pseudo procurement number.

(c) Column 4 - Item number - (4 digit field).- Enter the item number of each provisionable item as it appears on the procurement order. When the item procured is an equipment which consist of more than one provisionable item or unit, each of the additional units is to be assigned a sub-item number. The sub-item number assigned shall be the same as that which is recorded on the provisioning document. The first two spaces of this field will be used for item number control and the last two spaces will be used for sub-item number control. If any item number of a contract/procurement order for the ship contract will ever exceed two digits, then all of the item numbers will be entered in column 3, and column 4 will be restricted to sub-item numbers. Specifics concerning this requirement will be agreed upon during the initial preprovisioning conference (see 3.2).

(d) Column 5 - Nomenclature - (18 digit field).- Enter nomenclature in brief to describe item cited in column 4. (Use Federal Item Identification Guide). If nomenclatures for two or more sub-items for any one piece of equipment are identical, furnish distinguishing information in column 15.

(e) Column 6 - Date of procurement order - (4 digit field).- Enter date procurement order was issued.

(f) Column 7 - PTD required from the vendor to shipbuilder - (4-4 digit field).- (A and B) Enter in column 7A the date PTD is scheduled to arrive from the vendor, based upon the material required date in column 14. When PTD is received, enter the receipt date in column 7B.

(g) Column 8 - PTD submitted to SPCC - (4-4 digit field).- (A and B) Enter in column 8A the date PTD is scheduled to be submitted to SPCC, based upon the material required date in column 14. Enter the actual date of submission in column 8B. Revise actual date of submission (Column 8B), as required, to show submission of corrected or revised PTD.

(h) Column 9 - Provisioning from SPCC - (4-4 digit field).- (A and B) Enter in column 9A the date in column 8B plus 45 days. Enter the date PTD is

Source: https://assist.dla.mil -- Downloaded: 202610-19T21:19Z
Check the source to verify that this is the current version before use.

MIL-P-24310(SHIPS)

(i) Column 10 - Quantity - (4 digit field).- (A and B) This is an optional entry as determined by the supervising activity. Enter quantity of each item procured.
(j) Column 11 - Provisioning control number - (12 digit field).- Enter the Provisioning Control Number.
(k) Column 12 - Blank - (11 digit field).- Reserved for U. S. Navy use.
(l) Column 13 - Blank - (6 digit field).- Reserved for U. S. Navy use.
(m) Column 14 - Date required - (4 digit field).- Enter date provisionable item is scheduled for delivery to the shipbuilder.
(n) Column 15 - Supplemental information - (14 digit field).- Enter date such as drawing number, piece number, valve mark number, or other distinguishing information as required by (d).
(o) Column 16 -Delete code storage - (1 digit field).- Enter delete code from column 1 for storage as indicated in instructions for column 1.
(p) Column 17 - Hull application commonality code - (1 digit field)
(q) Column 18 - Remarks code - (1 digit field).- Enter a single letter code designation devised to report recurring situations which should be reported as a remarks comment. Key to this code shall be developed by the shipbuilder and submitted with each report.

30.4 EAM cards.- The shipbuilder shall prepare and submit to SPCC an initial set of key-punched and interpreted EAM cards duplicating the data contained in the basic LSPIP report. Subsequently with each follow-on report, the shipbuilder shall prepare and submit to SPCC key-punched and interpreted EAM cards for only those items added, changed or deleted from the previous LSPIR.

NOTE: Magnetic tape or other ADP machineable products may be prepared and submitted to SPCC. If the shipbuilder desires to provide a machineable input other than EAM cards, SPCC should be advised via the supervising activity so that appropriate procedures may be developed. SPCC will use these EAM cards for in- house processing.

30.4.1 Format.- The EAM cards shall be submitted in the following format:

EAM Card Number 1 Card column(s)	Data
1	Transaction Code
2-6	Ship/Hull Account Number
7-26	Procurement Order
27-30	Procurement Order Item No.
31-48	Nomenclature
49-52	Date PO Issued
53-64	Prov. Form Cont. No.
65-68	Date Comp/Equip req'd
69-72	Date PTD req'd from Vendor to Shipbuilder Scheduled
73-76	Date PTD Req'd from Vendor to Shipbuildre received
77-80	Date PTD submitted ICP Scheduled

EAM Card Number 2 Card column(s)	Data
1	Transaction Code
2-6	Ship/Hull Account Number
7-26	Procurement Order
27-30	Procurement Order Item No.
31-34	Date PTD Submitted to ICP Actual
35-38	Completed Provisioning from ICP Scheduled
39-42	Completed Provisioning from ICP Actual
43-48	Blank
49	Delete Code Shift
50	Hull Application Commonality Code
51	Remarks-Code
52-62	Blank
63-76	Installation Information
77-80	Quantity

Source: https://assist.dla.mil -- Downloaded: 202640-19T21:19Z
Check the source to verify that this is the current version before use.

30.5 Time frames.-

30.5.1 Controls.- MIL-P-15137 and the date the material is scheduled for delivery to the shipbuilder establishes the time frames necessary for determining the dates required by columns 7, 8A and 9A for all provisionable items, in general. Late procurements may necessitate deviating from these time frames and the establishment of more realistic dates to expedite processing of the PTD. In each such instance, which shall be kept to a minimum, the supervising activity will make the frame adjustment.

40. DETAILED INSTRUCTION FOR PREPARATION OF THE SUMMARY STATUS REPORT

40.1 Preparation.- The supervising activity will prepare the Summary Status Report (NAVSHIPS Report 4423-3) (figure 1). This report will be based upon the data contained in the latest Listing and Status of Provisionable Items Report (NAVSHIPS Report 4423-1) (see figure 4). This report will be prepared at the frequency specified in 3.5.1 and it will be distributed to the activities indicated in 3.5.2. A sample format of the Summary Status Report is provided on figure 1.

40.2 Data requirements.- The Summary Status Report will contain the following data:

(a) Block 1 - Report number.- The first report to be numbered 1, and each report thereafter to be numbered consecutively.
(b) Block 2 - Hull number.- Enter hull number(s) to which this report applies.
(c) Block 3 - Summarizing LSPIR submitted on (date).- Enter date of the LSPIR upon which the supervising activity is basing the Summary Status Report.
(d) Block 4 - Date of Summary Status Report. Scheduled no later than five days after the shipbuilder's report.
(e) Block 5 - Total Estimated Provisionable Items.- Enter estimated total from agreed to schedule, (see 3.3) and when changes occur, (see 4.2.)
(f) Block 6 - EDD.- Enter Estimated Delivery Date of the ship.
(g) Block 7 - Shipbuilder's progress (PTD submissions).- Identifies that part of the report which will reflect the shipbuilder's progress in submission of PTD.
(h) Block 8 - Total Identified Provisionable Items Enter the total number of items currently appearing on the shipbuilder's report. This includes those merely identified and anticipated for the hull, and those for which procurement action has been initiated.
(i) Block 9 - Number of Provisionable Items Procured.- Enter the total of those items anticipated for the hull for which procurement action has been initiated, i.e., column 6 has an entry.
(j) Block 10 - PTD Submission to SPCC.- Enter in the "schedule" column the total of the number of PTD scheduled to be submitted to SPCC as indicated in the PTD Submission Schedule nearest to the report date, and enter the total from column 8B the number of PTD actually submitted to SPCC in the LSPIR.
(k) Block 11 Provisioning Documentation from ICP.- Enter the total of the entries in column 8B, in the "schedule" block, and enter the total of the entries in column 9B, in the "actual" column.
(l) Block 12 - Corrective Action by the Supervising Activity (when Provisioning Progress deviates from scheduled progress by more than 05 percent).- Report corrective action taken and results achieved, (see 4.2).
(m) Block 13 - Submitted by.- Supervising activity.

Source: https://assist.dla.mil -- Downloaded: 202640-19T21:19Z
Check the source to verify that this is the current version before use.

SUMMARY STATUS REPORT
PROVISIONING MONITORING SYSTEM

1. Report No.	2. Hull No.	3. Summarizing LSPIR* Submitted on	4. Date of this Report
5. Total Estimated Provisionable Items		6. EDD	

7. Shipbuilder's Progress (PTD Submissions):

	Source	PTDS Schedule	Actual
8. Identified Provisionable Items	Col 5*		XXXX
9. Provisionable Items Procured	Col 6*		
10. PTD Submissions to the ICP	As indicated	XXXX	XXXX
11. Provisioning Data received from ICP	Col 8B/9B	XXXX	XXXX

12. Corrective action by Supervising Activity (when provisioning progress deviates from schedule by more than 05%):

* Listing & Status of Provisionable Items Report

13. Submitted by

Figure 1 - Summary status report provisioning monitoring system

Source: https://assist.dla.mil -- Downloaded: 202610-19T21:19Z
Check the source to verify that this is the current version before use.

SOURCE OF EQUIPMENT OR COMPONENT	REPORT IN PTDSS/LSPIR	PROVISIONING TECHNICAL DOCUMENTATION		
		REQUIRED yes/no	PREPARED BY	REMARKS
Vendor/Mfr	Yes	Yes*	Vendor/Mfr	Invoke MIL-P-15137(SHIPS) in Purch. Order
Shipbuilder Mfr'd	Yes	Yes*	Shipbuilder	Use Pseudo P. O. No.
Shipbuilder Stock	Yes	Yes*	Shipbuilder	Use Pseudo P. O. No.
Naval Ship Research and Development Center, Annapolis Div.	Yes	Yes*	Vendor/Mfr	Shop Equip. (NavShipYds only)
BPA - Blanket Purch. Author	Yes	Yes*	Shipbuilder**	(NavShipYds only)
AVY/DSA Supply System	Yes	Yes*	Shipbuilder**	(NavShipYds only)
Schedule A	No	No	----------	Government Furnished Material (GFM)
NAVSHIPS 4341-2 (Formerly NAVSHIP Form 3855)	No	No	----------	GFM

* Required to the extent of the requirements specified in MIL-P-15137 for "use of previously submitted lists and Allowance Parts Lists (APL)."

** If vendor is unable or unwilling to prepare PTD, the Naval Shipbuilder will prepare PTD for submission to SPCC in accordance with MIL-P-15137.

FIGURE 2 - Provisioning technical documentation requirement guide.

Source: https://assist.dla.mil -- Downloaded: 202640-19T21:19Z
Check the source to verify that this is the current version before use.

Facsimile of PDTSS Format
with example of scheduling
data included.

_____SHIPYARD

PROVISIONING TECHNICAL DOCUMENTATION SUBMISSION SCHEDULE

SHIP: _____ ESTIMATED TOTAL PROVISIONABLE ITEMS: 2200

LSPIR DUE DATE	PTD Submissions to SPCC		MILESTONES
	MONTHLY	ACCUMULATIVE	
15 Jan 1966			Contract signed
15 Apr 1966			Start of Construction
15 Aug 1966		400	First report due
15 Sep 1966	100	500	
15 Oct 1966	100	600	
15 Nov 1966	100	700	
15 Dec 1966	100	800	
15 Jan 1967	100	900	
15 Feb 1967	100	1000	
15 Mar 1967	100	1100	
15 Apr 1967	100	1200	
15 May 1967	100	1300	
15 Jun 1967	100	1400	
15 Jul 1967	100	1500	
15 Aug 1967	100	1600	
15 Sep 1967	100	1700	
15 Oct 1967	75	1775	
15 Nov 1967	50	1825	
15 Dec 1967	50	1875	
15 Jan 1968	50	1925	
15 Feb 1968	50	1975	
15 Mar 1968	50	2025	EDD - 150 DAYS - 95%(2050) (24 Mar 1968)
15 Apr 1968	50	2075	EDD - 120 DAYS - 98%(2090) (5 Apr 1968)
15 May 1968	30	2105	EDD - 0 -100%(2200)
15 Jun 1968	30	2135	(7 Aug 1968)
15 Jul 1968	25	2160	
15 Aug 1968	25	2185	
15 Sep 1968	15	2200	

SCHEDULE TO BE PREDICATED ON:
a. Completing the provisioning process within the time frames allotted by the construction/conversion schedule
b. The PTD submission schedule specified in MIL-P-15137
c. Achievement goals at specified milestones provided by SPCC

Figure 3 - Provisioning technical documentation submission schedule.

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.

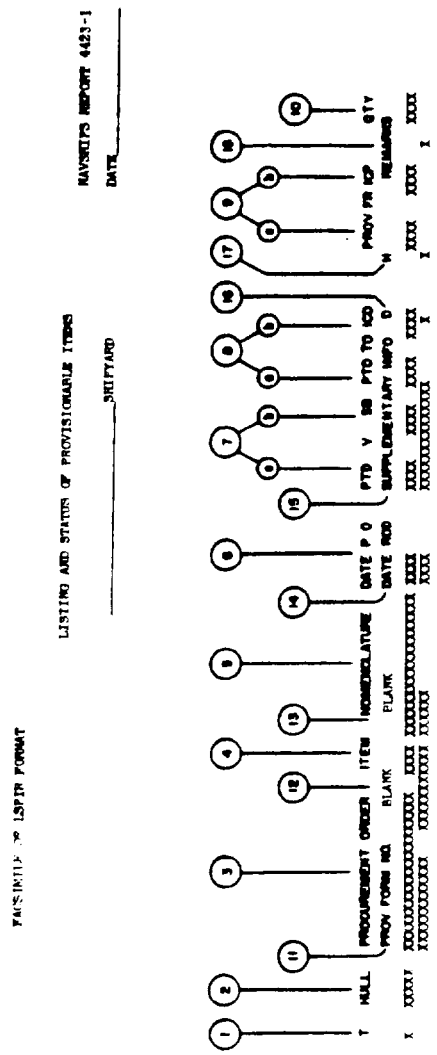


Figure 4 - Listing and status of provisionable items

Source: https://assist.dla.mil -- Downloaded: 202610-19T21:19Z
Check the source to verify that this is the current version before use.

SPECIFICATION ANALYSIS SHEET

Form Approved
Budget Bureau No. 119-R004

INSTRUCTIONS

This sheet is to be filled out by personnel either Government or contractor, involved in the use of the specification in procurement of products for ultimate use by the Department of Defense. This sheet is provided for obtaining information on the use of this specification which will insure that suitable products can be procured with a minimum amount of delay and at the least cost. Comments and the return of this form will be appreciated. Fold on lines on reverse side, staple in corner, and send to preparing activity *(as indicated on reverse hereof)*.

SPECIFICATION

ORGANIZATION *(Of submitter)* | CITY AND STATE

CONTRACT NO. | QUANTITY OF ITEMS PROCURED | DOLLAR AMOUNT
$

MATERIAL PROCURED UNDER A

☐ DIRECT GOVERNMENT CONTRACT ☐ SUBCONTRACT

1. HAS ANY PART OF THE SPECIFICATION CREATED PROBLEMS OR REQUIRED INTERPRETATION IN PROCUREMENT USE?

A. GIVE PARAGRAPH NUMBER AND WORDING.

B. RECOMMENDATIONS FOR CORRECTING THE DEFICIENCIES.

2. COMMENTS ON ANY SPECIFICATION REQUIREMENT CONSIDERED TOO RIGID

3. IS THE SPECIFICATION RESTRICTIVE?

☐ YES ☐ NO IF "YES", IN WHAT WAY?

4. REMARKS *(Attach any pertinent data which may be of use in improving this specification. If there are additional papers, attach to form and place both in an envelope addressed to preparing activity)*

SUBMITTED BY *(Printed or typed name and activity)* | DATE

DD FORM 1426 1 APR 63 REPLACES NAVSHIPS FORM 4863, WHICH IS OBSOLETE

(NAVSHIPS 0VPET 12-66)

Source: https://assist.dla.mil -- Downloaded: 202610-19T21:19Z
Check the source to verify that this is the current version before use.

FOLD

DEPARTMENT OF THE NAVY
NAVAL SHIP ENGINEERING CENTER
WASHINGTON, D. C. 20360

POSTAGE AND FEES PAID
NAVY DEPARTMENT

OFFICIAL BUSINESS

COMMANDER, NAVAL SHIP ENGINEERING CENTER
FEDERAL & MILITARY DOCUMENTS & DOD STANDARDIZATION BRANCH
DEPARTMENT OF THE NAVY
WASHINGTON, D. C. 20360

FOLD

Source: https://assist.dla.mil -- Downloaded: 2026-10-19T21:19Z
Check the source to verify that this is the current version before use.
