DATA ITEM DESCRIPTION

Title: RELIABILITY AND MAINTAINABILITY TEST PLAN

Number: DI-SESS-81585B
AMSC Number: N9585
DTIC Applicable: Yes
Defense Technical Information Center
ATTN: DTIC-
8725 John J. Kingman Road, Suite 0944
Fort Belvoir VA 22060-6218
Preparing Activity: AS
Applicable Forms: N/A

Approval Date: 20151001
Limitation: No
GIDEP Applicable: Yes
GIDEP Operations Center
Naval Warfare Assessment Center
P. O. Box 8000
Corona, CA 91718-8000
Project Number: NDTI-2015-002

Use/relationship:

The Reliability and Maintainability (R&M) Test Plan describes R&M tests and demonstrations at the equipment, subsystem and system levels (including Government developmental and operational tests), their purpose, and schedule. It identifies items to be tested, the test equipment and support requirements, the test conditions to be imposed, the parameters to be measured, and the criteria against which the test results will be measured. This document will be used by the procuring activity for review, approval, and subsequent surveillance and evaluation of the contractor's R&M test and demonstration program.

This Data Item Description (DID) contains the format, intended use information, and content preparation instructions for the data product generated by the specific and discrete task described in the solicitation, and should be tailored appropriately.

Requirements:

1. Format. The R&M Test Plan shall be in contractor's format.

2. Content. The R&M Test Plan shall identify and describe the planned contractor activities for implementation of R&M (Maintainability includes Built-In-Test) testing and demonstration throughout the integrated test program. The R&M Test Plan shall include the following:

   a. A complete listing of all tests and demonstrations to be conducted for the purpose of obtaining data for use in reliability and/or maintainability analysis and evaluation of the contract item or constituent elements thereof. This shall include all tests to be conducted by the Government, Contractor, Subcontractors, and Vendors participating in the program.
   b. A description of the overall test schedule (including time for retest, if required) and resources, including person-months. Include a figure that displays (in contractor format) the integrated planning and timing for Government, prime contractor, and subcontractor and vendor tests. A sample schedule is shown in Figure 1.

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:51Z
Check the source to verify that this is the current version before use.

c. A description of the adequacy (i.e. breadth of testing, timing of testing, stress to system) of R&M test provisions for achieving requirements.
d. Reliability growth planning curve(s) that was integrated with the program's master schedule, plotting reliability against test time (or life units) to meet the quantitative requirement(s) specified in the solicitation or contract. Also, include the rationale for the initial reliability, planned growth rate (growth rate should be tied to realistic management metrics governing the fraction of initial failure rate to be addressed by corrective actions along with the effectiveness of the corrective action), test resources and growth model used. Sample system level reliability growth planning curve is shown in Figure 2.
e. Describe data analysis methods, analytical procedures to be employed, data reduction routines, and reliability growth techniques used to assess demonstrated and projected reliability.
f. Summarize R&M engineering involvement in applicable tests or demonstrations from equipment (i.e. qualification, accelerated life tests, BIT demonstrations), subsystem integration tests through system-level performance tests. Delineate responsibilities with regard to R&M engineering, for test design, test plan review and approval, test performance, data reduction, data analysis, and failure reporting, analysis, and corrective action requirements.
g. Define applicable R&M parameter measurements, operating time data, test conditions, and failure and BIT information that should be collected during existing tests in the overall test plan to achieve maximum practical integration of R&M test requirements.
h. Attach preliminary applicable data collection sheets and R&M scoring and evaluation criteria (i.e., Failure Definition and Scoring Criteria), including the corrective action evaluation methodology that will be used to compute R&M performance based on the data collected during testing.
i. A list of test reports to be issued as a result of planned tests or demonstrations.
j. For each test or demonstration listed, provide a description of:
    i. The test or demonstration objectives and quantitative goals or requirements to be demonstrated, including specific references to the applicable sections of the specification
    ii. The quantity, configuration, and identification of items to be tested, including hardware and software design level and maturity.
    iii. The test or demonstration methods planned
    iv. The test conditions, including the duty cycle, and environmental, operational, and performance profiles
    v. The mode(s) of operation of the items under test, including configuration and mission requirements
    vi. The test duration or sample size.
    vii. The statistical R&M test design criteria, as appropriate, including decision criteria (fail and accept criteria) if applicable.
    viii. The measurements to be recorded and the provisions for recording measurement data required for R&M evaluation
    ix. The test conduct ground rules and system interface boundaries
    x. Adequacy of the item support elements and an estimate of their effect on the item maintainability.
    xi. Description of support equipment, tools and test equipment, technical manuals to be used, spares and consumables and any applicable safety and calibration equipment. Test

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:51Z
Check the source to verify that this is the current version before use.

facility descriptions and requirements, including provisions for voltage, temperature, and vibration

xii. The Government furnished property requirements and impact

xiii. List of test procedures to be used

xiv. Failure Reporting, Analysis and Corrective Action (FRACAS) system to be used

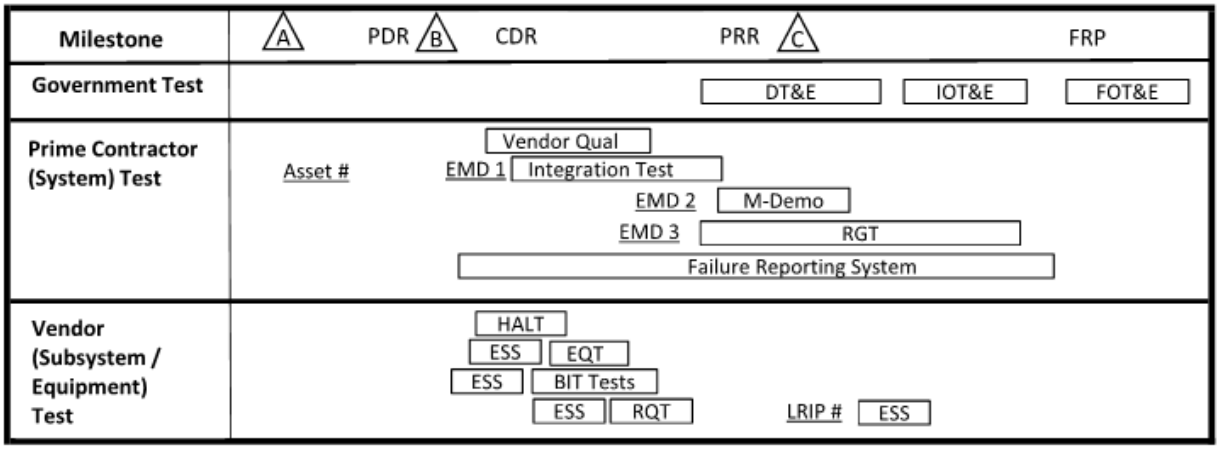


Figure 1. Notional Integrated Test Plan

Notes:

ALT – Accelerated Life Test
BIT – Built-in Test
CDR – Critical Design Review
DT&E – Development Test and Evaluation
EDM – Engineering Development Model
EQT – Environmental Qualification Test
ESS – Environmental Stress Screening
Flt Test – Flight Test
FOT&E – Follow-on Operational Test and Evaluation
FRP – Full Rate Production
HALT – Highly Accelerated Life Test
IOT&E – Initial Operational Test and Evaluation
LRIP – Low Rate Initial Production
M-Demo – Maintainability (and Built-in Test) Demonstration
PDR – Preliminary Design Review
PRAT - Production Reliability Acceptance Test
PRR – Production Readiness Review
RGT – Reliability Growth Test
RQT – Reliability Qualification Test

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:51Z
Check the source to verify that this is the current version before use.

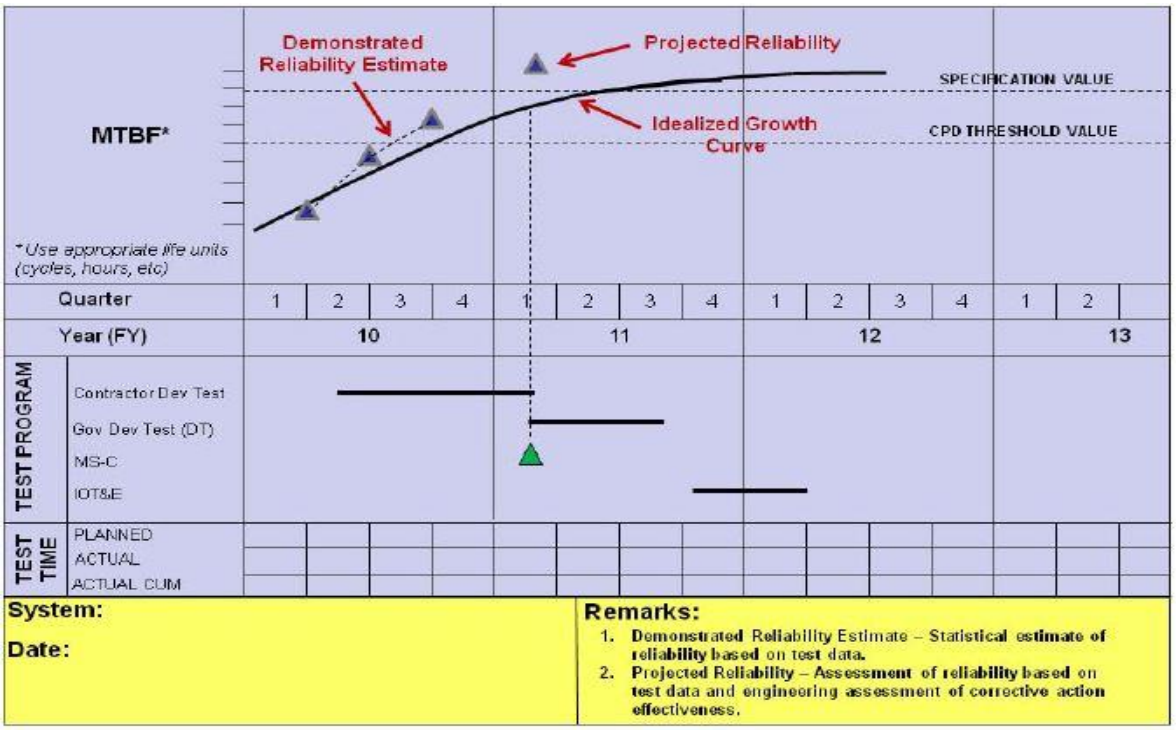


Figure 2. Sample EMD Test Sequence Growth Curve

End of DI-SESS-81585B

Source: https://assist.dla.mil -- Downloaded: 2026-10-26T10:51Z
Check the source to verify that this is the current version before use.
